

## INTRODUCTION

In accordance with the Arkansas Highway Improvement Act of 2016, and specifically Arkansas Code § 27-65-107(a)(19), the Arkansas Highway Commission submits this report on the progress of each public road construction project of ten million dollars (\$10,000,000) or more to the Highway Commission Review and Advisory Subcommittee of the Legislative Council.

For additional information contact:

Gill A. Rogers | Governmental Relations Officer

Arkansas Department of Transportation P.O. Box 2261 | Little Rock, AR 72203 10324 Interstate 30 | Little Rock, AR 72209

Office: (501) 569-2108 Cell: (501) 920-3172

Gill.Rogers@ardot.gov

## **GLOSSARY**

**ACHM** – Asphalt Concrete Hot Mix

Bridge and Approaches - Constructing bridge structures and sections leading up to the bridge

Calendar day contract – Contract where the number of calendar days are bid

**CAP** – Connecting Arkansas Program

CPM -- Critical Path Method—A step-by-step project management technique that identifies critical activities that must be completed before the next stage can proceed.

(F) – Project with Federal Oversight

Grading and Structures - Earthwork and bridge construction; "structures" includes bridges and drainage structures

Interchange – Improvements to the junction between two or more roadways, typically including an overpass or bridge with associated ramps

IRP – Interstate Rehabilitation Program

Major Widening – Widening of an existing roadway to improve capacity or enhance safety, generally by adding a lane or lanes

New Location – Construction of a roadway on a location not previously developed for vehicular transportation

**PCC Pavement** – Portland Cement Concrete Pavement

**Reconstruction** – Generally, removing an existing roadway and building a new road in the same place

Rehabilitation – Modifying or improving an existing roadway; generally less costly and less time consuming than a full reconstruction

Resurfacing – Installation or application of a new driving surface; could be an overlay, sealing job, or similar procedure

**(S)** – Project with State Oversight

Safety and Traffic Engineering – Various improvements to enhance safety and/or improve traffic flow

Working Day Contract – Contract for which time will be assessed for each day on which conditions allow the Contractor to work per Standard Specification for Highway Construction 108.06

# **TABLE OF CONTENTS**

Proj	ects Under Construction	1
	Sorted by Route	3
	Sorted by County	7
Sum	mary Progress Reports by Route	11
Proj	ects Changed From Last Quarter	49
Proj	ects Scheduled	53
	Sorted by Route	55
	Sorted by County	59
Proj	ect Maps	63
	Projects Under Construction	65
	Projects Scheduled	66
Арр	endix	67
	Arkansas Highway Commission	69
	ARDOT Administrative Contacts	69
	ARDOT District Map & Contacts	70
	ΔCT 1	71

**PROJECTS UNDER CONSTRUCTION** As of March 31, 2020

## **PROJECTS UNDER CONSTRUCTION**

SORTED BY ROUTE

## Sorted by Route

#### **Under Construction**

Route	County	Job No	Job Name	Let Date	Cost (\$ in Million)	Page #
I-30	Clark & Hot Spring	012307	De Roche Creek Strs. & Apprs. (S)	06/19/2019	12.7	13
I-30	Saline	CA0601	Hwy. 70 – Sevier St. (Widening) (F)	12/05/2018	187.3	14
I-40	Prairie	BB0610	White River Str. & Apprs. (F)	11/02/2016	100.6	15
I-40 & I-540	Crawford & Sebastian	BB0401	Oklahoma State Line – East (I-40 & I-540) (Sel. Secs.) (S)	10/24/2018	53.2	16
1-49	Benton	BB0903	Hwy. 71B Interchange Impvts. (S)	07/25/2018	26.9	17
I-530	Jefferson	BB0203	Hwy. 65B – Hwy. 65 (F)	07/19/2017	67.2	18
I-555	Craighead	100959	Hwy. 63B – Hwy. 18 (S)	11/06/2019	33.8	19
I-555	Crittenden & Poinsett	012340	I-55 – Hwy. 149 (S)	11/06/2019	11.0	20
Hwy. 5	Saline	061335	Alcoa Rd. – Hwy. 183 (S)	09/12/2018	17.4	21
Hwy. 7	Garland	R60140	Hwy. 70 East – Hwy. 7 North (F)	11/06/2019	75.2	22
Hwy. 7	Newton	009784	Buffalo River & Mill Creek Strs. & Apprs. (S)	01/16/2019	13.6	23
Hwy. 10	Pulaski	061331	Pleasant Ridge Rd. – Pleasant Valley Dr. (L.R.) (F)	03/06/2020*	81.0	24
Hwy. 18	Craighead	100824	BNSF Railroad Overpass (Hwy. 18) (Jonesboro) (S)	10/24/2018	25.2	25
Hwy. 18	Mississippi	CA1002	Manila – East (Widening) (S)	11/02/2016	35.5	26
Hwy. 65	Boone	CA0906	Maxie Camp Rd. – Hwy. 206 (Widening) (S)	08/30/2017	22.9	27
Hwy. 65	Van Buren	CA0801	Hwy. 110 – Clinton (Widening) (S)	01/16/2019	34.0	28
Hwy. 67	Jackson & White	050375	Bald Knob – Newport (S)	12/05/2018	18.7	29
Hwy. 67	White	050374	Lonoke Co. Line – Judsonia (S)	07/24/2019	20.9	30
Hwy. 79	Monroe	110540	White River Strs. Demo. & Removal (Clarendon) (S)	01/17/2018	11.3	31
Hwy. 82	Ashley	020534	Co. Rd. 411 – Hwy. 425 (East of Crossett) (S)	11/02/2016	24.7	32
Hwy. 82	Ashley	CA0202	Hwy. 425 – Hamburg (Widening) (S)	09/12/2018	26.7	33
Hwy. 82	Columbia	CA0705	Co. Rd. 27 – Hwy. 79 (Widening) (S)	01/08/2020	34.2	34

## Sorted by Route

#### **Under Construction**

Route	County	Job No	Job Name	Let Date	Cost (\$ in Million)	Page #
Hwy. 167	Calhoun	070283	Bangs Slough - Hwy. 172 (S)	06/22/2016	17.0	35
Hwy. 167	Calhoun	CA0701	Hwy. 167 Improvements (Hampton) (S)	02/26/2020	12.5	36
Hwy. 167	Calhoun	CA0703	Hwy. 274 – North (Widening) (S)	02/21/2018	29.0	37
Hwy. 167	Calhoun & Union	070282	Ouachita River Str. & Apprs. (S)	11/05/2014	29.4	38
Hwy. 321	Lonoke	061509	Hwy. 367 – Hwy. 89 (Cabot) (S)	07/24/2019	24.2	39
Hwy. 335	Union	070368	Hwy. 82 – Hwy. 7 (Rehab.) (S)	11/02/2016	11.4	40
Hwy. 367	Jackson	005836	White River Str. & Apprs. (Newport) (S)	10/30/2013	31.4	41
Hwy. 412	Greene	100708	Hwy. 412 West - Hwy. 49 (S)	01/18/2017	12.8	42
Hwy. 412	Greene & Lawrence	CA1003	Hwy. 67 – Hwy. 141 (Widening) (S)	01/16/2019	58.5	43
Hwy. 425	Ashley	CA0201	Louisiana State Line – Hwy. 82 (Widening) (S)	09/12/2018	44.6	44
Hwy. 549	Benton	CA0903	Hwy. 71 Interchange (B.V. Bypass) (F)	07/24/2019	66.6	45
Hwy. 549	Benton	090508	Hwy. 71 – Co. Rd. 34 (Add'l Lns.) (B.V. Bypass) (S)	11/15/2017	27.5	46
Hwy. 549	Benton	CA0905	Co. Rd. 34 - Missouri State Line (B.V. Bypass) (F)	07/24/2019	35.5	47

## **PROJECTS UNDER CONSTRUCTION**

SORTED BY COUNTY

## Sorted by County

#### **Under Construction**

County	Route	Job No	Job Name	Let Date	Cost (\$ in Million)	Page #
Ashley	Hwy. 82	020534	Co. Rd. 411 – Hwy. 425 (East of Crossett) (S)	11/02/2016	24.7	32
Ashley	Hwy. 82	CA0202	Hwy. 425 – Hamburg (Widening) (S)	09/12/2018	26.7	33
Ashley	Hwy. 425	CA0201	Louisiana State Line – Hwy. 82 (Widening) (S)	09/12/2018	44.6	44
Benton	I-49	BB0903	Hwy. 71B Interchange Impvts. (S)	07/25/2018	26.9	17
Benton	Hwy. 549	CA0903	Hwy. 71 Interchange (B.V. Bypass) (F)	07/24/2019	66.6	45
Benton	Hwy. 549	090508	Hwy. 71 – Co. Rd. 34 (Add'l Lns.) (B.V. Bypass) (S)	11/15/2017	27.5	46
Benton	Hwy. 549	CA0905	Co. Rd. 34 - Missouri State Line (B.V. Bypass) (F)	07/24/2019	35.5	47
Boone	Hwy. 65	CA0906	Maxie Camp Rd. – Hwy. 206 (Widening) (S)	08/30/2017	22.9	27
Calhoun	Hwy. 167	070283	Bangs Slough - Hwy. 172 (S)	06/22/2016	17.0	35
Calhoun	Hwy. 167	CA0701	Hwy. 167 Improvements (Hampton) (S)	02/26/2020	12.5	36
Calhoun	Hwy. 167	CA0703	Hwy. 274 – North (Widening) (S)	02/21/2018	29.0	37
Calhoun & Union	Hwy. 167	070282	Ouachita River Str. & Apprs. (S)	11/05/2014	29.4	38
Clark & Hot Spring	I-30	012307	De Roche Creek Strs. & Apprs. (S)	06/19/2019	12.7	13
Columbia	Hwy. 82	CA0705	Co. Rd. 27 – Hwy. 79 (Widening) (S)	01/08/2020	34.2	34
Craighead	I-555	100959	Hwy. 63B – Hwy. 18 (S)	11/06/2019	33.8	19
Craighead	Hwy. 18	100824	BNSF Railroad Overpass (Hwy. 18) (Jonesboro) (S)	10/24/2018	25.2	25
Crawford & Sebastian	I-40 & I-540	BB0401	Oklahoma State Line – East (I-40 & I-540) (Sel. Secs.) (S)	10/24/2018	53.2	16
Crittenden & Poinsett	I-555	012340	I-55 – Hwy. 149 (S)	11/06/2019	11.0	20
Garland	Hwy. 7	R60140	Hwy. 70 East – Hwy. 7 North (F)	11/06/2019	75.2	22
Greene	Hwy. 412	100708	Hwy. 412 West - Hwy. 49 (S)	01/18/2017	12.8	42
Greene & Lawrence	Hwy. 412	CA1003	Hwy. 67 – Hwy. 141 (Widening) (S)	01/16/2019	58.5	43
Jackson	Hwy. 367	005836	White River Str. & Apprs. (Newport) (S)	10/30/2013	31.4	41

## Sorted by County

#### **Under Construction**

			The construction			_
County	Route	Job No	Job Name	Let Date	Cost (\$ in Million)	Page #
Jackson & White	Hwy. 67	050375	Bald Knob – Newport (S)	12/05/2018	18.7	29
Jefferson	I-530	BB0203	Hwy. 65B – Hwy. 65 (F)	07/19/2017	67.2	18
Lonoke	Hwy. 321	061509	Hwy. 367 – Hwy. 89 (Cabot) (S)	07/24/2019	24.2	39
Mississippi	Hwy. 18	CA1002	Manila – East (Widening) (S)	11/02/2016	35.5	26
Monroe	Hwy. 79	110540	White River Strs. Demo. & Removal (Clarendon) (S)	01/17/2018	11.3	31
Newton	Hwy. 7	009784	Buffalo River & Mill Creek Strs. & Apprs. (S)	01/16/2019	13.6	23
Prairie	I-40	BB0610	White River Str. & Apprs. (F)	11/02/2016	100.6	15
Pulaski	Hwy. 10	061331	Pleasant Ridge Rd. – Pleasant Valley Dr. (L.R.) (F)	03/06/2020*	81.0	24
Saline	I-30	CA0601	Hwy. 70 – Sevier St. (Widening) (F)	12/05/2018	187.3	14
Saline	Hwy. 5	061335	Alcoa Rd. – Hwy. 183 (S)	09/12/2018	17.4	21
Union	Hwy. 335	070368	Hwy. 82 – Hwy. 7 (Rehab.) (S)	11/02/2016	11.4	40
Van Buren	Hwy. 65	CA0801	Hwy. 110 – Clinton (Widening) (S)	01/16/2019	34.0	28
White	Hwy. 67	050374	Lonoke Co. Line – Judsonia (S)	07/24/2019	20.9	30

## **SUMMARY PROGRESS REPORTS**

SORTED BY ROUTE

## **Summary Progress Report**

Projects Awarded at \$10 Million or More

**Contract ID:** 012307

Contract Name: De Roche Creek Strs. & Apprs. (S)

**Funding Type:** Federal & State

6 & 7 **District:** 

County: **Clark & Hot Spring** 

Route: **I-30** 

Prime Contractor: Manhattan Road & Bridge Co.

Type of Work: **Bridges And Approaches** 

**Contract Bid Amount:** \$12,652,300.00 **Current Contract Amount:** \$12,659,100.00 **Total Amount Paid:** \$2,155,864.42

\$10,503,235.58 Amount Remaining: (Based on Current Contract Amount) Percent Complete: 17.0% (Calculated from the Current Contract Amount) Percent Time Used: 37.1% This is a calendar day contract.

Letting Date: June 19, 2019 Work Order Date: August 09, 2019

Original Estimated Completion Date: Late 2020 **Current Estimated Completion Date:** Late 2020

#### **Description of Project:**

The purpose of this project is to replace two structures on I-30 over De Roche Creek, north of Caddo Valley in Clark & Hot Spring Counties.

## **Summary Progress Report**

Projects Awarded at \$10 Million or More

**Contract ID:** CA0601

Contract Name: Hwy. 70 - Sevier St. (Widening) (F)

**Funding Type:** CAP, IRP, Federal, & State

**District:** 

Saline County: Route: **I-30** 

Prime Contractor: Johnson Bros. Corp., A Southland Company

Type of Work: Major Widening

**Contract Bid Amount:** \$187,339,930.14 **Current Contract Amount:** \$187,899,123.50 **Total Amount Paid:** \$23,056,997.60

\$164,842,125.90 Amount Remaining: (Based on Current Contract Amount) Percent Complete: 12.3% (Calculated from the Current Contract Amount) Percent Time Used: 24.9% This is a calendar day contract.

Letting Date: December 05, 2018 Work Order Date: February 07, 2019

Original Estimated Completion Date: Late 2022 Current Estimated Completion Date: **Early 2023** 

#### Description of Project:

The purpose of this project is to widen 5.9 miles of I-30 from four lanes to six lanes west of Benton in Saline County.

Contract cost has been increased by 0.3%. The increased cost is due to the need for additional traffic control devices, curb and gutter, drop inlets and pipe culverts, also additional quantities of excavation are needed to remove an existing spoil pile and further foundation work is needed due to poor soils beneath a planned retaining wall.

The Contractor has not progressed the project as estimated and therefore based on schedule updates the ECD has moved further on the calendar.

## **Summary Progress Report**

Projects Awarded at \$10 Million or More

**Contract ID: BB0610** 

Contract Name: White River Str. & Apprs. (F)

**Funding Type:** IRP, Federal, & State

**District:** 

County: **Prairie** Route: **I-40** 

Prime Contractor: Parsons-Mahan

Type of Work: **Bridge And Approaches** 

**Contract Bid Amount:** \$100,559,842.64 **Current Contract Amount:** \$100,712,573.38 **Total Amount Paid:** \$82,713,702.19

\$17,998,871.19 Amount Remaining: (Based on Current Contract Amount) Percent Complete: 82.1% (Calculated from the Current Contract Amount) Percent Time Used: 87.8% This is a working day contract.

November 02, 2016 Letting Date: Work Order Date: December 29, 2016

Original Estimated Completion Date: Mid 2020 **Current Estimated Completion Date:** Late 2020

Description of Project:

The purpose of this project is to replace the White River Bridge on I-40 in Prairie County.

## **Summary Progress Report**

Projects Awarded at \$10 Million or More

**Contract ID: BB0401** 

Contract Name: Oklahoma State Line - East (I-40 & I-540) (Sel. Secs.) (S)

**Funding Type:** IRP, Federal, & State

District:

Crawford & Sebastian County:

Route: I-40 & I-540

Prime Contractor: APAC-Central, Inc.

Type of Work: Rehabilitation

**Contract Bid Amount:** \$53,245,516.85 **Current Contract Amount:** \$56,041,598.06 **Total Amount Paid:** \$34,538,741.37

\$21,502,856.69 Amount Remaining: (Based on Current Contract Amount) Percent Complete: 61.6% (Calculated from the Current Contract Amount) Percent Time Used: 69.8% This is a calendar day contract.

Letting Date: October 24, 2018 Work Order Date: December 27, 2018

Original Estimated Completion Date: Mid 2020 Current Estimated Completion Date: Late 2020

#### **Description of Project:**

The purpose of this project is to rehabilitate 42 bridges & resurface 21.1 miles of I-40 & I-540 in Crawford & Sebastian Counties.

Automated Work Zone Information System added to provide real time traffic flow information and warning to the traveling public. Change order adding the system was \$465,000. Two additional bridges (which were not addressed in the plans) were added for hyrdrodemolition and latex modified overlay for \$1.2 million and two bridges were added for polymer overlay for \$20,000. A change order to add additional ACHM Patching for maintenance of traffic was necessary due to extensive failures in an existing shoulder which occurred when stage traffic was moved onto the shoulder. (\$237,000). A change order was edited to add Barrier Wall in order to allow enough work area at bridge locations to complete the Pier Protection work.

## **Summary Progress Report**

Projects Awarded at \$10 Million or More

Contract ID: **BB0903** 

Contract Name: Hwy. 71B Intchng. Impvts. (S) **Funding Type:** IRP, Federal, State, & Local

District:

County: Benton Route: I-49

Prime Contractor: APAC-Central, Inc.

Type of Work: Interchange

Contract Bid Amount: \$26,897,563.15 **Current Contract Amount:** \$27,228,000.90 **Total Amount Paid:** \$15,099,981.67

Amount Remaining: \$12,128,019.23 (Based on Current Contract Amount) Percent Complete: 55.5% (Calculated from the Current Contract Amount) 68.7% Percent Time Used: This is a calendar day contract.

Letting Date: July 25, 2018

Work Order Date: September 13, 2018

Original Estimated Completion Date: Late 2020 Current Estimated Completion Date: Mid 2021

#### Description of Project:

The purpose of this project is to construct a Single Point Urban Interchange (SPUI) at the Hwy 71B Intersection on I-49 in Benton County.

A SPUI, also called a single-point interchange or a single-point diamond interchange, is designed to help move large volumes of traffic through limited amounts of space safely and efficiently. The fabrication and delivery of the steel girders delayed the project by 89 days.

Utilities along the portion of work on Hwy. 71B were to be relocated before that phase of work is to begin. Acquisition of Right-of-way has slowed the relocation of utilities. The contractor is now in that portion of work and is limited as to what work can be progressed along Hwy. 71B. Relocation of utilities is just about complete but has caused an additional delay to the contractor in the schedule of work.

### **Summary Progress Report**

Projects Awarded at \$10 Million or More

**Contract ID: BB0203** 

Contract Name: Hwy. 65B - Hwy. 65 (F) **Funding Type:** IRP, Federal, & State

**District:** 

**Jefferson** County: Route: I-530

Prime Contractor: Webber, LLC Type of Work: Reconstruction

**Contract Bid Amount:** \$67,232,300.00 **Current Contract Amount:** \$73,939,514.81 **Total Amount Paid:** \$68,654,814.48

\$5,284,700.33 Amount Remaining: (Based on Current Contract Amount) Percent Complete: 92.9% (Calculated from the Current Contract Amount) Percent Time Used: 95.8% This is a calendar day contract.

Letting Date: July 19, 2017

Work Order Date: September 12, 2017

Original Estimated Completion Date: Mid 2019 **Current Estimated Completion Date:** Mid 2020

#### **Description of Project:**

The purpose of this project is to reconstruct 10.35 miles of I-530 in Pine Bluff, Jefferson County.

Contract time has been adjusted 230 days; most of which is the result of multiple change orders due to the condition of the existing base course beneath the PCC Pavement and other issues impacting the project's schedule. Contract has also been extended due to adverse weather conditions. Current estimated completion date is Mid 2020. Current Contract Amount has been increased by \$4.6 million; \$2.4 million accounts for addition of PCC Pavement Base to improve existing sub-base, which was retained but required remediation. \$715,000 has been used to increase planned quantities for Soil Stabilization and Stone Backfill to remediate existing soils at isolated roadway and ramp locations and bridge ends.

## **Summary Progress Report**

Projects Awarded at \$10 Million or More

**Contract ID:** 100959

Contract Name: Hwy. 63B - Hwy. 18 (S)

**Funding Type:** Federal & State

10 **District:** 

County: Craighead

Route: I-555

Koss Construction Co. Prime Contractor:

Type of Work: Reconstruction

**Contract Bid Amount:** \$33,837,374.87 **Current Contract Amount:** \$33,765,855.67

**Total Amount Paid:** \$0.00

\$33,837,374.87 Amount Remaining: (Based on Current Contract Amount) Percent Complete: 0.0% (Calculated from the Current Contract Amount) Percent Time Used: 0.0% This is a calendar day contract.

November 06, 2019 Letting Date: Work Order Date: January 21, 2020

Original Estimated Completion Date: Mid 2021 **Current Estimated Completion Date:** Mid 2021

#### **Description of Project:**

The purpose of this project is to reconstruct 4.7 miles of roadway and resurface nine structures on I-555 in Jonesboro, Craighead County.

## **Summary Progress Report**

Projects Awarded at \$10 Million or More

**Contract ID:** 012340

Contract Name: I-55 - Hwy. 149 (S) **Funding Type:** Federal & State

1 & 10 **District:** 

County: Crittenden & Poinsett

Route: I-555

Prime Contractor: Atlas Asphalt, Inc.

Resurfacing Type of Work:

**Contract Bid Amount:** \$11,030,168.55 **Current Contract Amount:** \$11,030,168.55

**Total Amount Paid:** \$0.00

\$11,030,168.55 Amount Remaining: (Based on Current Contract Amount) Percent Complete: 0.0% (Calculated from the Current Contract Amount) Percent Time Used: 0.0% This is a calendar day contract.

November 06, 2019 Letting Date: Work Order Date: January 21, 2020

Original Estimated Completion Date: Late 2020 **Current Estimated Completion Date:** Late 2020

#### **Description of Project:**

The purpose of this project is to resurface 13.0 miles of I-555 from Turrell to Marked Tree in Poinsett & Crittenden Counties.

## **Summary Progress Report**

Projects Awarded at \$10 Million or More

Contract ID: 061335

Contract Name: Alcoa Rd. - Hwy. 183 (S)

**Funding Type:** Federal & State

District:

**Saline** County: Route: Hwy. 5

Prime Contractor: Redstone Const. Group, Inc.

Type of Work: Major Widening

**Contract Bid Amount:** \$17,394,675.98 **Current Contract Amount:** \$17,795,405.02 **Total Amount Paid:** \$8,860,220.74

Amount Remaining: \$8,935,184.28 (Based on Current Contract Amount) Percent Complete: 49.8% (Calculated from the Current Contract Amount) 68.6% Percent Time Used: This is a calendar day contract.

Letting Date: September 12, 2018 Work Order Date: October 26, 2018

Original Estimated Completion Date: Mid 2020 Current Estimated Completion Date: Late 2020

#### **Description of Project:**

The purpose of this project is to widen 2.3 miles of Hwy. 5 from two lanes to five lanes in Saline County.

The project schedule continues to be affected by utility delays and R/W concerns. Utilities continue to preclude work. Efforts at moving continue. Contractor continues to attempt to mitigate delays. The Contractor and Department have worked to locate and develop details to avoid the AT&T fiber duct bank, new details have been provided to the Contractor to avoid AT&T. Additional utility impacts are expected and will be addressed as discovered.

Contract cost has been increased by approximately 2.3% due to subgrade issues, additional removal and disposal items and additional retaining walls needed to address driveways with limited right-of-way.

## **Summary Progress Report**

Projects Awarded at \$10 Million or More

**Contract ID:** R60140

Contract Name: Hwy. 70 East – Hwy. 7 North (F)

**Funding Type:** Federal, State, & Local

**District:** 

County: Garland Route: Hwy. 7

Prime Contractor: McGeorge Contracting Co., Inc.

**New Location** Type of Work:

**Contract Bid Amount:** \$75,151,270.63 **Current Contract Amount:** \$75,151,270.63 **Total Amount Paid:** \$745,101.79

\$74,406,168.84 Amount Remaining: (Based on Current Contract Amount) Percent Complete: 1.0% (Calculated from the Current Contract Amount) Percent Time Used: 1.9% This is a calendar day contract.

November 06, 2019 Letting Date: Work Order Date: December 26, 2019

Original Estimated Completion Date: Late 2022 **Current Estimated Completion Date:** Late 2022

#### **Description of Project:**

The purpose of this project is to extend the Hot Springs Bypass north 5.8 miles to the Hwy. 5 & 7 junction in Garland County.

## **Summary Progress Report**

Projects Awarded at \$10 Million or More

**Contract ID:** 009784

Contract Name: Buffalo River & Mill Creek Strs. & Apprs. (S)

**Funding Type:** Federal, State, & Local

9 District:

County: Newton Route: Hwy. 7

Prime Contractor: Crouse Construction Co. Type of Work: **Bridges And Approaches** 

**Contract Bid Amount:** \$13,554,821.97 **Current Contract Amount:** \$13,580,935.32 **Total Amount Paid:** \$4,873,649.46

\$8,707,285.86 Amount Remaining: (Based on Current Contract Amount) Percent Complete: 35.9% (Calculated from the Current Contract Amount) Percent Time Used: 38.3% This is a working day contract.

Letting Date: January 16, 2019 Work Order Date: January 29, 2019

Original Estimated Completion Date: Late 2020 Current Estimated Completion Date: Late 2020

#### **Description of Project:**

The purpose of this project is to replace the Hwy. 7 structure over the Buffalo River and replace the CR 213 structure over Mill Creek in Newton County.

There is a new bridge to be built on County Road 213 to replace an existing low water bridge that has undersized pipe culverts in place. The realignment of the new Hwy. 7 bridge prevents the use of the county road in its existing configuration. The county road will be realigned with the construction of a new bridge over Mill Creek and then connecting to Hwy. 7. The cost of the county road bridge is being paid by the Department. Construction of the new bridge is on schedule.

## **Summary Progress Report**

Projects Awarded at \$10 Million or More

**Contract ID:** 061331

Contract Name: Pleasant Ridge Rd. - Pleasant Valley Dr. (L.R.) (F)

**Funding Type:** Federal & State

**District:** 

County: **Pulaski** Route: Hwy. 10

Prime Contractor: Kiewit Infrastructure South Co.

Type of Work: Interchange

**Contract Bid Amount:** \$81,049,325.00 **Current Contract Amount:** \$81,049,325.00

**Total Amount Paid:** \$0.00

\$81,049,325.00 Amount Remaining: (Based on Current Contract Amount) Percent Complete: 0% (Calculated from the Current Contract Amount) Percent Time Used: 0% This is a calendar day contract.

Award Date: March 6, 2020

Work Order Date: TBD

Original Estimated Completion Date: Early 2023 **Current Estimated Completion Date: Early 2023** 

#### **Description of Project:**

The purpose of this project is to construct a Single Point Urban Interchange (SPUI) at the Rodney Parham Intersection on Highway10 in Pulaski County.

## **Summary Progress Report**

Projects Awarded at \$10 Million or More

**Contract ID:** 100824

**Contract Name:** BNSF Railroad Overpass (Hwy. 18) (Jonesboro) (S)

**Funding Type:** Federal, State, & Local

10 **District:** 

Craighead County: Route: Hwy. 18

Prime Contractor: Capital Paving And Construction, LLC

Type of Work: **Bridge And Approaches** 

**Contract Bid Amount:** \$25,182,888.88 **Current Contract Amount:** \$25,226,800.54 **Total Amount Paid:** \$8,576,293.39

\$16,650,507.15 Amount Remaining: (Based on Current Contract Amount) Percent Complete: 34.0% (Calculated from the Current Contract Amount) Percent Time Used: 33.8% This is a calendar day contract.

Letting Date: October 24, 2018 Work Order Date: December 27, 2018

Original Estimated Completion Date: Early 2022 **Current Estimated Completion Date: Early 2022** 

#### Description of Project:

The purpose of this project is to construct a railroad overpass on Hwy. 18 in Jonesboro, Craighead County.

Construction of a railroad overpass on Highland Drive (Hwy. 18) and an overpass on Watt Street. This job is a partnering job with the City of Jonesboro that also includes a \$1.2 million 2014 TIGER grant award.

## **Summary Progress Report**

Projects Awarded at \$10 Million or More

**Contract ID:** CA1002

Contract Name: Manila – East (Widening) (S)

**Funding Type:** CAP, Federal, & State

**District:** 

County: **Mississippi** Route: Hwy. 18

W.G. Yates & Sons Const. Co. Prime Contractor:

Type of Work: Major Widening

**Contract Bid Amount:** \$35,471,089.83 **Current Contract Amount:** \$36,321,011.23 **Total Amount Paid:** \$23,395,994.49

\$12,925,016.74 Amount Remaining: (Based on Current Contract Amount) Percent Complete: 64.4% (Calculated from the Current Contract Amount) 117.0% Percent Time Used: This is a calendar day contract.

Letting Date: November 02, 2016 Work Order Date: December 19, 2016

Original Estimated Completion Date: **Early 2019** Current Estimated Completion Date: Late 2020

#### **Description of Project:**

The purpose of this project is to widen 1.8 miles of Hwy. 18 from two lanes to five lanes east of Manila in Mississippi County.

Due to having four active projects in south Arkansas, this Contractor has not been able to effectively keep up with their workload. This project was delayed by utility relocations and weather early on. the contractor is in Liquidated Damages. Last summer work progressed at a faster rate than we have seen on this project in the past. Activities completed include: earthwork, base course, and concrete deck pours. The Current Estimated Completion Date looks to be obtainable if progress continues at the current rate.

Traffic has been switched to the next stage of construction. Demolition of the existing bridges and construction of the second phase of the new bridges has begun.

Over half of the dollar overrun on this project pertains to two change orders totaling approximately \$430,000. One change order to include rock fill to provide a stable foundation in a marsh area in order to then place the planned compacted embankment for main lane construction. The second change order is to increase the planned amount of ACHM leveling in order to meet the planned finished profile grades of the project. There are 27 additional change orders currently approved on the project totaling approximately \$400,000 for various changes/additions of items that were determined to be required to complete the project.

## **Summary Progress Report**

Projects Awarded at \$10 Million or More

**Contract ID:** CA0906

**Contract Name:** Maxie Camp Rd. - Hwy. 206 (Widening) (S)

**Funding Type:** CAP 9 **District:** 

County: **Boone** Route: Hwy. 65

Prime Contractor: Nabholz Construction Corporation

Type of Work: Major Widening

**Contract Bid Amount:** \$22,942,315.85 **Current Contract Amount:** \$23,797,221.41 **Total Amount Paid:** \$18,352,087.70

\$5,445,133.71 Amount Remaining: (Based on Current Contract Amount) Percent Complete: 77.1% (Calculated from the Current Contract Amount) Percent Time Used: 110.1% This is a calendar day contract.

Letting Date: August 30, 2017 Work Order Date: October 11, 2017

Original Estimated Completion Date: Mid 2019 **Current Estimated Completion Date:** Mid 2020

#### **Description of Project:**

The purpose of this project is to widen 4.37 miles of Hwy. 65 from two lanes to five lanes in Boone County.

Additional cost to the project has been mostly due to the increase in ACHM quantities that were required for leveling of asphalt surface at the beginning of the project. The job completion date was moved back due to a utility delay that resulted in the addition of 131 days to the contract.

## **Summary Progress Report**

Projects Awarded at \$10 Million or More

**Contract ID:** CA0801

**Contract Name:** Hwy. 110 - Clinton (Widening) (S)

**Funding Type:** CAP 8 **District:** 

County: Van Buren Route: Hwy. 65

Prime Contractor: Bobby Kennedy Construction Co.

Type of Work: Major Widening

**Contract Bid Amount:** \$33,984,382.53 **Current Contract Amount:** \$34,173,433.13 **Total Amount Paid:** \$8,798,825.62

\$25,374,607.51 Amount Remaining: (Based on Current Contract Amount) Percent Complete: 25.7% (Calculated from the Current Contract Amount) Percent Time Used: 35.1% This is a calendar day contract.

Letting Date: January 16, 2019 Work Order Date: March 07, 2019

Original Estimated Completion Date: Late 2021 **Current Estimated Completion Date:** Late 2021

#### **Description of Project:**

The purpose of this project is to widen from Hwy. 110 to Clinton 7.9 miles of Hwy. 65 from two lanes to five lanes in Van Buren County.

## **Summary Progress Report**

Projects Awarded at \$10 Million or More

**Contract ID:** 050375

Contract Name: Bald Knob - Newport (S)

**Funding Type:** Federal & State

**District:** 

County: Jackson & White

Route: Hwy. 67

Prime Contractor: Emery Sapp & Sons, Inc.

Type of Work: Rehabilitation

**Contract Bid Amount:** \$18,692,509.65 **Current Contract Amount:** \$23,853,190.04 **Total Amount Paid:** \$7,341,126.99

\$16,512,063.05 Amount Remaining: (Based on Current Contract Amount) Percent Complete: 30.8% (Calculated from the Current Contract Amount) Percent Time Used: 29.5% This is a calendar day contract.

Letting Date: December 05, 2018 Work Order Date: January 30, 2019

Original Estimated Completion Date: Late 2021 Current Estimated Completion Date: Late 2021

#### **Description of Project:**

The purpose of this project is to rehabilitate 27.4 miles of Hwy. 67 in Jackson & White Counties.

Contract has been increased by \$4.8 million due to change orders. A number of items necessary to complete the project were added by two change orders with accounted for the \$4.8 million. These change orders address work associated with the removal and replacement of approach slabs and gutters, and joint rehabilitation. Also included items necessary to correct a location with settlement of the existing roadway.

## **Summary Progress Report**

Projects Awarded at \$10 Million or More

**Contract ID:** 050374

Contract Name: Lonoke Co. Line – Judsonia (S)

**Funding Type:** Federal & State

**District:** 

County: White Route: Hwy. 67

Prime Contractor: Emery Sapp & Sons, Inc.

Type of Work: Rehabilitation

**Contract Bid Amount:** \$20,889,159.20 **Current Contract Amount:** \$21,137,272.96 **Total Amount Paid:** \$1,811,061.40

\$19,326,211.56 Amount Remaining: (Based on Current Contract Amount) Percent Complete: 8.6% (Calculated from the Current Contract Amount) Percent Time Used: 11.8% This is a calendar day contract.

Letting Date: July 24, 2019

Work Order Date: September 18, 2019

Original Estimated Completion Date: Early 2022 **Current Estimated Completion Date: Early 2022** 

#### **Description of Project:**

The purpose of this project is to rehabilitate 24.9 miles of Hwy. 67 from the Lonoke County Line to Judsonia in White County.

A change order of approximately \$248,000 was required for additional ACHM patching and to include the item Joint Rehabilitation (Type C) that was not present in the original contract.

# **Summary Progress Report**

Projects Awarded at \$10 Million or More

**Contract ID:** 110540

**Contract Name:** White River Strs. Demo. & Removal (Clarendon) (S)

**Funding Type:** Federal & State

**District:** 

County: Monroe Route: Hwy. 79

Prime Contractor: Century Construction Group, Inc.

Removal Of Structures Type of Work:

**Contract Bid Amount:** \$11,306,869.84 **Current Contract Amount:** \$12,333,701.81 **Total Amount Paid:** \$7,017,629.13

\$5,316,072.68 Amount Remaining: (Based on Current Contract Amount) Percent Complete: 56.9% (Calculated from the Current Contract Amount) Percent Time Used: 18.7% This is a working day contract.

Letting Date: January 17, 2018 Work Order Date: August 08, 2018

Original Estimated Completion Date: Late 2020 **Current Estimated Completion Date:** Mid 2021

#### **Description of Project:**

The purpose of this project is to demolish two bridges and roadway embankment on Highway 79 in Clarendon, Monroe County.

# **Summary Progress Report**

Projects Awarded at \$10 Million or More

**Contract ID:** 020534

Contract Name: Co. Rd. 411 - Hwy. 425 (East of Crossett) (S)

**Funding Type:** Federal & State

2 **District:** 

County: **Ashley** Route: Hwy. 82

Prime Contractor: Johnsville Company, LLC

Type of Work: Major Widening

**Contract Bid Amount:** \$24,690,883.99 **Current Contract Amount:** \$26,132,048.33 **Total Amount Paid:** \$18,145,906.94

\$7,986,141.39 Amount Remaining: (Based on Current Contract Amount) Percent Complete: 69.4% (Calculated from the Current Contract Amount) Percent Time Used: 82.8% This is a working day contract.

November 02, 2016 Letting Date: Work Order Date: December 07, 2016

Original Estimated Completion Date: **Early 2020 Current Estimated Completion Date:** Late 2020

#### **Description of Project:**

The purpose of this project is to widen 5.3 miles of Hwy. 82 from two lanes to five lanes in Ashley County.

Contract has been increased by \$1.44 million due to change orders, with the item soil stabilization accounting for \$1.39 million. Contract quantity for the item was increased to aid drying and compaction efforts of project earthwork due to unstable existing soils.

# **Summary Progress Report**

Projects Awarded at \$10 Million or More

**Contract ID:** CA0202

Contract Name: Hwy. 425 – Hamburg (Widening) (S)

**Funding Type:** CAP 2 District:

County: **Ashley** Route: Hwy. 82

Prime Contractor: JB James Construction, LLC

Type of Work: Major Widening

**Contract Bid Amount:** \$26,704,204.59 **Current Contract Amount:** \$27,678,980.71 **Total Amount Paid:** \$19,708,472.34

\$7,970,508.37 Amount Remaining: (Based on Current Contract Amount) Percent Complete: 71.2% (Calculated from the Current Contract Amount) Percent Time Used: 94.6% This is a calendar day contract.

Letting Date: September 12, 2018 Work Order Date: October 26, 2018

Original Estimated Completion Date: Early 2020 **Current Estimated Completion Date:** Mid 2020

#### **Description of Project:**

The purpose of this project is to widen 5.4 miles of Hwy. 82 from two lanes to five lanes in Ashley County.

Contract has been increased by \$829,108 due to change orders, with the item soil stabilization accounting for \$710,100. Contract quantity for the item was increased to aid drying and compaction efforts of project earthwork due to unstable existing soils.

# **Summary Progress Report**

Projects Awarded at \$10 Million or More

**Contract ID:** CA0705

Contract Name: Co. Rd. 27 - Hwy. 79 (Widening) (S)

**Funding Type: CAP & State** 

7 **District:** 

County: Columbia Route: Hwy. 82

Prime Contractor: JB James Construction, LLC

Type of Work: Major Widening

**Contract Bid Amount:** \$34,222,056.40 **Current Contract Amount:** \$34,222,056.40

**Total Amount Paid:** \$0.00

\$34,222,056.40 Amount Remaining: (Based on Current Contract Amount) Percent Complete: 0.0% (Calculated from the Current Contract Amount) Percent Time Used: 0.0% This is a calendar day contract.

January 08, 2020 Letting Date: Work Order Date: February 26, 2020

Original Estimated Completion Date: Early 2022 **Current Estimated Completion Date: Early 2022** 

#### **Description of Project:**

The purpose of this project is to widen 5.8 miles of Hwy. 82 from two to five lanes in the vicinity of Magnolia in Columbia County.

# **Summary Progress Report**

Projects Awarded at \$10 Million or More

**Contract ID:** 070283

Contract Name: Bangs Slough - Hwy. 172 (S)

**Funding Type:** Federal & State

7 **District:** 

County: Calhoun Route: Hwy. 167

Prime Contractor: W.G. Yates & Sons Const. Co.

Type of Work: Major Widening

**Contract Bid Amount:** \$16,969,845.16 **Current Contract Amount:** \$17,301,481.61 **Total Amount Paid:** \$9,854,518.01

\$7,446,963.60 Amount Remaining: (Based on Current Contract Amount) Percent Complete: 57.0% (Calculated from the Current Contract Amount) Percent Time Used: 117.5% This is a working day contract.

Letting Date: June 22, 2016 Work Order Date: August 11, 2016

Original Estimated Completion Date: Late 2018 **Current Estimated Completion Date:** Late 2020

#### **Description of Project:**

The purpose of this project is to widen 3.9 miles of Hwy. 167 from two lanes to five lanes in Calhoun County.

Due to having four active projects in District 7, this contractor has not been able to effectively keep up with their workload. Estimated completion date remains unchanged.

# **Summary Progress Report**

Projects Awarded at \$10 Million or More

**Contract ID:** CA0701

Contract Name: Hwy. 167 Improvements (Hampton) (S)

**Funding Type: CAP & State** 

7 **District:** 

County: Calhoun Route: Hwy. 167

Prime Contractor: McGeorge Contracting Co., Inc.

Type of Work: Major Widening

**Contract Bid Amount:** \$12,474,345.28 **Current Contract Amount:** \$12,474,345.28

**Total Amount Paid:** \$0.00

\$12,474,345.28 Amount Remaining: (Based on Current Contract Amount) Percent Complete: 0.0% (Calculated from the Current Contract Amount) Percent Time Used: 0.0% This is a calendar day contract.

Letting Date: February 26, 2020 Work Order Date: April 10, 2020

Original Estimated Completion Date: Mid 2023 **Current Estimated Completion Date:** Mid 2023

#### **Description of Project:**

The purpose of this project is to widen 1.8 miles of Hwy. 167 in Hampton to five lanes in Calhoun County.

# **Summary Progress Report**

Projects Awarded at \$10 Million or More

**Contract ID:** CA0703

Contract Name: Hwy. 274 - North (Widening) (S)

**Funding Type: CAP** 7 **District:** 

Calhoun County: Route: Hwy. 167

Prime Contractor: D & J Construction Co., LLC

Type of Work: Major Widening

**Contract Bid Amount:** \$28,964,146.84 **Current Contract Amount:** \$29,710,703.99 **Total Amount Paid:** \$22,468,204.47

\$7,242,499.52 Amount Remaining: (Based on Current Contract Amount) Percent Complete: 75.6% (Calculated from the Current Contract Amount) 89.6% Percent Time Used: This is a calendar day contract.

Letting Date: February 21, 2018 Work Order Date: April 12, 2018

Original Estimated Completion Date: Mid 2020 Current Estimated Completion Date: Mid 2020

#### **Description of Project:**

The purpose of this project is to widen 7.1 miles of Hwy. 167 from two lanes to five lanes in Calhoun County.

The increase in the Contract Amount can largely be attributed to two items:

<sup>1)</sup> Additional ACHM Leveling was needed to meet the required Plan lines and grades.

<sup>2)</sup> In the vicinity of Champagnolle Creek, widening of the roadway has moved the ditch line to where the new backslope cuts into a levee of Champagnolle Creek. A Change Order was processed to line the bank of the creek and the adjacent roadway ditch with Rip Rap material in order to promote stability of the creek channel as well as the new ditch line.

# **Summary Progress Report**

Projects Awarded at \$10 Million or More

Contract ID: 070282

Contract Name: Ouachita River Str. & Apprs. (S)

**Funding Type:** Federal & State

District:

County: Calhoun & Union

Route: Hwy. 167

W.G. Yates & Sons Const. Co. Prime Contractor:

Type of Work: **Bridge And Approaches** 

**Contract Bid Amount:** \$29,442,371.37 **Current Contract Amount:** \$32,855,965.04 **Total Amount Paid:** \$28,799,946.33

\$4,056,018.71 Amount Remaining: (Based on Current Contract Amount) Percent Complete: 87.7% (Calculated from the Current Contract Amount) Percent Time Used: 127.8% This is a working day contract.

November 05, 2014 Letting Date: Work Order Date: December 31, 2014

Original Estimated Completion Date: Late 2017 Current Estimated Completion Date: Late 2020

#### **Description of Project:**

The purpose of this project is to construct a new bridge over the Ouachita River on Hwy. 167 in Calhoun and Union Counties.

Due to having four active projects in District 7, this Contractor has not been able to effectively keep up with their workload. Water levels on the job have been higher than the levels shown historically on the plans. As a result, the time required to construct bridge substructure and foundation elements has increased due to the contractor having to employ additional construction practices (sheet piling in footings, dewatering).

# **Summary Progress Report**

Projects Awarded at \$10 Million or More

**Contract ID:** 061509

Contract Name: Hwy. 367 - Hwy. 89 (Cabot) (S)

**Funding Type:** Federal & State

**District:** 

County: Lonoke Route: Hwy. 321

Prime Contractor: Rogers Group, Inc. Type of Work: Major Widening

**Contract Bid Amount:** \$24,171,571.91 **Current Contract Amount:** \$24,449,840.85 **Total Amount Paid:** \$1,608,070.77

\$22,841,770.08 Amount Remaining: (Based on Current Contract Amount) Percent Complete: 6.6% (Calculated from the Current Contract Amount) Percent Time Used: 17.6% This is a calendar day contract.

Letting Date: July 24, 2019

Work Order Date: September 18, 2019

Original Estimated Completion Date: Mid 2021 **Current Estimated Completion Date:** Late 2021

#### **Description of Project:**

The purpose of this project is to widen 3.2 miles of Hwy. 321 in Cabot from two lanes to five lanes in Lonoke County.

Delay in access to Railroad right of way has affected the schedule of the project by limiting access to bridge replacement in this area.

# **Summary Progress Report**

Projects Awarded at \$10 Million or More

**Contract ID:** 070368

Contract Name: Hwy. 82 - Hwy. 7 (Rehab.) (S)

**Funding Type:** Federal & State

7 District:

County: Union Route: Hwy. 335

W.G. Yates & Sons Const. Co. Prime Contractor:

Type of Work: Rehabilitation

**Contract Bid Amount:** \$11,363,430.15 **Current Contract Amount:** \$12,012,962.45 **Total Amount Paid:** \$1,945,986.85

\$10,066,975.60 Amount Remaining: (Based on Current Contract Amount) Percent Complete: 16.2% (Calculated from the Current Contract Amount) Percent Time Used: 53.8% This is a working day contract.

Letting Date: November 02, 2016 Work Order Date: December 19, 2016

Original Estimated Completion Date: Mid 2018 Current Estimated Completion Date: Late 2020

#### **Description of Project:**

The purpose of this project is to rehabilitate 7.4 miles of Hwy. 335 in Union County.

Due to having four active projects in District 7, this Contractor has not been able to effectively keep up with their workload.

Additional Information: At the start of the project, utility conflicts prevented the job from progressing. These conflicts ended in November 2017, and time charges were initiated. Since November 2017, the Contractor has not pursued the work available to them in a timely manner due to inadequate crews (lack of manpower) and slow internal Contractor coordination. Current work includes earthwork operations and installing drainage structures.

# **Summary Progress Report**

Projects Awarded at \$10 Million or More

**Contract ID:** 005836

Contract Name: White River Str. & Apprs. (Newport) (S)

**Funding Type:** Federal & State

District:

County: Jackson Route: Hwy. 367

Prime Contractor: Tanner Construction Co., Inc.

Type of Work: **Bridge And Approaches** 

**Contract Bid Amount:** \$31,361,489.76 **Current Contract Amount:** \$32,652,432.92 **Total Amount Paid:** \$26,864,985.63

\$5,787,447.29 Amount Remaining: (Based on Current Contract Amount) Percent Complete: 82.3% (Calculated from the Current Contract Amount) 137.4% Percent Time Used: This is a working day contract.

Letting Date: October 30, 2013 Work Order Date: December 17, 2013

Original Estimated Completion Date: Late 2016 Current Estimated Completion Date: **Early 2021** 

#### **Description of Project:**

The purpose of this project is to construct a new Hwy. 367 bridge over the White River in Newport in Jackson County.

Prime Contractor had difficulty constructing Pier 1 and Pier 2 of the substructure portion of the bridge. Weather played a part in some of this, but most has been the inability of the contractor to construct the proper cofferdams necessary for proper construction of the Pier footings. Contractor's efforts have been slower than expected. The substructure is now complete. The current Estimated Completion Date range should be obtainable if the Contractor proceeds at a pace consistent with typical superstructure construction.

# **Summary Progress Report**

Projects Awarded at \$10 Million or More

Contract ID: 100708

Contract Name: Hwy. 412 West - Hwy. 49 (S)

**Funding Type:** Federal & State

10 District:

County: Greene Route: Hwy. 412

Prime Contractor: Dumey Contracting, Inc.

Type of Work: **New Location** 

**Contract Bid Amount:** \$12,768,504.54 **Current Contract Amount:** \$13,893,830.34 **Total Amount Paid:** \$12,425,255.94

\$1,468,574.40 Amount Remaining: (Based on Current Contract Amount) Percent Complete: 89.4% (Calculated from the Current Contract Amount) Percent Time Used: 58.0% This is a working day contract.

Letting Date: January 18, 2017 Work Order Date: March 13, 2017

Original Estimated Completion Date: Late 2018 Current Estimated Completion Date: Late 2020

#### **Description of Project:**

The purpose of this project is to construct the western portion of the Paragould Bypass in Greene County.

The project was slowed early on by utility and right of way issues. Weather has also played a role in slowing the completion of the project. The discrepancy in time charges and percent complete is due to no time being charged during the utility and right of way issues that were no fault of the Contractor for the first year of the project. Weather played a role in slowing the project in Fall 2018 and also in Spring 2019.

Design changes during construction along with poor soil conditions (undercut) lead to change orders in the amount of approximately \$648,000.

# **Summary Progress Report**

Projects Awarded at \$10 Million or More

**Contract ID:** CA1003

**Contract Name:** Hwy. 67 - Hwy. 141 (Widening) (S)

**Funding Type:** CAP 10 **District:** 

County: **Greene & Lawrence** 

Route: Hwy. 412

Prime Contractor: Atlas Asphalt, Inc.-Delta Asphalt Of Ark, Inc., A Jv

Type of Work: Major Widening

**Contract Bid Amount:** \$58,516,744.20 **Current Contract Amount:** \$58,852,830.94 **Total Amount Paid:** \$25,019,276.25

\$33,833,554.69 Amount Remaining: (Based on Current Contract Amount) Percent Complete: 42.5% (Calculated from the Current Contract Amount) Percent Time Used: 23.9% This is a working day contract.

Letting Date: January 16, 2019 Work Order Date: March 28, 2019

Original Estimated Completion Date: Late 2022 **Current Estimated Completion Date:** Mid 2022

#### Description of Project:

The purpose of this project is to widen from Hwy. 67 to Hwy. 141 14.3 miles of Hwy. 412 from two lanes to five lanes in Greene & Lawrence Counties.

# **Summary Progress Report**

Projects Awarded at \$10 Million or More

**Contract ID:** CA0201

Contract Name: Louisiana State Line – Hwy. 82 (Widening) (S)

**Funding Type:** CAP, Federal, & State

2 District:

**Ashley** County: Route: Hwy. 425

Prime Contractor: Diamond B Const. Co., LLC

Type of Work: Major Widening

**Contract Bid Amount:** \$44,594,955.66 **Current Contract Amount:** \$51,520,289.49 **Total Amount Paid:** \$9,821,686.27

\$41,698,603.22 Amount Remaining: (Based on Current Contract Amount) Percent Complete: 19.1% (Calculated from the Current Contract Amount) Percent Time Used: 52.4% This is a calendar day contract.

Letting Date: September 12, 2018 Work Order Date: November 13, 2018

Original Estimated Completion Date: **Early 2021** Current Estimated Completion Date: Mid 2022

#### **Description of Project:**

The purpose of this project is to widen 10.0 miles of Hwy. 425 from two lanes to five lanes in Ashley County and Morehouse Parish, LA.

The project extends into Morehouse Parish in order to construct a transition from a 5-lane roadway in Arkansas to a 4-lane divided highway in Louisiana. Current contract amount has been increased by \$6.8 million due to change orders, with undercut items accounting for \$5.5 million. It was determined that the project required undercut to remove and replace existing unsuitable subgrade.

# **Summary Progress Report**

Projects Awarded at \$10 Million or More

**Contract ID:** CA0903

Contract Name: Hwy. 71 Interchange (B. V. Bypass) (F)

**Funding Type: CAP & State** 

9 **District:** 

County: **Benton** Route: Hwy. 549

Prime Contractor: Emery Sapp & Sons, Inc.

Type of Work: Interchange

**Contract Bid Amount:** \$66,593,069.36 **Current Contract Amount:** \$66,370,480.37 **Total Amount Paid:** \$14,705,111.82

\$51,665,368.55 Amount Remaining: (Based on Current Contract Amount) Percent Complete: 22.2% (Calculated from the Current Contract Amount) Percent Time Used: 19.0% This is a calendar day contract.

Letting Date: July 24, 2019 Work Order Date: August 30, 2019

Original Estimated Completion Date: Late 2021 **Current Estimated Completion Date:** Late 2021

#### **Description of Project:**

The purpose of this project is to construct an interchange at Hwy. 71 & Hwy. 549 for the Bella Vista Bypass (Future I-49) in Benton County.

Changes in planned construction have created a reduction in cost creating a savings to the Department. These changes in concrete islands, barrier wall locations and types of wall, etc. Change orders for underruns have been processed.

# **Summary Progress Report**

Projects Awarded at \$10 Million or More

Contract ID: 090508

Contract Name: Hwy. 71 - Co. Rd. 34 (Add'l Lns.) (B.V. Bypass) (S)

**Funding Type:** Federal & State

9 District:

County: **Benton** Route: Hwy. 549

Prime Contractor: Kolb Grading, LLC

Type of Work: **Additional Lanes** 

**Contract Bid Amount:** \$27,505,530.86 **Current Contract Amount:** \$28,591,295.98 **Total Amount Paid:** \$15,313,049.85

\$13,278,246.13 Amount Remaining: (Based on Current Contract Amount) Percent Complete: 53.6% (Calculated from the Current Contract Amount) Percent Time Used: 62.4% This is a working day contract.

Letting Date: November 15, 2017 Work Order Date: January 02, 2018

Original Estimated Completion Date: Late 2020 Current Estimated Completion Date: Late 2020

#### **Description of Project:**

The purpose of this project is to construct the additional lanes of 8.7 miles of the Bella Vista Bypass on Hwy. 549 in Benton County.

To date there have been 28 change orders that vary in amount with most being small. The two responsible for the majority of the additional costs are:

\$416,599.70 – 38.7% of the overall increase. The cross section sheets did not reflect the appropriate amount of "Rock Fill" volume needed to construct the bridge ends.

\$536,383.08 – 49.8% of the overall increase. This increase was due to a change in the Asphalt Binder Grade necessary to meet the anticipated Urban Freeway design requirements.

# **Summary Progress Report**

Projects Awarded at \$10 Million or More

Contract ID: CA0905

Contract Name: Co. Rd. 34 - Missouri State Line (B. V. Bypass) (F)

Funding Type: **CAP & State** 

9 District:

County: **Benton** Route: Hwy. 549

Prime Contractor: Emery Sapp & Sons, Inc.

**New Location** Type of Work:

Contract Bid Amount: \$35,516,446.50 **Current Contract Amount:** \$35,253,042.40 Total Amount Paid: \$16,432,693.19

\$18,820,349.21 Amount Remaining: (Based on Current Contract Amount) Percent Complete: 46.6% (Calculated from the Current Contract Amount) Percent Time Used: 45.5% This is a calendar day contract.

Letting Date: July 24, 2019

Work Order Date: September 05, 2019

Original Estimated Completion Date: Late 2020 Current Estimated Completion Date: Late 2020

#### Description of Project:

The purpose of this project is to construct the final 2.6 miles of the Bella Vista Bypass (Future I-49) in Benton County.

# **PROJECTS CHANGED** FROM LAST QUARTER

**Projects that were Let to Contract** 

	. rejecte that there are to continue							
Route	County	Job No	Job Name	Let Date	Cost (\$ in Millions)			
Hwy. 10	Pulaski	061331	Pleasant Ridge Rd. – Pleasant Valley Dr. (L.R.) (F)	NA	81.0			
Hwy. 82	Columbia	CA0705	Co. Rd. 27 – Hwy. 79 (Widening) (S)	01/08/2020	34.2			
Hwy. 167	Calhoun	CA0701	Hwy. 167 Improvements (Hampton) (S)	02/26/2020	12.5			

**Projects that became Substantially Complete** 

Route	County	Job No	Job Name	Let Date	Cost(\$ in Million)	Sub Cmplt Date
	Clark, Hempstead &					
I-30	Nevada	BB1101	Hwy. 299 – Gurdon Rest Area (S)	09/12/2018	39.0	01/08/2020
I-630	Pulaski	CA0608	Baptist Hospital – University Ave. (Widening) (F)	04/04/2018	87.4	03/11/2020

Projects where Job No. Changed

Route	County	Job No	Job Name	Year	Cost (\$ in Millions)	Previous Job No
1-49	Washington	040846	Hwy. 62 Intchng. Impvts. (F)	2022	\$20 - \$30 M	BB0410
I-49	Washington	040847	Hwy. 16/112 Spur Intchng. Impvts. (F)	2020	\$15 - \$20 M	BB0411

# **PROJECTS SCHEDULED** As of March 31, 2020

# **PROJECTS SCHEDULED** SORTED BY ROUTE

# Sorted by Route

#### **Projects Scheduled**

Route	County	Job No	Job Name	Year	Cost (\$ in Millions)
I-30 & I-40	Pulaski	CA0602	I-530 – Hwy. 67 (Widening & Reconst.) (I-30 & I-40) (F)	2020	\$500 - \$600 M
I-40, I-55 & Hwy. 77	Crittenden	110651	I-40/I-55/Hwy. 77 Intchng. Impvts. (F)	2022	\$15 - \$20 M
I-40 & Hwy. 59	Crawford	040714	I-40/Hwy. 59 Interchange Impvts. (Van Buren) (S)	2021	\$10 - \$15 M
1-40	Johnson	BB0801	Hwy. 164 – Hwy. 352 (S)	2020	\$10 - \$15 M
I-49	Washington	040846	Hwy. 62 Intchng. Impvts. (F)	2022	\$20 - \$30 M
I-49	Washington	040847	Hwy. 16/112 Spur Intchng. Impvts. (F)	2020	\$15 - \$20 M
I-69	Desha & Drew	020678	Hwy. 278 – Hwy. 65 (S)	2023	\$75 - \$100 M
I-430	Pulaski	061630	Hwy. 10 – Hwy. 100 (System Preservation & ITS Impvts.) (S)	2020	\$10 - \$15 M
Hwy. 1	Lee & St. Francis	110718	S. of Haynes – Hwy. 306 (S)	2021	\$10 - \$15 M
Hwy. 5	Baxter	90517	Izard Co. Line – Mountain Home (Safety Impvts.) (Sel. Secs.) (S)	2020	\$10 - \$15 M
Hwy. 7	Garland	061547	Hwy. 7S – Hwy. 5 (S)	2020	\$15 - \$20 M
Hwy. 7	Ouachita	70501	Louann – Camden (S)	2020	\$10 - \$15 M
Hwy. 10	Pulaski	061382	Taylor Loop Rd. – Pleasant Ridge Rd. (S)	2023	\$15 - \$20 M
Hwy. 10	Pulaski	061454	Gill St. & RR Overpass Strs. & Apprs. (S)	2021	\$15 - \$20 M
Hwy. 20	Phillips	110701	Hwy. 20 Strs. & Apprs. (S)	2021	\$10 - \$15 M
Hwy. 25	Lawrence	100974	Independence Co. Line – Black Rock (Safety Impvts.) (S)	2020	\$10 - \$15 M
Hwy. 45	Sebastian	040713	Hwy. 71 – Hwy. 255 (Ft. Smith) (S)	2021	\$15 - \$20 M
Hwy. 67	Lonoke	061371	Hwy. 67 Intchng. Impvts. (Cabot) (S)	2021	\$30 - \$40 M

Disclaimer: Cost ranges are planning level estimates based on historical data for similar type projects. Amounts shown may change as design progresses.

# Sorted by Route

#### **Projects Scheduled**

				,	0 . (6 . 54)!!!
Route	County	Job No	Job Name	Year	Cost (\$ in Millions)
Hwy. 67	Lonoke	061549	Hwy. 5 – White Co. Line (S)	2022	\$20 - \$30 M
Hwy. 67	Pulaski	CA0604	Main St. – Vandenberg Blvd. (Widening) (S)	2021	\$75 - \$100 M
Hwy. 70	Monroe	110664	Prairie Co. Line – Hwy. 17 (S)	2020	\$20 - \$30 M
Hwys. 70 & 278	Howard, Pike & Sevier	030501	Saline & Caddo Rivers Strs. & Apprs. (S)	2020	\$15 - \$20 M
Hwy. 71	Sevier	030026	Cossatot River – De Queen (S)	2021	\$15 - \$20 M
Hwy. 79	Arkansas & Jefferson	020630	Wabbaseka – Stuttgart (Passing Lanes) (S)	2020	\$10 - \$15 M
Hwy. 79	Jefferson	020615	Pine Bluff – South (S)	2021	\$10 - \$15 M
Hwy. 82	Ashley & Chicot	020675	Montrose – Lake Village (Sel. Secs.) (S)	2020	\$10 - \$15 M
Hwy. 82	Columbia	070458	UPRR Grade Separation (East of Lafayette Co. Line) (S)	2021	\$15 - \$20 M
Hwy. 82	Union	CA0706	Airport Dr. – Hwy. 82B (Widening) (S)	2020	\$20 - \$30 M
Hwy. 82B	Union	070367	Hwy. 82B Improvements (El Dorado) (S)	2022	\$20 - \$30 M
Hwy. 89	Faulkner	080457	UPRR Overpass & Realign. (Mayflower) (S)	2020	\$20 - \$30 M
Hwy. 112	Benton & Washington	012305	Hwy. 412 – Springdale Bypass (S)	2023	\$20 - \$30 M
Hwy. 167	Calhoun	CA0704	Hwy. 79 – South (Widening) (S)	2020	\$20 - \$30 M
Hwys. 255 & 253	Sebastian	040716	Massard Creek – Hwy. 22 (Widening & Reloc.) (Hwy. 255) (S)	2020	\$10 - \$15 M
Hwy. 270	Garland	CA0607	Fleetwood Dr. – Hwy. 227 (Widening) (S)	2020	\$10 - \$15 M
Hwys. 270 & 365S	Jefferson	020626	Hwy. 104 – Hwy. 365 (S)	2020	\$20 - \$30 M
Hwy. 351	Craighead	100942	Hwy. 351 RR Overpass (Airport Rd.) (Jonesboro) (S)	2020	\$10 - \$15 M
New	Clark	070442	Hwy. 67 – Hwy. 51 (Arkadelphia Bypass) (S)	2023	\$20 - \$30 M
New	Craighead	100657	I-555 - Hwy. 49 (Commerce Dr. Extension) (Jonesboro) (Phase 1) (S)	2021	\$30 - \$40 M
Various	Mississippi	100955	Hwys. 77, 140, 158, & 181 Strs. & Apprs. (Mississippi Co.) (S)	2021	\$20 - \$30 M

Disclaimer: Cost ranges are planning level estimates based on historical data for similar type projects. Amounts shown may change as design progresses.

# **PROJECTS SCHEDULED** SORTED BY COUNTY

# Sorted by County

#### **Projects Scheduled**


County	Route	Job No	Job Name	Year	Cost (\$ in Millions)
Arkansas & Jefferson	Hwy. 79	020630	Wabbaseka – Stuttgart (Passing Lanes) (S)	2020	\$10 - \$15 M
Ashley & Chicot	Hwy. 82	020675	Montrose – Lake Village (Sel. Secs.) (S)	2020	\$10 - \$15 M
Baxter	Hwy. 5	90517	Izard Co. Line – Mountain Home (Safety Impvts.) (Sel. Secs.) (S)	2020	\$10 - \$15 M
Benton & Washington	Hwy. 112	012305	Hwy. 412 – Springdale Bypass (S)	2023	\$20 - \$30 M
Calhoun	Hwy. 167	CA0704	Hwy. 79 – South (Widening) (S)	2020	\$20 - \$30 M
Clark	New	070442	Hwy. 67 – Hwy. 51 (Arkadelphia Bypass) (S)	2023	\$20 - \$30 M
Columbia	Hwy. 82	070458	UPRR Grade Separation (East of Lafayette Co. Line) (S)	2021	\$15 - \$20 M
Craighead	Hwy. 351	100942	Hwy. 351 RR Overpass (Airport Rd.) (Jonesboro) (S)	2020	\$10 - \$15 M
Craighead	New	100657	I-555 - Hwy. 49 (Commerce Dr. Extension) (Jonesboro) (Phase 1) (S)	2021	\$30 - \$40 M
Crawford	I-40 & Hwy. 59	040714	I-40/Hwy. 59 Interchange Impvts. (Van Buren) (S)	2021	\$10 - \$15 M
Crittenden	I-40, I-55 & Hwy. 77	110651	I-40/I-55/Hwy. 77 Intchng. Impvts. (F)	2022	\$15 - \$20 M
Desha & Drew	I-69	020678	Hwy. 278 – Hwy. 65 (S)	2023	\$75 - \$100 M
Faulkner	Hwy. 89	080457	UPRR Overpass & Realign. (Mayflower) (S)	2020	\$20 - \$30 M
Garland	Hwy. 7	061547	Hwy. 7S – Hwy. 5 (S)	2020	\$15 - \$20 M
Garland	Hwy. 270	CA0607	Fleetwood Dr. – Hwy. 227 (Widening) (S)	2020	\$10 - \$15 M
Howard, Pike & Sevier	Hwys. 70 & 278	030501	Saline & Caddo Rivers Strs. & Apprs. (S)	2020	\$15 - \$20 M
Jefferson	Hwy. 79	020615	Pine Bluff – South (S)	2021	\$10 - \$15 M
Jefferson	Hwys. 270 & 365S	020626	Hwy. 104 – Hwy. 365 (S)	2020	\$20 - \$30 M
Johnson	I-40	BB0801	Hwy. 164 – Hwy. 352 (S)	2020	\$10 - \$15 M
Lawrence	Hwy. 25	100974	Independence Co. Line – Black Rock (Safety Impvts.) (S)	2020	\$10 - \$15 M


# Sorted by County

#### **Projects Scheduled**

County	Route	Job No	Job Name	Year	Cost (\$ in Millions)
Lee & St. Francis	Hwy. 1	110718	S. of Haynes – Hwy. 306 (S)	2021	\$10 - \$15 M
Lonoke	Hwy. 67	061371	Hwy. 67 Intchng. Impvts. (Cabot) (S)	2021	\$30 - \$40 M
		061549		2022	\$20 - \$30 M
Lonoke	Hwy. 67	061549	Hwy. 5 – White Co. Line (S)	2022	\$20 - \$50 IVI
Monroe	Hwy. 70	110664	Prairie Co. Line – Hwy. 17 (S)	2020	\$20 - \$30 M
Mississippi	Various	100955	Hwys. 77, 140, 158, & 181 Strs. & Apprs. (Mississippi Co.) (S)	2021	\$20 - \$30 M
Ouachita	Hwy. 7	070501	Louann – Camden (S)	2020	\$10 - \$15 M
Phillips	Hwy. 20	110701	Hwy. 20 Strs. & Apprs. (S)	2021	\$10 - \$15 M
Pulaski	I-30 & I-40	CA0602	I-530 – Hwy. 67 (Widening & Reconst.) (I-30 & I-40) (F)	2020	\$500 - \$600M
Pulaski	I-430	061630	Hwy. 10 – Hwy. 100 (System Preservation & ITS Impvts.) (S)	2020	\$10 - \$15 M
Pulaski	Hwy. 10	061382	Taylor Loop Rd. – Pleasant Ridge Rd. (S)	2023	\$15 - \$20 M
Pulaski	Hwy. 10	061454	Gill St. & RR Overpass Strs. & Apprs. (S)	2021	\$15 - \$20 M
Pulaski	Hwy. 67	CA0604	Main St. – Vandenberg Blvd. (Widening) (S)	2021	\$75 - \$100 M
Sebastian	Hwy. 45	040713	Hwy. 71 – Hwy. 255 (Ft. Smith) (S)	2021	\$15 - \$20 M
Sebastian	Hwys. 255 & 253	040716	Massard Creek – Hwy. 22 (Widening & Reloc.) (Hwy. 255) (S)	2020	\$10 - \$15 M
Sevier	Hwy. 71	030026	Cossatot River – De Queen (S)	2021	\$15 - \$20 M
Union	, Hwy. 82	CA0706	Airport Dr. – Hwy. 82B (Widening) (S)	2020	\$20 - \$30 M
Union	Hwy. 82B	070367	Hwy. 82B Improvements (El Dorado) (S)	2022	\$20 - \$30 M
UTIIUTI	nwy. ozb	070307	inwy. 625 inipiovements (El Dorado) (5)	2022	320 - 330 IVI
Washington	I-49	040846	Hwy. 62 Intchng. Impvts. (F)	2022	\$20 - \$30 M
Washington	I-49	040847	Hwy. 16/112 Spur Intchng. Impvts. (F)	2020	\$15 - \$20 M

# **PROJECT MAPS**

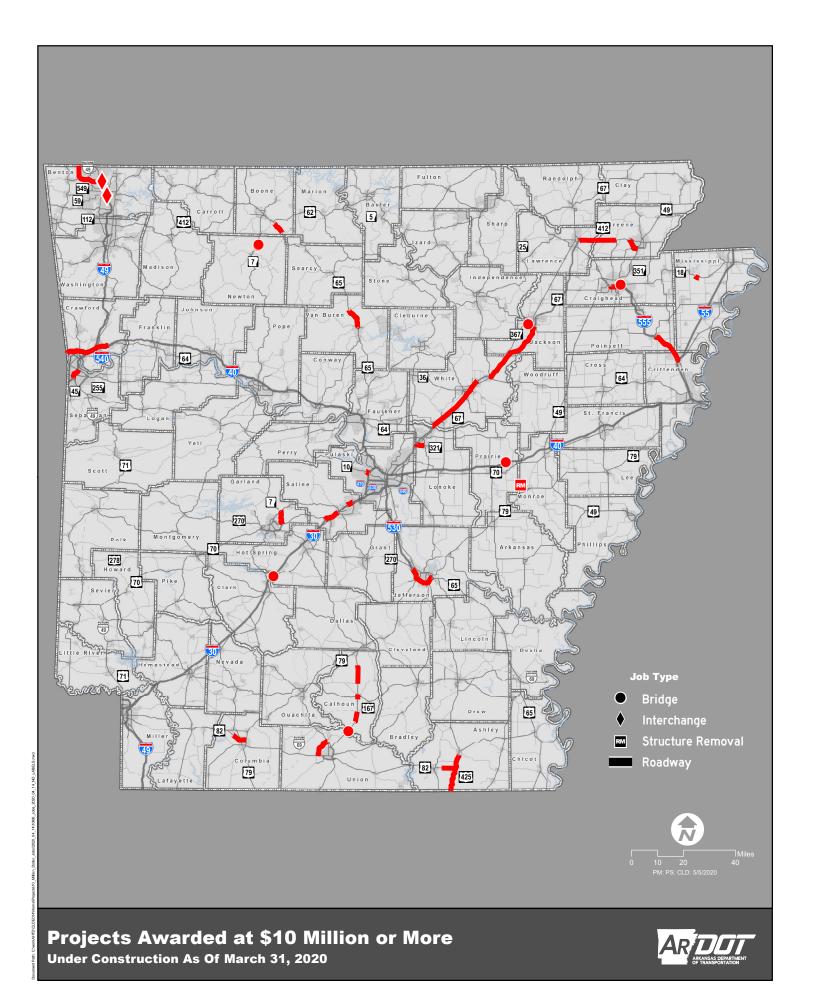

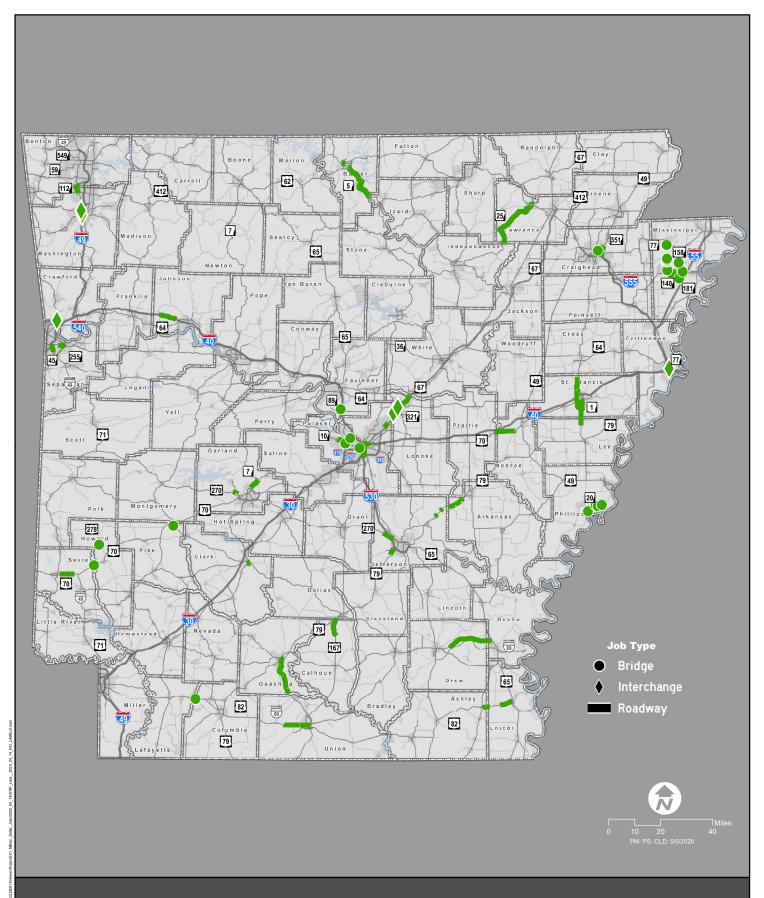

Scheduled STIP Projects Estimated at \$10 Million or More As Of March 31, 2020




## **APPENDIX**

ARKANSAS HIG	HWAY CO	MMISSION
NAME	PHONE	EMAIL
Robert S. Moore, Jr Chairman	(501) 569-2244	RobertSMooreJr@ardot.gov
Dalton A. Farmer, Jr Vice Chairman	(501) 569-2244	Alec.Farmer@ardot.gov
Philip Taldo - Member	(501) 569-2244	Philip.Taldo@ardot.gov
Keith Gibson - Member	(501) 569-2244	Keith.Gibson@ardot.gov
Marie Holder - Member	(501) 569-2244	Marie.Holder@ardot.gov

ARDOT ADMINISTRATIVE CONTACTS			
NAME	TITLE	PHONE	EMAIL
Lorie Tudor	Director	(501) 569-2211	Lorie.Tudor@ardot.gov
Randy Ort	Deputy Director and Chief Operating Officer	(501) 569-2612	Randy.Ort@ardot.gov
Emanuel Banks	Deputy Director and Chief Engineer	(501) 569-2214	Emanuel.Banks@ardot.gov
Kevin Thornton	Assistant Chief Administration	(501) 569-4982	Kevin.Thornton@ardot.gov
Mike Fugett	Assistant Chief Engineer Design	(501) 569-2301	Michael.Fugett@ardot.gov
Rex Vines	Assistant Chief Engineer Operations	(501) 569-2221	Rex.Vines@ardot.gov
Jared Wiley	Assistant Chief Engineer Planning	(501) 569-2241	Jared.Wiley@ardot.gov
Keli Wylie	Alternative Project Delivery Director	(501) 569-2247	Keli.Wylie@ardot.gov
Gill Rogers	Governmental Relations Officer	(501) 569-2108	Gill.Rogers@ardot.gov

## **ARDOT DISTRICT MAP & CONTACTS**

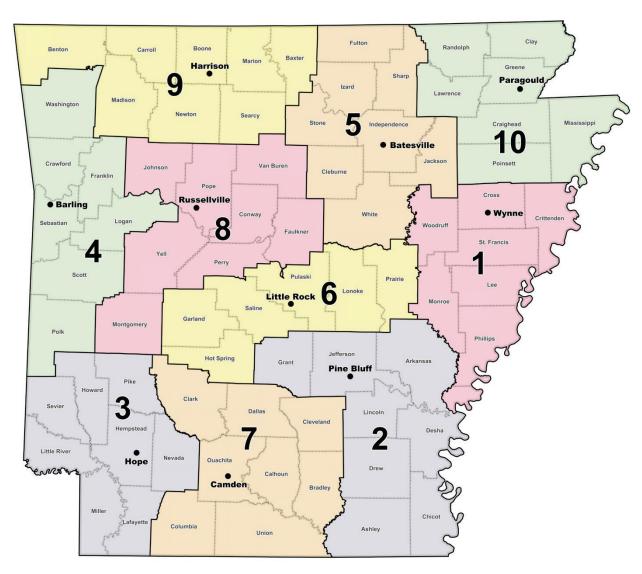

District	District Engineer	City	Email	Phone
District 1	Cannon Callicott	Wynne	Stephen.Callicott@ardot.gov	870-238-8144
District 2	Deric Wyatt	Pine Bluff	Deric.Wyatt@ardot.gov	870-534-1612
District 3	Stephen Frisbee	Норе	Steve.Frisbee@ardot.gov	870-777-3457
District 4	Chad Adams	Fort Smith	Chad.Adams@ardot.gov	479-484-5306
District 5	Bruce Street	Batesville	Bruce.Street@ardot.gov	870-251-2374
District 6	Mark Headley	Little Rock	Mark.Headley@ardot.gov	501-569-2266
District 7	David Archer	Camden	David.Archer@ardot.gov	870-836-6401
District 8	Jason Hughey	Russellville	Jason.Hughey@ardot.gov	479-968-2286
District 9	Steve Lawrence	Harrison	Steve.Lawrence@ardot.gov	870-743-2100
District 10	Brad Smithee	Paragould	Mark.Smithee@ardot.gov	870-239-9511

## ACT 1

## Stricken language would be deleted from and underlined language would be added to present law. Act 1 of the Third Extraordinary Session

1	State of Arkansas  90th General Assembly  Call Item  A Bill	n 2
2	•	
3	Third Extraordinary Session, 2016 HOUSE BILL 10	)09
4 5	By: Representatives Davis, Eaves, Brown, Della Rosa, J. Mayberry, Ballinger, Bell, Cozart, Dotson,	
6	Eads, Eubanks, Henderson, House, Lemons, Speaks, Sullivan	
7	By: Senator Hester	
8	By. Senator Frester	
9	For An Act To Be Entitled	
10	AN ACT TO CREATE THE ARKANSAS HIGHWAY IMPROVEMENT	
11	PLAN OF 2016; TO DECLARE AN EMERGENCY; AND FOR OTHER	
12	PURPOSES.	
13		
14		
15	Subtitle	
16	TO CREATE THE ARKANSAS HIGHWAY	
17	IMPROVEMENT PLAN OF 2016; AND TO DECLARE	
18	AN EMERGENCY.	
19		
20		
21	BE IT ENACTED BY THE GENERAL ASSEMBLY OF THE STATE OF ARKANSAS:	
22		
23	SECTION 1. DO NOT CODIFY. This act shall be known and may be cited a	as
24	the "Arkansas Highway Improvement Plan of 2016".	
25		
26	SECTION 2. Arkansas Code § 10-3-309(b)(2)(B), concerning the	
27	definition of "state agency", is amended to read as follows:	
28	(B) "State agency" does not include the following unless	
29	the Legislative Council adopts rules under subsection (h) of this section	
30	including that include one (1) or more of the following in the definition of	f
31	"state agency":	
32	(i) The Arkansas State Game and Fish Commission, i	£
33	the rule is not promulgated under authority of a statute enacted by the	
34	General Assembly;	
35	(ii) The Except as provided in §§ 10-3-3102 and 27-	=
36	65-107(a)(18)(A), the State Highway Commission and the Arkansas State Highway	ay

Ţ	and Transportation Department, if the rule is not promulgated under authority
2	of a statute enacted by the General Assembly; and
3	(iii) An institution of higher education.
4	
5	SECTION 3. Arkansas Code Title 10, Chapter 3, is amended to add an
6	additional subchapter to read as follows:
7	Subchapter 31 - Highway Commission Review and Advisory Subcommittee of
8	the Legislative Council
9	10-3-3101. Creation.
10	(a) The Highway Commission Review and Advisory Subcommittee of the
11	Legislative Council is created.
12	(b)(1) The Highway Commission Review and Advisory Subcommittee of the
13	Legislative Council shall consist of twenty (20) members with at least four
14	(4) or more members of the General Assembly from each congressional district
15	of the state.
16	(2) The Legislative Council may through a suspension of its
17	rules, alter the membership of the Highway Commission Review and Advisory
18	Subcommittee of the Legislative Council.
19	
20	10-3-3102. Duties.
21	(a) The Highway Commission Review and Advisory Subcommittee of the
22	Legislative Council shall review:
23	(1)(A) Proposed rules of the State Highway Commission required
24	under § 27-65-107(a)(18)(A).
25	(B)(i) Subdivision (a)(1)(A) of this section is limited to
26	rule review only.
27	(ii) Rules promulgated by the State Highway
28	Commission are not subject to approval by the Highway Commission Review and
29	Advisory Subcommittee of the Legislative Council, the Legislative Council, or
30	the Administrative Rules and Regulations Subcommittee of the Legislative
31	Council under this section or § 10-3-309; and
32	(2) Other State Highway Commission matters the Highway
33	Commission Review and Advisory Subcommittee of the Legislative Council
34	considers necessary to perform its duties under this section.
35	(b) The Highway Commission Review and Advisory Subcommittee of the
36	Legislative Council shall perform such other duties as may be assigned to it

1	by the Legislative Council.
2	
3	(c) As a subcommittee of the Legislative Council, actions of the
4	Highway Commission Review and Advisory Subcommittee shall be reported to the
5	Legislative Council for final consideration and adoption.
6	
7	SECTION 4. Arkansas Code § 19-3-521(a)(2)(B), concerning the
8	Securities Reserve Fund, is amended to read as follows:
9	(B) However, moneys in the Securities Reserve Fund in
10	excess of one hundred thousand dollars (\$100,000) shall be available at all
11	times to the Chief Fiscal Officer of the State <del>for transfer to the Budget</del>
12	Stabilization Trust Fund as authorized by § 19-5-905, there to be used as
13	provided by law.
14	
15	SECTION 5. Arkansas Code Title 19, Chapter 5, Subchapter 2 is amended
16	to add a new section to read as follows:
17	19-5-207. Certain sales and use taxes not subject to deduction,
18	transfer, or distribution.
19	The sales and use taxes levied under Arkansas Constitution, Amendment
20	91, § 3, are not subject to deduction, transfer, or distribution to the
21	Constitutional Officers Fund or the State Central Services Fund under §§ 19-
22	5-202, 19-5-203, and 19-5-205.
23	
24	SECTION 6. Arkansas Code § 19-5-406 is amended to read as follows:
25	19-5-406. Transfer of remaining revenue.
26	After making the maximum annual allocation, as provided $\underline{\text{for}}$ in § 19-5-
27	402: , all remaining general revenues available for distribution during each
28	fiscal year shall be transferred on the last day of business in each calendar
29	month to the General Revenue Allotment Reserve Fund, there to be used for the
30	respective purposes as provided by law.
31	(1) Seventy-five percent (75%) of the remaining general revenues
32	available for distribution during each fiscal year shall be transferred on
33	the last day of business in each calendar month to the General Revenue
34	Allotment Reserve Fund, there to be used for the respective purposes as
35	provided by law; and
36	(2) Twenty-five percent (25%) of the remaining general revenues

- available for distribution during each fiscal year shall be transferred on 1 2 the last day of business in each calendar month to the Arkansas Highway 3 Transfer Fund. 4 5 SECTION 7. Arkansas Code § 19-5-501(a)(2), concerning the Budget Stabilization Trust Fund, is amended to read as follows: 6 7 The Budget Stabilization Trust Fund shall consist of funds 8 made available and transferred to it from the Securities Reserve Fund as set 9 out in § 19-5-905 and this section, the fund balance and other assets 10 remaining in the State Budget Revolving Fund on June 30, 1987, and any other 11 funds made available by law. The Treasurer of State, after complying with § 27-70-204 for distributing interest income earned from investment of average 12 daily balances of the State Highway and Transportation Department Fund; § 15-13 14 41-110 for distributing interest earned from investment of average daily balances of the Game Protection Fund; and any other laws enacted by the 15 16 General Assembly for disposition of interest income earned from investment of 17 average daily State Treasury balances, shall credit to the Budget 18 Stabilization Trust Fund fifty percent (50%) of the interest income received 19 and credited to the Securities Reserve Fund and credit to the General 20 Improvement Fund fifty percent (50%) of the interest income received and 21 eredited to the Securities Reserve Fund as certified by the Chief Fiscal 22 Officer of the State. 23 24 SECTION 8. Arkansas Code § 19-5-905 is amended to read as follows: 25 19-5-905. Securities Reserve Fund. (a) There is established on the books of the Treasurer of State, the 26 Auditor of State, and the Chief Fiscal Officer of the State a trust fund to 27 be known as the "Securities Reserve Fund". This fund The Securities Reserve 28 29 Fund shall consist of moneys derived from savings effected in the retirement in advance of maturity of nonhighway direct general obligation bonds of the 30
- and interest derived from the sale of securities held in the Securities

  Account by the Treasurer of State as custodian. It shall be used for The

state, of discounts received in the purchase of securities, and of premiums

34 Securities Reserve Fund shall be used as follows:

31

35 (1) Paying To pay premiums and the purchase and absorbing of discounts in the sale of securities held in the Securities Account, not to

1 exceed five hundred thousand dollars (\$500,000) in any one (1) fiscal year; 2 (2) Guaranteeing To guarantee bonds in an aggregate principal amount not to exceed five million dollars (\$5,000,000) outstanding at any 3 4 time, with no bond bearing interest at a rate exceeding eight percent (8%) per annum, of the Museum and Cultural Commission Fund authorized, and in the 5 6 manner prescribed in the Arkansas Museum and Cultural Center Act, by § 13-5-301 et seq., not to exceed five hundred thousand dollars (\$500,000) in any 7 8 one (1) fiscal year; 9 (3) Guaranteeing To guarantee bonds of any other park or 10 recreation facility approved by the Governor and the Department of Parks and Tourism, not to exceed five hundred thousand dollars (\$500,000) in the 11 12 aggregate, after seeking advice of the Legislative Council and the Legislative Joint Auditing Committee; 13 14 Guaranteeing To guarantee industrial development bonds as (4) 15 authorized by \$\$ 15-4-702 - 15-4-710;(5) Absorbing To absorb losses incurred in the investing of 16 17 securities held in the Securities Account in the State Treasury and in bank 18 depositories. The balance of this fund the Securities Reserve Fund shall 19 always be available for this purpose; and 20 Guaranteeing To guarantee to students to attend truck 21 driving school at the Arkansas Commercial Driver Training Institute at Arkansas State University-Newport, in an aggregate principal amount not to 22 23 exceed four hundred thousand dollars (\$400,000) outstanding at any one (1) 24 time.; 25 (7) To distribute: 26 (A) Interest income earned on investment of average daily 27 balances of the following: 28 (i) The State Highway and Transportation Department Fund, as authorized by § 27-70-204; 29 30 (ii) The Game Protection Fund, as authorized by § 31 15-41-110; 32 (iii) The funds deposited into the State Treasury by state agencies, boards, and commissions that were previously held as cash 33 34 funds in a bank depository or investment depository, as authorized by § 19-3-35 518(d); and 36 (iv) State and Local Fiscal Assistance Act of 1972,

1	31 0.5.C. § 6701 et seq., as authorized by § 19-3-321(c);
2	(B) Interest income earned from investment of average
3	daily State Treasury balances by any other laws enacted by the General
4	Assembly;
5	(8) After the distributions enumerated in subdivision (a)(7) of
6	this section, for a one-time transfer by the Chief Fiscal Officer of the
7	State, one million five hundred thousand dollars (\$1,500,000) to the Arkansas
8	Highway Transfer Fund, to be transferred only in Fiscal Year 2017;
9	(9) After the distributions enumerated in subdivisions (a)(7)
10	and (8) of this section, for a transfer by the Chief Fiscal Officer of the
11	State of five million dollars (\$5,000,000) each fiscal year to the Budget
12	Stabilization Trust Fund;
13	(10) After the transfer to the Budget Stabilization Trust Fund
14	enumerated in subdivision (a)(9) of this section, for a transfer by the Chief
15	Fiscal Officer of the State of twenty million dollars (\$20,000,000) beginning
16	in Fiscal Year 2018 and each fiscal year thereafter to the Arkansas Highway
17	Transfer Fund;
18	(11) For a transfer by the Chief Fiscal Officer on the last
19	business day of the fiscal year to the Budget Stabilization Trust Fund to
20	reimburse the Budget Stabilization Trust Fund for any current fiscal year
21	transfers that have been made to the following:
22	(A) The Department of Correction Farm Fund under § 19-5-
23	501(b)(1);
24	(B) The State Military Department Fund under § 19-5-
25	501(b)(3);
26	(C) The Disaster Assistance Fund under § 19-5-1006;
27	(D) The Miscellaneous Revolving Fund under § 19-5-1009;
28	(E) The State Central Services Fund under § 19-5-501(d);
29	<u>and</u>
30	(F) The State Board of Election Commissioners, as
31	authorized by law; and
32	(12) After all distributions and transfers under this section,
33	less one hundred thousand dollars (\$100,000) under § 19-3-521(a)(2), for a
34	transfer by the Chief Fiscal Officer of the State on the last business day of
35	the fiscal year of the fund balance to the Long Term Reserve Fund.
36	(b) Moneys in this fund in excess of one hundred thousand dollars

```
($100,000) shall, at all times, be available to the Chief Fiscal Officer of
 1
 2
     the State for transfer to the Budget Stabilization Trust Fund, there to be
 3
     used as provided by law.
 4
           (e)(b) In the event any loss If any loss is shall be sustained in
 5
     relation to securities at any time held in the Securities Account or in any
 6
     bank depository and in the event if the credit balance in the Securities
     Reserve Fund shall be is insufficient to absorb such the loss, the Chief
 7
 8
     Fiscal Officer of the State shall cause a transfer of moneys to be made from
 9
     the Budget Stabilization Trust Fund to the Securities Reserve Fund in such
10
     amount as shall, when added to the credit balance in the Securities Reserve
11
     Fund, equal the amount of such the loss. It is the intent of the General
12
     Assembly that no loss shall be sustained by any account the funds of which
     were used in making such investments and deposits.
13
14
15
           SECTION 9. Arkansas Code § 19-5-1103(b), concerning the Property Tax
16
     Relief Trust Fund, is amended to read as follows:
           (b) The fund shall consist of such revenues as generated by §§ 26-52-
17
     302(c), 26-52-317(c)(1)(B), 26-52-319(a)(2)(B), 26-53-107(c), 26-53-107(c)
18
19
     145(c)(1)(B), 26-53-148(a)(2)(B), \frac{26-56-201(g)(1)(C)}{2}, and 26-56-224(c)(2) and
20
     shall be used for such purposes as set out in § 26-26-310.
21
22
           SECTION 10. Arkansas Code § 19-5-1227(b)(3), concerning the
23
     Educational Adequacy Fund, is amended to read as follows:
24
                 (3) The revenues generated by \$\$ 26-52-302(d), 26-52-316, 26-52-316
25
     317(c)(1)(C), 26-52-319(a)(2)(C), 26-53-107(d), 26-53-145(c)(1)(C), 26-53-145(c)(1)(C)
     148(a)(2)(C), \frac{26-56-201(g)(1)(B)}{2}, 26-56-224(c)(3), and 26-57-
26
27
     1002(d)(1)(A)(ii); and
28
29
           SECTION 11. Arkansas Code § 19-6-201(68), concerning the enumeration
30
     of general revenues, is repealed.
31
                 (68) The first four million dollars ($4,000,000) of the eight and
32
     one-half cent (8½) tax on distillate special fuels levied each fiscal year
33
     under $26-56-201(a)(1)(A)(i);
34
35
           SECTION 12. Arkansas Code § 19-6-301(3)(A), concerning the enumeration
```

05-19-2016 08:23:07 LGS030

7

of special revenues, is amended to read as follows:

36

1	(A) Eight and one-half cent (8.5¢) tax on distillate
2	special motor fuels levied by § 26-56-201(a)(1)(A)(i), after the deduction of
3	the first four million dollars (\$4,000,000) each fiscal year under § 26-56-
4	$\frac{201(g)(1)}{g}$ and $\frac{1}{g}$ one cent (1¢) tax on distillate special motor fuels levied
5	by § 26-56-201(a)(1)(A)(ii);
6	
7	SECTION 13. Arkansas Code Title 19, Chapter 6, Subchapter 8, is
8	amended to add an additional section to read as follows:
9	19-6-832. Arkansas Highway Transfer Fund.
10	(a) There is created on the books of the Treasurer of the State, the
11	Auditor of State, and the Chief Fiscal Officer of the State a special revenue
12	fund to be known as the "Arkansas Highway Transfer Fund".
13	(b) The Arkansas Highway Transfer Fund shall be used to provide
14	additional funding to the Arkansas State Highway and Transportation
15	Department for use in constructing and maintaining the highways of this
16	state.
17	(c) In the event revenues to the department are insufficient to fully
18	address the highway construction and maintenance needs of the state, the
19	department may provide a written document to the Governor outlining the
20	reasons that additional funding is needed and requesting that the Governor
21	provide a recommendation to the Legislative Council or the Joint Budget
22	Committee for review and approval of the transfer of funds in the Arkansas
23	Highway Transfer Fund to the State Highway and Transportation Department
24	<u>Fund.</u>
25	(d) Upon review and approval of the Legislative Council or the Joint
26	Budget Committee, the Chief Fiscal Officer of the State may transfer funds
27	from the Arkansas Highway Transfer Fund to the State Highway and
28	Transportation Department Fund as deemed necessary to provide additional
29	funding to address the highway construction and maintenance needs of the
30	state.
31	(e) The requirement of approval by the Legislative Council or Joint
32	Budget Committee is not a severable part of this section. If the requirement
33	of approval by the Legislative Council or Joint Budget Committee is ruled
34	unconstitutional by a court of competent jurisdiction, this entire section is
35	void.
36	

SECTION 14. The introductory language of Arkansas Code § 19-6-484, concerning the Conservation Tax Fund, is amended to read as follows:

The Conservation Tax Fund shall consist of those general revenues as specified in § 26-56-201(g)(1)(D) and those special revenues as specified in § 19-6-301(193) there to be distributed to the fund accounts as set out below, which are created by this section unless specifically created in other provisions of the Arkansas Code, and under the following procedures:

7 8 9

10

11 12

13

19

20

21

22

23

24

25

2627

28

29

30

31

32

33

34

35

36

1

2

3

4

5

6

SECTION 15. Arkansas Code § 19-6-486 is amended to read as follows: 19-6-486. Arkansas Rainy Day Fund. Long Term Reserve Fund.

- (a) There is created on the books of the Treasurer of State, the Auditor of State, and the Chief Fiscal Officer of the State a special revenue fund to be known as the "Arkansas Rainy Day Fund" "Long Term Reserve Fund".
- 14 (b) The fund shall consist of such funds as may be provided by the 15 General Assembly.
- 16 (c) The fund shall be used to distribute moneys to one (1) or more 17 funds or fund accounts in the Revenue Stabilization Law of Arkansas, § 19-5-18 101 et seq.
  - (d)(1) After determining the estimated amount of general revenue that will be available for allocation to the state agencies under the Revenue Stabilization Law, § 19-5-101 et seq., and after making the determination required by § 19-5-1227(c) and prior to making any transfers deemed necessary by the Chief Fiscal Officer of the State in § 19-5-1227(d), the Chief Fiscal Officer of the State may transfer funds from the Arkansas Rainy Day Fund Long Term Reserve Fund in the event a "revenue shortfall" exists to meet the state's financial obligation to provide an adequate educational system for the state and to provide for the effective operation of state government. In the event the Chief Fiscal Officer of the State determines that a "revenue shortfall" exists as defined as a circumstance when the official forecast of gross general revenue certified by the Chief Fiscal Officer of the State is projected to increase less than three percent (3%) over and above the gross general revenue collections of the previous fiscal year due to changes in economic conditions, he or she may then transfer funds from the Arkansas Rainy Day Fund Long Term Reserve Fund, as approved by the Legislative Council or Joint Budget Committee, to various funds and fund accounts, as deemed necessary, in the Revenue Stabilization Law for the purpose of meeting

- 1 unanticipated shortfalls in state general revenue.
- 2 (2) Or the Chief Fiscal Officer of the State may transfer funds
- 3 from the Arkansas Rainy Day Fund Long Term Reserve Fund to the Economic
- 4 Development Superprojects Project Fund for projects authorized under Arkansas
- 5 Constitution, Amendment 82, as approved by the Governor and the Legislative
- 6 Council or Joint Budget Committee.
- 7 (3) Determining the maximum amount of appropriation and general
- 8 revenue funding for a state agency each fiscal year is the prerogative of the
- 9 General Assembly. This is usually accomplished by delineating such maximums
- 10 in the appropriation acts for a state agency and the general revenue
- 11 allocations authorized for each fund and fund account by amendment to the
- 12 Revenue Stabilization Law. Further, the General Assembly has determined that
- 13 creating the Arkansas Rainy Day Fund Long Term Reserve Fund and establishing
- 14 the procedures for the transfer of funds to various fund and fund accounts in
- 15 the Revenue Stabilization Law or to the Economic Development Superprojects
- 16 Project Fund, or both, provides for the efficient and effective operation of
- 17 state government if a revenue shortfall is determined to exist. Therefore, it
- 18 is both necessary and appropriate that the General Assembly maintain
- 19 oversight by requiring prior approval of the Legislative Council or Joint
- 20 Budget Committee as provided by this section. The requirement of approval by
- 21 the Legislative Council or Joint Budget Committee is not a severable part of
- 22 this section. If the requirement of approval by the Legislative Council or
- 23 Joint Budget Committee is ruled unconstitutional by a court of competent
- 24 jurisdiction, this entire section is void.
- 25 (e)(1) Upon recommendation by the Chief Fiscal Officer of the State,
- 26 the Governor may determine that circumstances exist that meet the
- 27 requirements for the utilization of the Arkansas Rainy Day Fund Long Term
- 28 <u>Reserve Fund</u> as set out in this section and the procedures set out herein
- 29 shall apply.
- 30 (2) When the Governor determines there is a need requiring
- 31 transfer from the Arkansas Rainy Day Fund Long Term Reserve Fund, he or she
- 32 shall instruct the Chief Fiscal Officer of the State to prepare and submit
- 33 written documentation to the Legislative Council or the Joint Budget
- 34 Committee. Such documentation shall include:
- 35 (A) Sufficient financial data that will enable the
- 36 verification of the existence of an emergency and the amount necessary to

- 1 address the need for rainy day funds long term reserve funds;
- 2 (B) A proposed distribution of moneys from the Arkansas
- 3 Rainy Day Fund Long Term Reserve Fund to one or more funds or fund accounts
- 4 in the Revenue Stabilization Law, or to the Economic Development
- 5 Superprojects Project Fund, or both; and
- 6 (C) A statement certifying that no other funds are
- 7 available that could be transferred in lieu of the funds in the Arkansas
- 8 Rainy Day Fund Long Term Reserve Fund.
- 9 (3) Such documentation shall be submitted to the Legislative
- 10 Council or Joint Budget Committee for approval prior to the implementation of
- 11 the proposed distribution. The Chief Fiscal Officer of the State, after
- 12 having sought and received prior approval of the Legislative Council or Joint
- 13 Budget Committee, shall cause the required transfers to be made on his or her
- 14 books and on the books of the Treasurer of State and the Auditor of State
- 15 from the Arkansas Rainy Day Fund Long Term Reserve Fund to the appropriate
- 16 funds and fund accounts in the Revenue Stabilization Law or to the Economic
- 17 Development Superprojects Project Fund, or both. In no event shall the
- 18 amounts transferred in any fiscal year to the funds and fund accounts in the
- 19 Revenue Stabilization Law by this section cause the general revenues to
- 20 exceed the maximum allocations authorized in the Revenue Stabilization Law.
- 21 (4) Determining the maximum amount of appropriation and general
- 22 revenue funding for a state agency each fiscal year is the prerogative of the
- 23 General Assembly. This is usually accomplished by delineating such maximums
- 24 in the appropriation acts for a state agency and the general revenue
- 25 allocations authorized for each fund and fund account by amendment to the
- 26 Revenue Stabilization Law. Further, the General Assembly has determined that
- 27 creating the Arkansas Rainy Day Fund Long Term Reserve Fund and establishing
- 28 the procedures for the transfer of funds to various funds and fund accounts
- 29 in the Revenue Stabilization Law or to the Economic Development Superprojects
- 30 Project Fund, or both, provides for the efficient and effective operation of
- 31 state government if a revenue shortfall is determined to exist. Therefore, it
- 32 is both necessary and appropriate that the General Assembly maintain
- 33 oversight by requiring prior approval of the Legislative Council or Joint
- 34 Budget Committee as provided by this section. The requirement of approval by
- 35 the Legislative Council or Joint Budget Committee is not a severable part of
- 36 this section. If the requirement of approval by the Legislative Council or

- Joint Budget Committee is ruled unconstitutional by a court of competent jurisdiction, this entire section is void.
- 3 (f) During each fiscal year, after the provisions of § 19-5-1004(b)(2) 4 are complied with, the Chief Fiscal Officer of the State may replenish the Arkansas Rainy Day Fund Long Term Reserve Fund by transferring no more than 5 6 fifty percent (50%) of the balance in the General Revenue Allotment Reserve 7 Fund or an amount equal to all transfers made under this section during the 8 fiscal year immediately preceding the fiscal year in which such replenishment 9 is made under this section, whichever is less, to the Arkansas Rainy Day Fund 10 Long Term Reserve Fund. In no event shall the balance of the Arkansas Rainy 11 Day Fund Long Term Reserve Fund exceed one hundred twenty five million

12 13

17

18

19

20

2122

SECTION 16. Arkansas Code § 26-56-201(f), concerning the imposition and distribution of distillate special fuels tax, is amended to read as follows:

dollars (\$125,000,000) at any time.

(f) Except as provided in subsection (g) of this section, the The additional taxes collected under this section are special revenues and shall be distributed as set forth in the Arkansas Highway Revenue Distribution Law, § 27-70-201 et seq., subject to any requirements for the repayment of bonds issued under the Arkansas Highway Financing Act of 1999, § 27-64-201 et seq., the Arkansas Interstate Highway Financing Act of 2007, § 27-64-401 et seq., and the Arkansas Highway Financing Act of 2011, § 27-64-501 et seq.

232425

26

27

28

29

30

31

3233

34

- SECTION 17. Arkansas Code § 26-56-201(g), concerning the imposition and distribution of distillate special fuels tax, is amended to read as follows:
- (g)(1) In order to offset the general revenues lost by the tax exemption contained in § 26-52-436(c) and (d) and § 26-53-144(c) and (d), the Chief Fiscal Officer of the State shall, on or before June 30, 2013, and on or before June 30 of each fiscal year thereafter, deposit the first four million dollars (\$4,000,000) of the taxes collected under subdivision (a)(1)(A)(i) of this section as general revenues, to be distributed as follows:
- 35 (A) Seventy five percent (75%) to be deposited into the 36 General Revenue Fund Account of the State Apportionment Fund;

1	(b) Fourteen and SIX tenths percent (14.0%) to be
2	deposited into the Educational Adequacy Fund;
3	(C) Eight and three tenths percent (8.3%) to be deposited
4	into the Property Tax Relief Trust Fund; and
5	(D) Two and one tenth percent (2.1%) to be deposited into
6	the Conservation Tax Fund.
7	(2) The balance of the taxes collected under subdivision
8	(a)(1)(A)(i) of this section shall be deposited as special revenues and
9	distributed in the manner required by law.
LO	(3) The classification and distribution of taxes under
l 1	subdivision (g)(l) of this section is subject to any requirements for the
12	repayment of bonds issued under the
13	Arkansas Highway Financing Act of 1999, § 27-64-201 et seq., and the Arkansa
L 4	Interstate Highway Financing Act of 2007, § 27-64-401 et seq.
15	(4) The taxes collected under subdivision (a)(1)(A)(ii) of this
16	section shall be distributed as provided in § 26-56-221.
L 7	
18	SECTION 18. Arkansas Code § 27-70-206(1) concerning distribution of
19	highway revenue to state funds, is amended to read as follows:
20	(1) First, except as provided by § 19-5-207, three percent (3%)
21	of the amount thereof to the Constitutional Officers Fund and the State
22	Central Services Fund, there to be used for the purposes specified for $\frac{1}{2}$
23	each fund by the Revenue Stabilization Law, § 19-5-101 et seq.;
24	
25	SECTION 19. Arkansas Code § 27-65-107(a), concerning the powers and
26	duties of the State Highway Commission, is amended to add additional
27	subdivisions to read as follows:
28	(18)(A) To propose and submit rules regarding the:
29	(i) Criteria for distribution of funds and the
30	distribution of funds from the:
31	(a) State Highway and Transportation
32	Department Fund; and
33	(b) Road and Bridge Repair, Maintenance, and
34	Grants Fund; and
35	(ii) Spending priority designated for highway
36	construction contracts and public road construction projects by the Arkansas

1	State Highway and Transportation Department and the commission, including the
2	criteria used to establish the spending priority.
3	(B)(i) The commission shall submit the proposed rules
4	required under subdivision (a)(18)(A) of this section to the Highway
5	Commission Review and Advisory Subcommittee of the Legislative Council for
6	review.
7	(ii) Proposed rules required under subdivision
8	(a)(18)(A) of this section that are under consideration at the time the act
9	passes do not require review by the Highway Commission Review and Advisory
10	Subcommittee of the Legislative Council prior to implementation but shall be
11	submitted to the Highway Commission Review and Advisory Subcommittee of the
12	Legislative Council by October 1, 2017 as a report.
13	(iii) The proposed rules required under subdivision
14	(a)(18)(A) of this section are not required to be promulgated under the
15	Arkansas Administrative Procedure Act, § 25-15-201 et seq., but shall be
16	published after review by the Highway Commission Review and Advisory
17	Subcommittee of the Legislative Council; and
18	(19) To provide the Highway Commission Review and Advisory
19	Subcommittee of the Legislative Council with a report on the progress of each
20	public road construction project of ten million dollars (\$10,000,000) or more
21	at least quarterly or as required by the Highway Commission Review and
22	Advisory Subcommittee of the Legislative Council.
23	
24	SECTION 20. Arkansas Code § 27-65-107, concerning the powers and
25	duties of the State Highway Commission, is amended to add an additional
26	subsection to read as follows:
27	(d) As used in this section:
28	(1) "Highway construction contract" means a contract for the
29	construction, restoration, reconstruction, renovation, or repair of a road,
30	highway, bridge, overpass, interchange, right-of-way, or turnpike that is
31	part of the state highway system; and
32	(2) "Public road construction project" means the construction,
33	restoration, reconstruction, renovation, or repair of a road, highway,
34	street, bridge, overpass, interchange, or right-of-way in which the
35	construction, restoration, reconstruction, renovation, or repair is to be
36	performed or is initiated by the Arkansas State Highway and Transportation

1	Department or the commission.
2	
3	SECTION 21. TEMPORARY LANGUAGE. DO NOT CODIFY.
4	(a) The Chief Fiscal Officer of the State shall make a one-time
5	transfer on his or her books and those of the Treasurer of State and the
6	Auditor of State the sum of forty million dollars (\$40,000,000) from the
7	funds available in the Rainy Day Set-Aside of the $90^{\mathrm{th}}$ Session Projects
8	Account of the General Improvement Fund as authorized by Acts 2015, No. 1147,
9	§ 3(a)(11), to the Arkansas Highway Transfer Fund there to be used only for
10	the purposes set forth in § 19-6-832.
11	(b) Disbursement of funds authorized by this act shall be limited to
12	the appropriation for the agency and funds made available by law for the
13	support of the appropriations. The restrictions of the Arkansas Procurement
14	Law, § 19-11-201 et seq., the General Accounting and Budgetary Procedures
15	Law, § 19-4-101 et seq., the Revenue Stabilization Law, § 19-5-101 et seq.,
16	the Regular Salary Procedures and Restrictions Act, § 21-5-101 et seq., and
17	other fiscal control laws of this state, where applicable, and regulations
18	promulgated by the Department of Finance and Administration, as authorized by
19	law, shall be strictly complied with in disbursement of the funds.
20	(c) It is the intent of the General Assembly that any funds disbursed
21	under the authority of this act shall be in compliance with the stated
22	reasons for which this act was adopted, as evidenced by the Agency Requests,
23	Executive Recommendations, and Legislative Recommendations contained in the
24	budget manuals prepared by the Department of Finance and Administration,
25	letters, or summarized oral testimony in the official minutes of the
26	Legislative Council or Joint Budget Committee which relate to its passage and
27	adoption.
28	
29	SECTION 22. EFFECTIVE DATE. Sections 9-12, 14, 16 and 17 of this act
30	are effective on and after July 1, 2017.
31	
32	SECTION 23. EMERGENCY CLAUSE. It is found and determined by the
33	General Assembly of the State of Arkansas that Arkansas bridges and roads are
34	in need of repair and proper maintenance; that the repair and proper
35	maintenance of Arkansas bridges and roads are necessary for the preservation
36	of the public peace, health, and safety; that increased funding is essential

1	to the repair and proper maintenance of Arkansas bridges and roads; that this
2	act is designed to provide the necessary funding that is essential to the
3	repair and proper maintenance of Arkansas bridges and roads, and this act is
4	necessary because without this increased funding, the repair and proper
5	maintenance of Arkansas bridges and roads may not be performed. Therefore, an
6	emergency is declared to exist, and Sections 1-8, 13, 15, 18-21 of this act
7	being immediately necessary for the preservation of the public peace, health,
8	and safety shall become effective on July 1, 2016.
9	
10	
11	APPROVED: 05/23/2016
12	
13	
14	
15	
16	
17	
18	
19	
20	
21	
22	
23	
24	
25	
26	
27	
28	
29 30	
31	
32	
33	
34	
35	
36	



