



SFY 2019 1st QUARTER

REPORT TO THE

HIGHWAY COMMISSION
REVIEW & ADVISORY SUBCOMMITTEE



ARKANSAS HIGHWAY COMMISSION
10324 Interstate 30, Little Rock, Arkansas 72209

INTRODUCTION

In accordance with the Arkansas Highway Improvement Act of 2016, and specifically Arkansas Code § 27-65-107(a)(19), the Arkansas Highway Commission submits this report on the progress of each public road construction project of ten million dollars (\$10,000,000) or more to the Highway Commission Review and Advisory Subcommittee of the Legislative Council.

For additional information contact :

Gill A. Rogers | Governmental Relations Officer

Arkansas Department of Transportation

P.O. Box 2261 | Little Rock, AR 72203

10324 Interstate 30 | Little Rock, AR 72209

Office: (501) 569-2108 Cell: (501) 920-3172

Gill.Rogers@ardot.gov

GLOSSARY

ACHM – Asphalt Concrete Hot Mix

Bridge and Approaches – Constructing bridge structures and sections leading up to the bridge

Calendar day contract – Contract where the number of calendar days are bid

CAP – Connecting Arkansas Program

(F) – Project with Federal Oversight

Grading and Structures – Earthwork and bridge construction; “structures” includes bridges and drainage structures

Interchange – Improvements to the junction between two or more roadways, typically including an overpass or bridge with associated ramps

IRP – Interstate Rehabilitation Program

Major Widening – Widening of an existing roadway to improve capacity or enhance safety, generally by adding a lane or lanes

New Location – Construction of a roadway on a location not previously developed for vehicular transportation

PCC Pavement – Portland Cement Concrete Pavement

Reconstruction – Generally, removing an existing roadway and building a new road in the same place

Rehabilitation – Modifying or improving an existing roadway; generally less costly and less time consuming than a full reconstruction

Resurfacing – Installation or application of a new driving surface; could be an overlay, sealing job, or similar procedure

(S) – Project with State Oversight

Safety and Traffic Engineering – Various improvements to enhance safety and/or improve traffic flow

Working Day Contract – Contract for which time will be assessed for each day on which conditions allow the Contractor to work per Standard Specification for Highway Construction 108.06



**PROJECTS
UNDER CONSTRUCTION**
As of September 30, 2018

PROJECTS UNDER CONSTRUCTION

SORTED BY ROUTE

Sorted by Route Under Construction

Route	County	Job No	Job Name	Let Date	Cost (\$ in Million)	Page #
I-30	Clark, Hempstead & Nevada	BB1101	Hwy. 299 - Gurdon Rest Area (S)	09/12/2018	39.0	9
I-40	Prairie	BB0610	White River Str. & Apprs. (F)	11/02/2016	100.6	10
I-40	St. Francis	BB0112	Fishing Lake Str. & Apprs. (S)	09/01/2015	26.7	11
I-49	Benton	BB0903	Hwy. 71B Intchng. Impvts. (S)	07/25/2018	26.9	12
I-49	Benton	090376	Hwy. 62/102 Intchng. Impvts. & 8th Street Widening (Bentonville) (S)	11/02/2016	28.8	13
I-69	Drew	020484	Hwy. 425 - Hwy. 278 East (Bs. & Surf.) (Monticello Bypass) (S)	08/30/2017	16.2	14
I-530	Jefferson	BB0203	Hwy. 65B - Hwy. 65 (F)	07/19/2017	67.2	15
I-555	Poinsett	100956	Sunken Lands Strs. Rehab. (I-555) (S)	08/30/2017	12.3	16
I-630	Pulaski	CA0608	Baptist Hospital - University Ave. (Widening) (F)	04/04/2018	87.4	17
Hwy. 4 & 4S	Desha	020573	Ditch No. 43 - Arkansas City (S)	04/12/2017	12.9	18
Hwy. 5	Saline	061335	Alcoa Rd. - Hwy. 183 (S)	09/12/2018	17.4	19
Hwy. 7	Garland	060432	Hwy. 290 - Ouachita River Bridge (S)	04/12/2017	10.7	20
Hwy. 14	Jackson	050272	Cache River-Amagon Strs. & Apprs. (S)	02/10/2016	11.9	21
Hwy. 18	Mississippi	CA1002	Manila - East (Widening) (S)	11/02/2016	35.5	22
Hwy. 41	Little River & Sevier	030415	Little River Str. & Apprs. (S)	03/23/2016	14.0	23
Hwy. 62	Carroll	090230	Co. Rd. 914-West (S)	09/21/2016	17.8	24
Hwy. 63	Fulton	050230	Hwy. 9-So. of Hwy. 342 (Mammoth Spring) (S)	12/17/2014	21.6	25
Hwy. 64	Cross, White & Woodruff	012287	Hwy. 367 - Crittenden Co. Line (S)	07/19/2017	19.1	26
Hwy. 64	Faulkner & White	012155	Vilonia Bypass-East (F)	01/13/2016	21.4	27
Hwy. 65	Boone	CA0906	Maxie Camp Rd. - Hwy. 206 (Widening) (S)	08/30/2017	22.9	28
Hwy. 65	Van Buren	080423	Bee Branch-North (S)	11/15/2017	30.9	29

Sorted by Route
Under Construction

Route	County	Job No	Job Name	Let Date	Cost (\$ in Million)	Page #
Hwy. 67	Lonoke	061102	Hwy. 67 Interchange (N. of Cabot) (S)	12/07/2016	25.5	30
Hwy. 67	Lonoke & Pulaski	CA0605	Vandenberg Blvd. - Hwy. 5 (Widening) (S)	12/07/2016	79.3	31
Hwy. 67	Randolph	100759	Black River Str. & Apprs. (Pocahontas) (S)	03/23/2016	10.1	32
Hwy. 79	Monroe	110540	White River Strs. Demo. & Removal (Clarendon) (S)	01/17/2018	11.3	33
Hwy. 82	Ashley	020534	Co. Rd. 411 - Hwy. 425 (East of Crossett) (S)	11/02/2016	24.7	34
Hwy. 82	Ashley	CA0202	Hwy. 425 - Hamburg (Widening) (S)	09/12/2018	26.7	35
Hwy. 82	Columbia	070365	Hwy. 79 No.-Co. Rd. 525 (Magnolia) (S)	03/23/2016	22.2	36
Hwy. 167	Calhoun	070283	Bangs Slough-Hwy. 172 (S)	06/22/2016	17.0	37
Hwy. 167	Calhoun	CA0702	Hampton - Hwy. 274 (Widening) (S)	07/19/2017	21.8	38
Hwy. 167	Calhoun	CA0703	Hwy. 274 - North (Widening) (S)	02/21/2018	29.0	39
Hwy. 167	Union	070280	El Dorado-Hwy. 335 (S)	10/13/2015	21.2	40
Hwy. 167	Calhoun & Union	070282	Ouachita River Str. & Apprs. (S)	11/05/2014	29.4	41
Hwy. 265	Benton	090373	Hwy. 264-Pleasant Grove Rd. (S)	12/01/2015	15.4	42
Hwy. 265	Benton & Washington	012007	Randall Wobbe Lane - Hwy. 264 (Springdale) (S)	11/15/2017	10.2	43
Hwy. 335	Union	070368	Hwy. 82 - Hwy. 7 (Rehab.) (S)	11/02/2016	11.4	44
Hwy. 367	Jackson	005836	White River Str. & Apprs. (Newport) (S)	10/30/2013	31.4	45
Hwy. 412	Greene	100708	Hwy. 412 West-Hwy. 49 (S)	01/18/2017	12.8	46
Hwy. 425	Ashley	CA0201	Louisiana State Line - Hwy. 82 (Widening) (S)	09/12/2018	44.6	47
Hwy. 549	Benton	090508	Hwy. 71 - Co. Rd. 34 (Add'l Lns.) (B.V. Bypass) (S)	11/15/2017	27.5	48

PROJECTS UNDER CONSTRUCTION
SORTED BY COUNTY

Sorted by County Under Construction

County	Route	Job No	Job Name	Let Date	Cost (\$ in Million)	Page #
Ashley	Hwy. 82	020534	Co. Rd. 411 - Hwy. 425 (East of Crossett) (S)	11/02/2016	24.7	34
Ashley	Hwy. 82	CA0202	Hwy. 425 - Hamburg (Widening) (S)	09/12/2018	26.7	35
Ashley	Hwy. 425	CA0201	Louisiana State Line - Hwy. 82 (Widening) (S)	09/12/2018	44.6	47
Benton	I-49	090376	Hwy. 62/102 Intchn. Impvts. & 8th Street Widening (Bentonville) (S)	11/02/2016	28.8	13
Benton	I-49	BB0903	Hwy. 71B Intchn. Impvts. (S)	07/25/2018	26.9	12
Benton	Hwy. 265	090373	Hwy. 264-Pleasant Grove Rd. (S)	12/01/2015	15.4	42
Benton	Hwy. 549	090508	Hwy. 71 - Co. Rd. 34 (Add'l Lns.) (B.V. Bypass) (S)	11/15/2017	27.5	48
Benton & Washington	Hwy. 265	012007	Randall Wobbe Lane - Hwy. 264 (Springdale) (S)	11/15/2017	10.2	43
Boone	Hwy. 65	CA0906	Maxie Camp Rd. - Hwy. 206 (Widening) (S)	08/30/2017	22.9	28
Calhoun	Hwy. 167	070283	Bangs Slough-Hwy. 172 (S)	06/22/2016	17.0	37
Calhoun	Hwy. 167	CA0702	Hampton - Hwy. 274 (Widening) (S)	07/19/2017	21.8	38
Calhoun	Hwy. 167	CA0703	Hwy. 274 - North (Widening) (S)	02/21/2018	29.0	39
Calhoun & Union	Hwy. 167	070282	Ouachita River Str. & Apprs. (S)	11/05/2014	29.4	41
Carroll	Hwy. 62	090230	Co. Rd. 914-West (S)	09/21/2016	17.8	24
Clark, Hempstead & Nevada	I-30	BB1101	Hwy. 299 - Gurdon Rest Area (S)	09/12/2018	39.0	9
Columbia	Hwy. 82	070365	Hwy. 79 No.-Co. Rd. 525 (Magnolia) (S)	03/23/2016	22.2	36
Cross, White & Woodruff	Hwy. 64	012287	Hwy. 367 - Crittenden Co. Line (S)	07/19/2017	19.1	26
Desha	Hwy. 4 & 4S	020573	Ditch No. 43 - Arkansas City (S)	04/12/2017	12.9	18
Drew	I-69	020484	Hwy. 425 - Hwy. 278 East (Bs. & Surf.) (Monticello Bypass) (S)	08/30/2017	16.2	14
Faulkner & White	Hwy. 64	012155	Vilonia Bypass-East (F)	01/13/2016	21.4	27
Fulton	Hwy. 63	050230	Hwy. 9-So. of Hwy. 342 (Mammoth Spring) (S)	12/17/2014	21.6	25

Sorted by County Under Construction

County	Route	Job No	Job Name	Let Date	Cost (\$ in Million)	Page #
Garland	Hwy. 7	060432	Hwy. 290 - Ouachita River Bridge (S)	04/12/2017	10.7	20
Greene	Hwy. 412	100708	Hwy. 412 West-Hwy. 49 (S)	01/18/2017	12.8	46
Jackson	Hwy. 14	050272	Cache River-Amagon Strs. & Apprs. (S)	02/10/2016	11.9	21
Jackson	Hwy. 367	005836	White River Str. & Apprs. (Newport) (S)	10/30/2013	31.4	45
Jefferson	I-530	BB0203	Hwy. 65B - Hwy. 65 (F)	07/19/2017	67.2	15
Little River & Sevier	Hwy. 41	030415	Little River Str. & Apprs. (S)	03/23/2016	14.0	23
Lonoke	Hwy. 67	061102	Hwy. 67 Interchange (N. of Cabot) (S)	12/07/2016	25.5	30
Lonoke & Pulaski	Hwy. 67	CA0605	Vandenberg Blvd. - Hwy. 5 (Widening) (S)	12/07/2016	79.3	31
Monroe	Hwy. 79	110540	White River Strs. Demo. & Removal (Clarendon) (S)	01/17/2018	11.3	33
Mississippi	Hwy. 18	CA1002	Manila - East (Widening) (S)	11/02/2016	35.5	22
Poinsett	I-555	100956	Sunken Lands Strs. Rehab. (I-555) (S)	08/30/2017	12.3	16
Prairie	I-40	BB0610	White River Str. & Apprs. (F)	11/02/2016	100.6	10
Pulaski	I-630	CA0608	Baptist Hospital - University Ave. (Widening) (F)	04/04/2018	87.4	17
Randolph	Hwy. 67	100759	Black River Str. & Apprs. (Pocahontas) (S)	03/23/2016	10.1	32
Saline	Hwy. 5	061335	Alcoa Rd. - Hwy. 183 (S)	09/12/2018	17.4	19
St. Francis	I-40	BB0112	Fishing Lake Str. & Apprs. (S)	09/01/2015	26.7	11
Union	Hwy. 167	070280	El Dorado-Hwy. 335 (S)	10/13/2015	21.2	40
Union	Hwy. 335	070368	Hwy. 82 - Hwy. 7 (Rehab.) (S)	11/02/2016	11.4	44
Van Buren	Hwy. 65	080423	Bee Branch-North (S)	11/15/2017	30.9	29

SUMMARY PROGRESS REPORTS

SORTED BY ROUTE

Arkansas Department of Transportation
Summary Progress Report
Projects Awarded at \$10 Million or More

Contract ID: BB1101
Contract Name: Hwy. 299 - Gurdon Rest Area (S)
Funding Type: IRP, Federal, & State
District: 3 & 7
County: Clark, Hempstead & Nevada
Route: I-30

Prime Contractor: Redstone Const. Group, Inc.
Type of Work: Resurfacing
Contract Bid Amount: \$39,017,512.83
Current Contract Amount: \$39,017,512.83
Total Amount Paid: \$0.00
Amount Remaining: \$39,017,512.83 (Based on Current Contract Amount)
Percent Complete: 0.0% (Calculated from the Current Contract Amount)
Percent Time Used: 0.0% This is a calendar day contract.

Letting Date: September 12, 2018
Work Order Date: TBD
Original Estimated Completion Date: Mid 2020
Current Estimated Completion Date: Mid 2020

Description of Project:

The purpose of this project is to resurface 19.3 miles of I-30 in Clark, Hempstead and Nevada Counties.

Arkansas Department of Transportation
Summary Progress Report
Projects Awarded at \$10 Million or More

Contract ID: BB0610
Contract Name: White River Str. & Apprs. (F)
Funding Type: IRP, Federal, & State
District: 6
County: Prairie
Route: I-40

Prime Contractor: Parsons-Mahan
Type of Work: Bridge And Approaches
Contract Bid Amount: \$100,559,842.64
Current Contract Amount: \$99,873,975.42
Total Amount Paid: \$64,134,843.55
Amount Remaining: \$35,739,131.87 (Based on Current Contract Amount)
Percent Complete: 64.2% (Calculated from the Current Contract Amount)
Percent Time Used: 45.3% This is a working day contract.

Letting Date: November 02, 2016
Work Order Date: December 29, 2016
Original Estimated Completion Date: Mid 2020
Current Estimated Completion Date: Late 2019

Description of Project:

The purpose of this project is to replace the White River Bridge on I-40 in Prairie County.

Arkansas Department of Transportation
Summary Progress Report
Projects Awarded at \$10 Million or More

Contract ID: BB0112
Contract Name: Fishing Lake Str. & Apprs. (S)
Funding Type: IRP, Federal, & State
District: 1
County: St. Francis
Route: I-40

Prime Contractor: Manhattan Road & Bridge Co.
Type of Work: Bridge And Approaches
Contract Bid Amount: \$26,710,417.68
Current Contract Amount: \$27,866,608.86
Total Amount Paid: \$25,297,231.17
Amount Remaining: \$2,569,377.69 (Based on Current Contract Amount)
Percent Complete: 90.8% (Calculated from the Current Contract Amount)
Percent Time Used: 91.1% This is a working day contract.

Letting Date: September 01, 2015
Work Order Date: October 09, 2015
Original Estimated Completion Date: Mid 2018
Current Estimated Completion Date: Late 2018

Description of Project:

The purpose of this project is to replace the I-40 bridge over Fishing Lake in St. Francis County.

Arkansas Department of Transportation
Summary Progress Report
Projects Awarded at \$10 Million or More

Contract ID: BB0903
Contract Name: Hwy. 71B Intchnng. Impvts. (S)
Funding Type: Federal, State, & Local
District: 9
County: Benton
Route: I-49

Prime Contractor: Apac-Central, Inc.
Type of Work: Interchange
Contract Bid Amount: \$26,897,563.15
Current Contract Amount: \$26,897,563.15
Total Amount Paid: \$0.00
Amount Remaining: \$26,897,563.15 (Based on Current Contract Amount)
Percent Complete: 0.0% (Calculated from the Current Contract Amount)
Percent Time Used: 0.0% This is a calendar day contract.

Letting Date: July 25, 2018
Work Order Date: September 13, 2018
Original Estimated Completion Date: Late 2020
Current Estimated Completion Date: Late 2020

Description of Project:

The purpose of this project is to construct a Single Point Urban Interchange (SPUI) at the Hwy 71B Intersection on I-49 in Benton County.

Arkansas Department of Transportation
Summary Progress Report
Projects Awarded at \$10 Million or More

Contract ID: 090376
Contract Name: Hwy. 62/102 Intchn. Impvts. & 8th Street Widening (Bentonville) (S)
Funding Type: Federal, State, & Local
District: 9
County: Benton
Route: I-49

Prime Contractor: Crossland Construction Co., Inc.
Type of Work: Interchange
Contract Bid Amount: \$28,808,497.29
Current Contract Amount: \$29,238,557.97
Total Amount Paid: \$20,014,671.64
Amount Remaining: \$9,223,886.33 (Based on Current Contract Amount)
Percent Complete: 68.5% (Calculated from the Current Contract Amount)
Percent Time Used: 83.8% This is a calendar day contract.

Letting Date: November 02, 2016
Work Order Date: January 04, 2017
Original Estimated Completion Date: Mid 2018
Current Estimated Completion Date: Early 2019

Description of Project:

The purpose of this project is to extend 8th Street, construct a new interchange at 8th Street on I-49 and improve the interchange at Hwy. 62/102 in Benton County.

Arkansas Department of Transportation
Summary Progress Report
Projects Awarded at \$10 Million or More

Contract ID: 020484
Contract Name: Hwy. 425 - Hwy. 278 East (Bs. & Surf.) (Monticello Bypass) (S)
Funding Type: Federal & State
District: 2
County: Drew
Route: I-69

Prime Contractor: Pine Bluff Sand & Gravel Co.
Type of Work: New Location
Contract Bid Amount: \$16,197,356.29
Current Contract Amount: \$16,718,361.12
Total Amount Paid: \$16,063,442.20
Amount Remaining: \$654,918.92 (Based on Current Contract Amount)
Percent Complete: 96.1% (Calculated from the Current Contract Amount)
Percent Time Used: 76.3% This is a working day contract.

Letting Date: August 30, 2017
Work Order Date: October 05, 2017
Original Estimated Completion Date: Late 2018
Current Estimated Completion Date: Late 2018

Description of Project:

The purpose of this project is to place the base and surface for the Monticello Bypass in Drew County.

Arkansas Department of Transportation
Summary Progress Report
Projects Awarded at \$10 Million or More

Contract ID: BB0203
Contract Name: Hwy. 65B - Hwy. 65 (F)
Funding Type: IRP, Federal, & State
District: 2
County: Jefferson
Route: I-530

Prime Contractor: Webber, LLC
Type of Work: Reconstruction
Contract Bid Amount: \$67,232,300.00
Current Contract Amount: \$67,012,858.81
Total Amount Paid: \$23,763,824.92
Amount Remaining: \$43,249,033.89 (Based on Current Contract Amount)
Percent Complete: 35.5% (Calculated from the Current Contract Amount)
Percent Time Used: 38.8% This is a calendar day contract.

Letting Date: July 19, 2017
Work Order Date: September 12, 2017
Original Estimated Completion Date: Mid 2019
Current Estimated Completion Date: Late 2019

Description of Project:

The purpose of this project is to reconstruct 10.35 miles of I-530 in Pine Bluff, Jefferson County.

Arkansas Department of Transportation
Summary Progress Report
Projects Awarded at \$10 Million or More

Contract ID: 100956
Contract Name: Sunken Lands Strs. Rehab. (I-555) (S)
Funding Type: Federal & State
District: 10
County: Poinsett
Route: I-555

Prime Contractor: American Contrg. & Svs., Inc.
Type of Work: Bridge Rehabilitation
Contract Bid Amount: \$12,272,673.80
Current Contract Amount: \$12,389,606.85
Total Amount Paid: \$11,099,666.99
Amount Remaining: \$1,289,939.86 (Based on Current Contract Amount)
Percent Complete: 89.6% (Calculated from the Current Contract Amount)
Percent Time Used: 65.5% This is a calendar day contract.

Letting Date: August 30, 2017
Work Order Date: October 13, 2017
Original Estimated Completion Date: Late 2018
Current Estimated Completion Date: Late 2018

Description of Project:

The purpose of this project is to rehabilitate 16 bridges on 1.71 miles on I-555 in Poinsett County.

Arkansas Department of Transportation
Summary Progress Report
Projects Awarded at \$10 Million or More

Contract ID: CA0608
Contract Name: Baptist Hospital - University Ave. (Widening) (F)
Funding Type: CAP, Federal, & State
District: 6
County: Pulaski
Route: I-630

Prime Contractor: Manhattan Road & Bridge Co.
Type of Work: Major Widening
Contract Bid Amount: \$87,384,772.06
Current Contract Amount: \$87,715,381.19
Total Amount Paid: \$14,764,799.90
Amount Remaining: \$72,950,581.29 (Based on Current Contract Amount)
Percent Complete: 16.8% (Calculated from the Current Contract Amount)
Percent Time Used: 2.4% This is a calendar day contract.

Letting Date: April 04, 2018
Work Order Date: May 25, 2018
Original Estimated Completion Date: Early 2020
Current Estimated Completion Date: Mid 2020

Description of Project:

The purpose of this project is to widen 2.2 miles of I-630 from six lanes to eight lanes in Little Rock, Pulaski County.

Arkansas Department of Transportation
Summary Progress Report
Projects Awarded at \$10 Million or More

Contract ID: 020573
Contract Name: Ditch No. 43 - Arkansas City (S)
Funding Type: Federal & State
District: 2
County: Desha
Route: Hwy. 4 & 4S

Prime Contractor: R. Thompson, Inc.
Type of Work: Reconstruction
Contract Bid Amount: \$12,883,464.56
Current Contract Amount: \$13,172,640.59
Total Amount Paid: \$8,843,229.11
Amount Remaining: \$4,329,411.48 (Based on Current Contract Amount)
Percent Complete: 67.1% (Calculated from the Current Contract Amount)
Percent Time Used: 94.7% This is a fixed date contract.

Letting Date: April 12, 2017
Work Order Date: April 28, 2017
Original Estimated Completion Date: Late 2018
Current Estimated Completion Date: Late 2018

Description of Project:

The purpose of this project is to reconstruct 5.1 miles of Hwys. 4 & 4S in Desha County.

Arkansas Department of Transportation
Summary Progress Report
Projects Awarded at \$10 Million or More

Contract ID: 061335
Contract Name: Alcoa Rd. - Hwy. 183 (S)
Funding Type: Federal & State
District: 6
County: Saline
Route: Hwy. 5

Prime Contractor: Redstone Const. Group, Inc.
Type of Work: Major Widening
Contract Bid Amount: \$17,394,675.98
Current Contract Amount: \$17,394,675.98
Total Amount Paid: \$0.00
Amount Remaining: \$17,394,675.98 (Based on Current Contract Amount)
Percent Complete: 0.0% (Calculated from the Current Contract Amount)
Percent Time Used: 0.0% This is a calendar day contract.

Letting Date: September 12, 2018
Work Order Date: October 26, 2018
Original Estimated Completion Date: Mid 2020
Current Estimated Completion Date: Mid 2020

Description of Project:

The purpose of this project is to widen 2.3 miles of Hwy. 5 from two lanes to five lanes in Saline County.

Arkansas Department of Transportation
Summary Progress Report
Projects Awarded at \$10 Million or More

Contract ID: 060432
Contract Name: Hwy. 290 - Ouachita River Bridge (S)
Funding Type: Federal & State
District: 6
County: Garland
Route: Hwy. 7

Prime Contractor: Kiewit Infrastructure South Co.
Type of Work: Major Widening
Contract Bid Amount: \$10,698,642.19
Current Contract Amount: \$11,286,790.72
Total Amount Paid: \$8,905,431.86
Amount Remaining: \$2,381,358.86 (Based on Current Contract Amount)
Percent Complete: 78.9% (Calculated from the Current Contract Amount)
Percent Time Used: 71.3% This is a calendar day contract.

Letting Date: April 12, 2017
Work Order Date: May 30, 2017
Original Estimated Completion Date: Early 2018
Current Estimated Completion Date: Late 2018

Description of Project:

The purpose of this project is to widen 1.4 miles of Hwy. 7 from two lanes to five lanes south of Hot Springs in Garland County.

Arkansas Department of Transportation
Summary Progress Report
Projects Awarded at \$10 Million or More

Contract ID: 050272
Contract Name: Cache River-Amagon Strs. & Apprs. (S)
Funding Type: Federal & State
District: 5
County: Jackson
Route: Hwy. 14

Prime Contractor: Robertson, Inc., Bridge & Grading Div.
Type of Work: Bridges And Approaches
Contract Bid Amount: \$11,908,017.25
Current Contract Amount: \$12,510,989.52
Total Amount Paid: \$11,898,859.46
Amount Remaining: \$612,130.06 (Based on Current Contract Amount)
Percent Complete: 95.1% (Calculated from the Current Contract Amount)
Percent Time Used: 107.6% This is a working day contract.

Letting Date: February 10, 2016
Work Order Date: March 25, 2016
Original Estimated Completion Date: Late 2018
Current Estimated Completion Date: Late 2018

Description of Project:

The purpose of this project is to replace four bridge structures on Hwy. 14 east of Newport in Jackson County.

Arkansas Department of Transportation
Summary Progress Report
Projects Awarded at \$10 Million or More

Contract ID: CA1002
Contract Name: Manila - East (Widening) (S)
Funding Type: CAP, Federal, & State
District: 10
County: Mississippi
Route: Hwy. 18

Prime Contractor: W.G. Yates & Sons Const. Co.
Type of Work: Major Widening
Contract Bid Amount: \$35,471,089.83
Current Contract Amount: \$36,154,429.38
Total Amount Paid: \$13,051,610.36
Amount Remaining: \$23,102,819.02 (Based on Current Contract Amount)
Percent Complete: 36.1% (Calculated from the Current Contract Amount)
Percent Time Used: 62.7% This is a calendar day contract.

Letting Date: November 02, 2016
Work Order Date: December 19, 2016
Original Estimated Completion Date: Early 2019
Current Estimated Completion Date: Late 2019

Description of Project:

The purpose of this project is to widen 1.8 miles of Hwy. 18 from two lanes to five lanes east of Manila in Mississippi County.

Arkansas Department of Transportation
Summary Progress Report
Projects Awarded at \$10 Million or More

Contract ID: 030415
Contract Name: Little River Str. & Apprs. (S)
Funding Type: Federal & State
District: 3
County: Little River & Sevier
Route: Hwy. 41

Prime Contractor: Jensen Construction Co.
Type of Work: Bridge And Approaches
Contract Bid Amount: \$13,965,914.82
Current Contract Amount: \$14,186,344.61
Total Amount Paid: \$10,937,705.44
Amount Remaining: \$3,248,639.17 (Based on Current Contract Amount)
Percent Complete: 77.1% (Calculated from the Current Contract Amount)
Percent Time Used: 78.1% This is a working day contract.

Letting Date: March 23, 2016
Work Order Date: May 13, 2016
Original Estimated Completion Date: Late 2018
Current Estimated Completion Date: Early 2019

Description of Project:

The purpose of this project is to replace the bridge on Hwy. 41 that crosses the Little River in Little River and Sevier Counties.

Arkansas Department of Transportation
Summary Progress Report
Projects Awarded at \$10 Million or More

Contract ID: 090230
Contract Name: Co. Rd. 914-West (S)
Funding Type: Federal & State
District: 9
County: Carroll
Route: Hwy. 62

Prime Contractor: Nabholz Construction Corporation
Type of Work: Major Widening
Contract Bid Amount: \$17,804,173.30
Current Contract Amount: \$18,924,513.67
Total Amount Paid: \$14,013,671.50
Amount Remaining: \$4,910,842.17 (Based on Current Contract Amount)
Percent Complete: 74.1% (Calculated from the Current Contract Amount)
Percent Time Used: 76.0% This is a calendar day contract.

Letting Date: September 21, 2016
Work Order Date: November 08, 2016
Original Estimated Completion Date: Late 2018
Current Estimated Completion Date: Late 2018

Description of Project:

The purpose of this project is to widen 3.7 miles of Hwy. 62 west of Alpena from two lanes to five lanes in Carroll County.

Arkansas Department of Transportation
Summary Progress Report
Projects Awarded at \$10 Million or More

Contract ID: 050230
Contract Name: Hwy. 9-So. of Hwy. 342 (Mammoth Spring) (S)
Funding Type: Federal & State
District: 5
County: Fulton
Route: Hwy. 63

Prime Contractor: Pace Construction Co., LLC
Type of Work: Major Widening
Contract Bid Amount: \$21,633,578.03
Current Contract Amount: \$22,655,757.77
Total Amount Paid: \$20,501,016.36
Amount Remaining: \$2,154,741.41 (Based on Current Contract Amount)
Percent Complete: 90.5% (Calculated from the Current Contract Amount)
Percent Time Used: 93.1% This is a working day contract.

Letting Date: December 17, 2014
Work Order Date: February 18, 2015
Original Estimated Completion Date: Late 2017
Current Estimated Completion Date: Late 2018

Description of Project:

The purpose of this project is to widen 1.9 miles of Hwy. 63 from three lanes to five lanes in Mammoth Spring, Fulton County.

Arkansas Department of Transportation
Summary Progress Report
Projects Awarded at \$10 Million or More

Contract ID: 012287
Contract Name: Hwy. 367 - Crittenden Co. Line (S)
Funding Type: Federal & State
District: 1 & 5
County: Cross, White & Woodruff
Route: Hwy. 64

Prime Contractor: Atlas Asphalt, Inc.
Type of Work: Resurfacing
Contract Bid Amount: \$19,149,094.56
Current Contract Amount: \$19,837,274.24
Total Amount Paid: \$16,802,646.45
Amount Remaining: \$3,034,627.79 (Based on Current Contract Amount)
Percent Complete: 84.7% (Calculated from the Current Contract Amount)
Percent Time Used: 76.5% This is a working day contract.

Letting Date: July 19, 2017
Work Order Date: September 05, 2017
Original Estimated Completion Date: Mid 2018
Current Estimated Completion Date: Late 2018

Description of Project:

The purpose of this project is to resurface 62.51 miles of Hwy. 64 in Cross, White and Woodruff Counties.

Arkansas Department of Transportation
Summary Progress Report
Projects Awarded at \$10 Million or More

Contract ID: 012155
Contract Name: Vilonia Bypass-East (F)
Funding Type: Federal & State
District: 5 & 8
County: Faulkner & White
Route: Hwy. 64

Prime Contractor: Rogers Group, Inc.
Type of Work: Major Widening
Contract Bid Amount: \$21,386,020.44
Current Contract Amount: \$21,716,330.00
Total Amount Paid: \$18,123,290.31
Amount Remaining: \$3,593,039.69 (Based on Current Contract Amount)
Percent Complete: 83.5% (Calculated from the Current Contract Amount)
Percent Time Used: 83.4% This is a working day contract.

Letting Date: January 13, 2016
Work Order Date: March 15, 2016
Original Estimated Completion Date: Late 2018
Current Estimated Completion Date: Late 2018

Description of Project:

The purpose of this project is to widen 7.4 miles of Hwy. 64 from two lanes to five lanes east of Vilonia in Faulkner and White Counties.

Arkansas Department of Transportation
Summary Progress Report
Projects Awarded at \$10 Million or More

Contract ID: CA0906
Contract Name: Maxie Camp Rd. - Hwy. 206 (Widening) (S)
Funding Type: CAP & State
District: 9
County: Boone
Route: Hwy. 65

Prime Contractor: Nabholz Construction Corporation
Type of Work: Major Widening
Contract Bid Amount: \$22,942,315.85
Current Contract Amount: \$23,613,698.99
Total Amount Paid: \$7,186,503.59
Amount Remaining: \$16,427,195.40 (Based on Current Contract Amount)
Percent Complete: 30.4% (Calculated from the Current Contract Amount)
Percent Time Used: 41.1% This is a calendar day contract.

Letting Date: August 30, 2017
Work Order Date: October 11, 2017
Original Estimated Completion Date: Mid 2019
Current Estimated Completion Date: Late 2019

Description of Project:

The purpose of this project is to widen 4.37 miles of Hwy. 65 from two lanes to five lanes in Boone County.

Arkansas Department of Transportation
Summary Progress Report
Projects Awarded at \$10 Million or More

Contract ID: 080423
Contract Name: Bee Branch-North (S)
Funding Type: Federal & State
District: 5
County: Van Buren
Route: Hwy. 65

Prime Contractor: White River Materials, Inc.
Type of Work: Resurfacing
Contract Bid Amount: \$30,870,727.09
Current Contract Amount: \$30,943,614.08
Total Amount Paid: \$12,850,834.83
Amount Remaining: \$18,092,779.25 (Based on Current Contract Amount)
Percent Complete: 41.5% (Calculated from the Current Contract Amount)
Percent Time Used: 22.5% This is a calendar day contract.

Letting Date: November 15, 2017
Work Order Date: January 02, 2018
Original Estimated Completion Date: Late 2019
Current Estimated Completion Date: Late 2019

Description of Project:

The purpose of this project is to widen Hwy. 65 from three lanes to five lanes in Van Buren County.

Arkansas Department of Transportation
Summary Progress Report
Projects Awarded at \$10 Million or More

Contract ID: 061102
Contract Name: Hwy. 67 Interchange (N. of Cabot) (S)
Funding Type: Federal & Local
District: 6
County: Lonoke
Route: Hwy. 67

Prime Contractor: Manhattan Road & Bridge Co.
Type of Work: Major Widening
Contract Bid Amount: \$25,525,894.33
Current Contract Amount: \$27,189,637.48
Total Amount Paid: \$21,948,942.21
Amount Remaining: \$5,240,695.27 (Based on Current Contract Amount)
Percent Complete: 80.7% (Calculated from the Current Contract Amount)
Percent Time Used: 78.4% This is a calendar day contract.

Letting Date: December 07, 2016
Work Order Date: January 25, 2017
Original Estimated Completion Date: Late 2018
Current Estimated Completion Date: Late 2018

Description of Project:

The purpose of this project is to construct a new interchange at Hwy. 67/Hwy. 38 north of Cabot in Lonoke County.

*Arkansas Department of Transportation
Summary Progress Report
Projects Awarded at \$10 Million or More*

Contract ID: CA0605
Contract Name: Vandenberg Blvd. - Hwy. 5 (Widening) (S)
Funding Type: CAP & State
District: 6
County: Lonoke & Pulaski
Route: Hwy. 67

Prime Contractor: Weaver-Bailey Contrs., Inc.
Type of Work: Major Widening
Contract Bid Amount: \$79,264,377.02
Current Contract Amount: \$89,378,752.75
Total Amount Paid: \$55,687,100.60
Amount Remaining: \$33,691,652.15 (Based on Current Contract Amount)
Percent Complete: 62.7% (Calculated from the Current Contract Amount)
Percent Time Used: 168.0% This is a calendar day contract.

Letting Date: December 07, 2016
Work Order Date: March 20, 2017
Original Estimated Completion Date: Late 2018
Current Estimated Completion Date: Early 2019

Description of Project:

The purpose of this project is to widen 4.6 miles of Hwy. 67 from four lanes to six lanes between Jacksonville and Cabot in Lonoke and Pulaski Counties.

Arkansas Department of Transportation
Summary Progress Report
Projects Awarded at \$10 Million or More

Contract ID: 100759
Contract Name: Black River Str. & Apprs. (Pocahontas) (S)
Funding Type: Federal & State
District: 10
County: Randolph
Route: Hwy. 67

Prime Contractor: Jensen Construction Co.
Type of Work: Bridge And Approaches
Contract Bid Amount: \$10,139,227.11
Current Contract Amount: \$10,255,871.39
Total Amount Paid: \$9,359,644.47
Amount Remaining: \$896,226.92 (Based on Current Contract Amount)
Percent Complete: 91.3% (Calculated from the Current Contract Amount)
Percent Time Used: 87.0% This is a working day contract.

Letting Date: March 23, 2016
Work Order Date: May 13, 2016
Original Estimated Completion Date: Late 2018
Current Estimated Completion Date: Late 2018

Description of Project:

The purpose of this project is to replace the northbound bridge over the Black River on Hwy. 67 in Pocahontas, Randolph County.

Arkansas Department of Transportation
Summary Progress Report
Projects Awarded at \$10 Million or More

Contract ID: 110540
Contract Name: White River Strs. Demo. & Removal (Clarendon) (S)
Funding Type: Federal & State
District: 1
County: Monroe
Route: Hwy. 79

Prime Contractor: Century Construction Group, Inc.
Type of Work: Removal Of Structures
Contract Bid Amount: \$11,306,869.84
Current Contract Amount: \$11,306,869.84
Total Amount Paid: \$111,325.95
Amount Remaining: \$11,195,543.89 (Based on Current Contract Amount)
Percent Complete: 1.0% (Calculated from the Current Contract Amount)
Percent Time Used: 0.0% This is a working day contract.

Letting Date: January 17, 2018
Work Order Date: TBD
Original Estimated Completion Date: Late 2020
Current Estimated Completion Date: Late 2020

Description of Project:

The purpose of this project is to demolish two bridges and roadway embankment on Highway 79 in Clarendon, Monroe County.

Arkansas Department of Transportation
Summary Progress Report
Projects Awarded at \$10 Million or More

Contract ID: 020534
Contract Name: Co. Rd. 411 - Hwy. 425 (East of Crossett) (S)
Funding Type: Federal & State
District: 2
County: Ashley
Route: Hwy. 82

Prime Contractor: Johnsville Company, LLC
Type of Work: Major Widening
Contract Bid Amount: \$24,690,883.99
Current Contract Amount: \$25,608,488.33
Total Amount Paid: \$10,292,430.66
Amount Remaining: \$15,316,057.67 (Based on Current Contract Amount)
Percent Complete: 40.2% (Calculated from the Current Contract Amount)
Percent Time Used: 39.2% This is a working day contract.

Letting Date: November 02, 2016
Work Order Date: December 07, 2016
Original Estimated Completion Date: Early 2020
Current Estimated Completion Date: Early 2020

Description of Project:

The purpose of this project is to widen 5.3 miles of Hwy. 82 from two lanes to five lanes in Ashley County.

Arkansas Department of Transportation
Summary Progress Report
Projects Awarded at \$10 Million or More

Contract ID: CA0202
Contract Name: Hwy. 425 - Hamburg (Widening) (S)
Funding Type: CAP & State
District: 2
County: Ashley
Route: Hwy. 82

Prime Contractor: Jb James Construction, LLC
Type of Work: Major Widening
Contract Bid Amount: \$26,704,204.59
Current Contract Amount: \$26,704,204.59
Total Amount Paid: \$0.00
Amount Remaining: \$26,704,204.59 (Based on Current Contract Amount)
Percent Complete: 0.0% (Calculated from the Current Contract Amount)
Percent Time Used: 0.0% This is a calendar day contract.

Letting Date: September 12, 2018
Work Order Date: October 26, 2018
Original Estimated Completion Date: Early 2020
Current Estimated Completion Date: Early 2020

Description of Project:

The purpose of this project is to widen 5.4 miles of Hwy. 82 from two lanes to five lanes in Ashley County.

Arkansas Department of Transportation
Summary Progress Report
Projects Awarded at \$10 Million or More

Contract ID: 070365
Contract Name: Hwy. 79 No.-Co. Rd. 525 (Magnolia) (S)
Funding Type: Federal & State
District: 7
County: Columbia
Route: Hwy. 82

Prime Contractor: James Construction Group, LLC
Type of Work: Major Widening
Contract Bid Amount: \$22,175,162.47
Current Contract Amount: \$22,304,627.23
Total Amount Paid: \$14,301,670.56
Amount Remaining: \$8,002,956.67 (Based on Current Contract Amount)
Percent Complete: 64.1% (Calculated from the Current Contract Amount)
Percent Time Used: 75.0% This is a working day contract.

Letting Date: March 23, 2016
Work Order Date: May 04, 2016
Original Estimated Completion Date: Late 2018
Current Estimated Completion Date: Early 2019

Description of Project:

The purpose of this project is to widen 4.2 miles of Hwy. 82 from two lanes to five lanes in Magnolia, Columbia County.

Arkansas Department of Transportation
Summary Progress Report
Projects Awarded at \$10 Million or More

Contract ID: 070283
Contract Name: Bangs Slough-Hwy. 172 (S)
Funding Type: Federal & State
District: 7
County: Calhoun
Route: Hwy. 167

Prime Contractor: W.G. Yates & Sons Const. Co.
Type of Work: Major Widening
Contract Bid Amount: \$16,969,845.16
Current Contract Amount: \$17,120,273.60
Total Amount Paid: \$5,878,553.04
Amount Remaining: \$11,241,720.56 (Based on Current Contract Amount)
Percent Complete: 34.3% (Calculated from the Current Contract Amount)
Percent Time Used: 61.8% This is a working day contract.

Letting Date: June 22, 2016
Work Order Date: August 11, 2016
Original Estimated Completion Date: Late 2018
Current Estimated Completion Date: Mid 2019

Description of Project:

The purpose of this project is to widen 3.9 miles of Hwy. 167 from two lanes to five lanes in Calhoun County.

Arkansas Department of Transportation
Summary Progress Report
Projects Awarded at \$10 Million or More

Contract ID: CA0702
Contract Name: Hampton - Hwy. 274 (Widening) (S)
Funding Type: CAP, Federal, & State
District: 7
County: Calhoun
Route: Hwy. 167

Prime Contractor: McGeorge Contracting Co., Inc.
Type of Work: Major Widening
Contract Bid Amount: \$21,759,588.17
Current Contract Amount: \$23,085,193.71
Total Amount Paid: \$13,573,927.54
Amount Remaining: \$9,511,266.17 (Based on Current Contract Amount)
Percent Complete: 58.8% (Calculated from the Current Contract Amount)
Percent Time Used: 35.0% This is a calendar day contract.

Letting Date: July 19, 2017
Work Order Date: September 06, 2017
Original Estimated Completion Date: Late 2019
Current Estimated Completion Date: Late 2019

Description of Project:

The purpose of this project is to widen 4.27 miles of Hwy. 167 from two lanes to five lanes north of Hampton in Calhoun County.

Arkansas Department of Transportation
Summary Progress Report
Projects Awarded at \$10 Million or More

Contract ID: CA0703
Contract Name: Hwy. 274 - North (Widening) (S)
Funding Type: CAP, Federal, & State
District: 7
County: Calhoun
Route: Hwy. 167

Prime Contractor: D & J Construction Co., LLC
Type of Work: Major Widening
Contract Bid Amount: \$28,964,146.84
Current Contract Amount: \$28,982,347.16
Total Amount Paid: \$7,015,260.04
Amount Remaining: \$21,967,087.12 (Based on Current Contract Amount)
Percent Complete: 24.2% (Calculated from the Current Contract Amount)
Percent Time Used: 10.3% This is a calendar day contract.

Letting Date: February 21, 2018
Work Order Date: April 12, 2018
Original Estimated Completion Date: Mid 2020
Current Estimated Completion Date: Early 2020

Description of Project:

The purpose of this project is to widen 7.1 miles of Hwy. 167 from two lanes to five lanes in Calhoun County.

Arkansas Department of Transportation
Summary Progress Report
Projects Awarded at \$10 Million or More

Contract ID: 070280
Contract Name: El Dorado-Hwy. 335 (S)
Funding Type: Federal & State
District: 7
County: Union
Route: Hwy. 167

Prime Contractor: W.G. Yates & Sons Const. Co.
Type of Work: Major Widening
Contract Bid Amount: \$21,195,750.67
Current Contract Amount: \$21,469,586.62
Total Amount Paid: \$15,734,652.62
Amount Remaining: \$5,734,934.00 (Based on Current Contract Amount)
Percent Complete: 73.3% (Calculated from the Current Contract Amount)
Percent Time Used: 94.0% This is a working day contract.

Letting Date: October 13, 2015
Work Order Date: November 24, 2015
Original Estimated Completion Date: Mid 2018
Current Estimated Completion Date: Late 2018

Description of Project:

The purpose of this project is to widen 5.0 miles of Hwy. 167 from two lanes to five lanes in Union County.

Arkansas Department of Transportation
Summary Progress Report
Projects Awarded at \$10 Million or More

Contract ID: 070282
Contract Name: Ouachita River Str. & Apprs. (S)
Funding Type: Federal & State
District: 7
County: Calhoun & Union
Route: Hwy. 167

Prime Contractor: W.G. Yates & Sons Const. Co.
Type of Work: Bridge And Approaches
Contract Bid Amount: \$29,442,371.37
Current Contract Amount: \$29,689,365.45
Total Amount Paid: \$18,660,064.29
Amount Remaining: \$11,029,301.16 (Based on Current Contract Amount)
Percent Complete: 62.9% (Calculated from the Current Contract Amount)
Percent Time Used: 92.5% This is a working day contract.

Letting Date: November 05, 2014
Work Order Date: December 31, 2014
Original Estimated Completion Date: Late 2017
Current Estimated Completion Date: Late 2019

Description of Project:

The purpose of this project is to construct a new bridge over the Ouachita River on Hwy. 167 in Calhoun and Union Counties.

Arkansas Department of Transportation
Summary Progress Report
Projects Awarded at \$10 Million or More

Contract ID: 090373
Contract Name: Hwy. 264-Pleasant Grove Rd. (S)
Funding Type: Federal & State
District: 9
County: Benton
Route: Hwy. 265

Prime Contractor: Crossland Construction Co., Inc.
Type of Work: New Location
Contract Bid Amount: \$15,414,276.49
Current Contract Amount: \$16,308,212.19
Total Amount Paid: \$14,130,294.49
Amount Remaining: \$2,177,917.70 (Based on Current Contract Amount)
Percent Complete: 86.6% (Calculated from the Current Contract Amount)
Percent Time Used: 68.0% This is a working day contract.

Letting Date: December 01, 2015
Work Order Date: January 19, 2016
Original Estimated Completion Date: Late 2017
Current Estimated Completion Date: Late 2018

Description of Project:

The purpose of this project is to widen and construct Hwy. 265 along Old Wire Rd. and on new location for 4.0 miles in Benton County.

Arkansas Department of Transportation
Summary Progress Report
Projects Awarded at \$10 Million or More

Contract ID: 012007
Contract Name: Randall Wobbe Lane - Hwy. 264 (Springdale) (S)
Funding Type: Federal & State
District: 4 & 9
County: Benton & Washington
Route: Hwy. 265

Prime Contractor: Apac-Central, Inc.
Type of Work: New Location
Contract Bid Amount: \$10,243,391.73
Current Contract Amount: \$10,267,932.14
Total Amount Paid: \$4,775,148.56
Amount Remaining: \$5,492,783.58 (Based on Current Contract Amount)
Percent Complete: 46.5% (Calculated from the Current Contract Amount)
Percent Time Used: 34.1% This is a calendar day contract.

Letting Date: November 15, 2017
Work Order Date: January 02, 2018
Original Estimated Completion Date: Mid 2019
Current Estimated Completion Date: Early 2019

Description of Project:

The purpose of this project is to widen and relocate 1.9 miles of Hwy. 265 in Springdale in Benton and Washington Counties.

Arkansas Department of Transportation
Summary Progress Report
Projects Awarded at \$10 Million or More

Contract ID: 070368
Contract Name: Hwy. 82 - Hwy. 7 (Rehab.) (S)
Funding Type: Federal & State
District: 7
County: Union
Route: Hwy. 335

Prime Contractor: W.G. Yates & Sons Const. Co.
Type of Work: Rehabilitation
Contract Bid Amount: \$11,363,430.15
Current Contract Amount: \$11,367,615.35
Total Amount Paid: \$508,767.25
Amount Remaining: \$10,858,848.10 (Based on Current Contract Amount)
Percent Complete: 4.5% (Calculated from the Current Contract Amount)
Percent Time Used: 39.4% This is a working day contract.

Letting Date: November 02, 2016
Work Order Date: December 19, 2016
Original Estimated Completion Date: Mid 2018
Current Estimated Completion Date: Late 2019

Description of Project:

The purpose of this project is to rehabilitate 7.4 miles of Hwy. 335 in Union County.

Arkansas Department of Transportation
Summary Progress Report
Projects Awarded at \$10 Million or More

Contract ID: 005836
Contract Name: White River Str. & Apprs. (Newport) (S)
Funding Type: Federal & State
District: 5
County: Jackson
Route: Hwy. 367

Prime Contractor: Tanner Construction Co., Inc.
Type of Work: Bridge And Approaches
Contract Bid Amount: \$31,361,489.76
Current Contract Amount: \$32,018,867.90
Total Amount Paid: \$26,033,339.50
Amount Remaining: \$5,985,528.40 (Based on Current Contract Amount)
Percent Complete: 81.3% (Calculated from the Current Contract Amount)
Percent Time Used: 110.8% This is a working day contract.

Letting Date: October 30, 2013
Work Order Date: December 17, 2013
Original Estimated Completion Date: Late 2016
Current Estimated Completion Date: Late 2019

Description of Project:

The purpose of this project is to construct a new Hwy. 367 bridge over the White River in Newport in Jackson County.

*Arkansas Department of Transportation
Summary Progress Report
Projects Awarded at \$10 Million or More*

Contract ID: 100708
Contract Name: Hwy. 412 West-Hwy. 49 (S)
Funding Type: Federal & State
District: 10
County: Greene
Route: Hwy. 412

Prime Contractor: Dumey Contracting, Inc.
Type of Work: New Location
Contract Bid Amount: \$12,768,504.54
Current Contract Amount: \$13,585,824.12
Total Amount Paid: \$8,665,547.10
Amount Remaining: \$4,920,277.02 (Based on Current Contract Amount)
Percent Complete: 63.8% (Calculated from the Current Contract Amount)
Percent Time Used: 20.3% This is a working day contract.

Letting Date: January 18, 2017
Work Order Date: March 13, 2017
Original Estimated Completion Date: Late 2018
Current Estimated Completion Date: Late 2018

Description of Project:

The purpose of this project is to construct the western portion of the Paragould Bypass in Greene County.

Arkansas Department of Transportation
Summary Progress Report
Projects Awarded at \$10 Million or More

Contract ID: CA0201
Contract Name: Louisiana State Line - Hwy. 82 (Widening) (S)
Funding Type: CAP, Federal, & State
District: 2
County: Ashley
Route: Hwy. 425

Prime Contractor: Diamond B Const. Co., LLC
Type of Work: Major Widening
Contract Bid Amount: \$44,594,955.66
Current Contract Amount: \$44,594,955.66
Total Amount Paid: \$0.00
Amount Remaining: \$44,594,955.66 (Based on Current Contract Amount)
Percent Complete: 0.0% (Calculated from the Current Contract Amount)
Percent Time Used: 0.0% This is a calendar day contract.

Letting Date: September 12, 2018
Work Order Date: TBD
Original Estimated Completion Date: Early 2021
Current Estimated Completion Date: Early 2021

Description of Project:

The purpose of this project is to widen 10.0 miles of Hwy. 425 from two lanes to five lanes in Ashley County and Morehouse Parish, LA.

Arkansas Department of Transportation
Summary Progress Report
Projects Awarded at \$10 Million or More

Contract ID: 090508
Contract Name: Hwy. 71 - Co. Rd. 34 (Add'l Lns.) (B.V. Bypass) (S)
Funding Type: Federal & State
District: 9
County: Benton
Route: Hwy. 549

Prime Contractor: Kolb Grading, LLC
Type of Work: Additional Lanes
Contract Bid Amount: \$27,505,530.86
Current Contract Amount: \$27,562,397.91
Total Amount Paid: \$8,221,293.23
Amount Remaining: \$19,341,104.68 (Based on Current Contract Amount)
Percent Complete: 29.8% (Calculated from the Current Contract Amount)
Percent Time Used: 20.9% This is a working day contract.

Letting Date: November 15, 2017
Work Order Date: January 02, 2018
Original Estimated Completion Date: Late 2020
Current Estimated Completion Date: Late 2020

Description of Project:

The purpose of this project is to construct the additional lanes of 8.7 miles of the Bella Vista Bypass on Hwy. 549 in Benton County.



PROJECTS CHANGED FROM LAST QUARTER

Projects that were Let to Contract

Route	County	Job No	Job Name	Let Date	Cost (\$ in Millions)
I-30	Hempstead, Nevada & Clark	BB1101	Hwy. 299 - Gurdon Rest Area (S)	09/12/2018	39.0
I-49	Benton	BB0903	Hwy. 71B Intchn. Impvts. (S)	07/25/2018	26.9
Hwy. 5	Saline	061335	Alcoa Rd. - Hwy. 183 (S)	09/12/2018	17.4
Hwy. 82	Ashley	CA0202	Hwy. 425 - Hamburg (Widening) (S)	09/12/2018	26.7
Hwy. 425	Ashley	CA0201	Louisiana State Line - Hwy. 82 (Widening) (S)	09/12/2018	44.6

Projects that became Substantially Complete

Route	County	Job No	Job Name	Let Date	Cost(\$ in Million)	Sub Cmplt Date
I-40	St. Francis	BB0116	Shearerville - West (Pvmt. Impvts.) (F)	05/31/2017	29.7	07/26/2018
Hwy. 1	Lee & Phillips	110217	Walnut Corner-Cypress Corner (S)	01/13/2016	24.6	08/01/2018



PROJECTS SCHEDULED

As of September 30, 2018

PROJECTS SCHEDULED

SORTED BY ROUTE

Sorted by Route

Projects Scheduled

Route	County	Job No	Job Name	Year	Cost (\$ in Millions)
I-30	Pulaski	BB0619	65th St. - South Terminal (S)	2022	20-30
I-30	Saline	CA0601	Hwy. 70 - Sevier St. (Widening) (F)	2018	150-175
I-30 & I-40	Pulaski	CA0602	I-530 - Hwy. 67 (Widening & Reconst.) (I-30 & I-40) (F)	2019	>200
I-40	Crawford	BB0401	Oklahoma State Line - East (I-40 & I-540) (Sel. Secs.) (S)	2018	40-50
I-40, I-55 & Hwy. 77	Crittenden	110651	I-40/I-55/Hwy. 77 Intchn. Impvts. (F)	2020	15-20
I-49	Washington	BB0411	Hwy. 16/112 Spur Intchn. Impvts. (S)	2019	15-20
I-69	Various	020678	Hwy. 278 - Hwy. 65 (S)	2023	50-75
I-555	Craighead	100959	Hwy. 63B - Hwy. 18 (S)	2019	30-40
Hwy. 5	Baxter	090517	Izard Co. Line - Mountain Home (Safety Impvts.) (Sel. Secs.) (S)	2019	10-15
Hwy. 7	Garland	061547	Hwy. 7S - Hwy. 5 (S)	2019	10-15
Hwy. 10	Pulaski	061331	Pleasant Ridge Rd. - Pleasant Valley Dr. (L.R.) (F)	2019	30-40
Hwy. 18	Craighead	100824	BNSF Railroad Overpass (Hwy. 18) (Jonesboro) (S)	2018	20-30
Hwy. 18S & New	Craighead	100657	I-555 - Hwy. 49 (Commerce Dr. Extension) (Jonesboro) (Phase I) (S)	2020	30-40
Hwy. 23	Franklin	040726	Madison Co. Line - South (S)	2019	10-15
Hwy. 25	Lawrence	100974	Independence Co. Line - Black Rock (Safety Impvts.) (S)	2019	10-15
Hwy. 36	White	050280	Joy - Searcy (Safety Impvts.) (S)	2019	10-15
Hwy. 45	Sebastian	040713	Hwy. 71 - Hwy. 255 (Ft. Smith) (S)	2021	15-20
Hwy. 49	Greene	100632	Co. Rd. 845 - Hwy. 135 (Paragould) (S)	2019	15-20
Hwy. 65	Van Buren	CA0801	Hwy. 110 - Clinton (Widening) (S)	2019	30-40

Sorted by Route

Projects Scheduled

Route	County	Job No	Job Name	Year	Cost (\$ in Millions)
Hwy. 67	Lonoke	061371	Hwy. 67 Intchn. Impvts. (Cabot) (S)	2020	20-30
Hwy. 67	Lonoke	061549	Hwy. 5 - White Co. Line (S)	2019	50-75
Hwy. 67	Pulaski	CA0604	Main St. - Vandenberg Blvd. (Widening) (S)	2020	75-100
Hwy. 70	Monroe	110664	Prairie Co. Line - Hwy. 17 (S)	2020	20-30
Hwys. 70 & 278	Howard, Pike & Sevier	030501	Saline & Caddo Rivers Strs. & Apprs. (S)	2020	10-15
Hwy. 71	Sevier	030026	Cossatot River - De Queen (S)	2021	15-20
Hwy. 82	Columbia	CA0705	Co. Rd. 27 - Hwy. 79 (Widening) (S)	2019	20-30
Hwy. 82	Union	CA0706	Airport Dr. - Hwy. 82B (Widening) (S)	2019	20-30
Hwy. 82B	Union	070367	Hwy. 82B Improvements (El Dorado) (F)	2019	20-30
Hwy. 89	Faulkner	080457	UPRR Overpass & Realign. (Mayflower) (S)	2020	15-20
Hwy. 112	Benton & Washington	012270	Hwy. 112 Corridor Impvts. P.E.	2022	10-15
Hwy. 167	Calhoun	CA0704	Hwy. 79 - South (Widening) (S)	2019	20-30
Hwy. 255	Sebastian	040716	Hwy. 22 - Massard Creek (Widening & Reloc.) (Hwy. 255) (S)	2019	10-15
Hwy. 270	Garland	CA0607	Fleetwood Dr. - Hwy. 227 (Widening) (S)	2019	10-15
Hwys. 270 & 365S	Jefferson	020626	Hwy. 104 - Hwy. 365 (S)	2019	15-20
Hwy. 321	Lonoke	061509	Hwy. 367 - Hwy. 89 (Cabot) (S)	2019	15-20
Hwy. 412	Greene & Lawrence	CA1003	Hwy. 67 - Hwy. 141 (Widening) (S)	2019	50-75
Hwy. 549	Benton	CA0903	Hwy. 71 Interchange (B. V. Bypass) (S)	2020	50-75
Hwy. 549	Benton	CA0905	Co. Rd. 34 - Missouri State Line (B. V. Bypass) (S)	2020	30-40

Sorted by Route Projects Scheduled

Route	County	Job No	Job Name	Year	Cost (\$ in Millions)
NEW	Garland	R60016	East - West Arterial (Hot Springs) P.E.	2019	10-15

Disclaimer: Cost ranges are planning level estimates based on historical data for similar type projects. Amounts shown may change as design progresses.

PROJECTS SCHEDULED

SORTED BY COUNTY

Sorted by County

Projects Scheduled

County	Route	Job No	Job Name	Year	Cost (\$ in Millions)
Baxter	Hwy. 5	090517	Izard Co. Line - Mountain Home (Safety Impvts.) (Sel. Secs.) (S)	2019	10-15
Benton	Hwy. 549	CA0903	Hwy. 71 Interchange (B. V. Bypass) (S)	2020	50-75
Benton	Hwy. 549	CA0905	Co. Rd. 34 - Missouri State Line (B. V. Bypass) (S)	2020	30-40
Benton & Washington	Hwy. 112	012270	Hwy. 112 Corridor Impvts. P.E.	2022	10-15
Calhoun	Hwy. 167	CA0704	Hwy. 79 - South (Widening) (S)	2019	20-30
Columbia	Hwy. 82	CA0705	Co. Rd. 27 - Hwy. 79 (Widening) (S)	2019	20-30
Craighead	I-555	100959	Hwy. 63B - Hwy. 18 (S)	2019	30-40
Craighead	Hwy. 18	100824	BNSF Railroad Overpass (Hwy. 18) (Jonesboro) (S)	2018	20-30
Craighead	Hwy. 18S & New	100657	I-555 - Hwy. 49 (Commerce Dr. Extension) (Jonesboro) (Phase I) (S)	2020	30-40
Crawford	I-40	BB0401	Oklahoma State Line - East (I-40 & I-540) (Sel. Secs.) (S)	2018	40-50
Crittenden	I-40, I-55 & Hwy. 77	110651	I-40/I-55/Hwy. 77 Intchnng. Impvts. (F)	2020	15-20
Faulkner	Hwy. 89	080457	UPRR Overpass & Realign. (Mayflower) (S)	2020	15-20
Franklin	Hwy. 23	040726	Madison Co. Line - South (S)	2019	10-15
Garland	Hwy. 7	061547	Hwy. 7S - Hwy. 5 (S)	2019	10-15
Garland	Hwy. 270	CA0607	Fleetwood Dr. - Hwy. 227 (Widening) (S)	2019	10-15
Garland	NEW	R60016	East - West Arterial (Hot Springs) P.E.	2019	10-15
Greene	Hwy. 49	100632	Co. Rd. 845 - Hwy. 135 (Paragould) (S)	2019	15-20
Greene & Lawrence	Hwy. 412	CA1003	Hwy. 67 - Hwy. 141 (Widening) (S)	2019	50-75
Howard, Pike & Sevier	Hwys. 70 & 278	030501	Saline & Caddo Rivers Strs. & Apprs. (S)	2020	10-15

Sorted by County

Projects Scheduled

County	Route	Job No	Job Name	Year	Cost (\$ in Millions)
Jefferson	Hwys. 270 & 365S	020626	Hwy. 104 - Hwy. 365 (S)	2019	15-20
Lawrence	Hwy. 25	100974	Independence Co. Line - Black Rock (Safety Impvts.) (S)	2019	10-15
Lonoke	Hwy. 67	061371	Hwy. 67 Intchn. Impvts. (Cabot) (S)	2020	20-30
Lonoke	Hwy. 67	061549	Hwy. 5 - White Co. Line (S)	2019	50-75
Lonoke	Hwy. 321	061509	Hwy. 367 - Hwy. 89 (Cabot) (S)	2019	15-20
Monroe	Hwy. 70	110664	Prairie Co. Line - Hwy. 17 (S)	2020	20-30
Pulaski	I-30	BB0619	65th St. - South Terminal (S)	2022	20-30
Pulaski	I-30 & I-40	CA0602	I-530 - Hwy. 67 (Widening & Reconst.) (I-30 & I-40) (F)	2019	>200
Pulaski	Hwy. 10	061331	Pleasant Ridge Rd. - Pleasant Valley Dr. (L.R.) (F)	2019	30-40
Pulaski	Hwy. 67	CA0604	Main St. - Vandenberg Blvd. (Widening) (S)	2020	75-100
Saline	I-30	CA0601	Hwy. 70 - Sevier St. (Widening) (F)	2018	150-175
Sebastian	Hwy. 45	040713	Hwy. 71 - Hwy. 255 (Ft. Smith) (S)	2021	15-20
Sebastian	Hwy. 255	040716	Hwy. 22 - Massard Creek (Widening & Reloc.) (Hwy. 255) (S)	2019	10-15
Sevier	Hwy. 71	030026	Cossatot River - De Queen (S)	2021	15-20
Union	Hwy. 82	CA0706	Airport Dr. - Hwy. 82B (Widening) (S)	2019	20-30
Union	Hwy. 82B	070367	Hwy. 82B Improvements (El Dorado) (F)	2019	20-30
Van Buren	Hwy. 65	CA0801	Hwy. 110 - Clinton (Widening) (S)	2019	30-40
Various	I-69	020678	Hwy. 278 - Hwy. 65 (S)	2023	50-75
Washington	I-49	BB0411	Hwy. 16/112 Spur Intchn. Impvts. (S)	2019	15-20


Sorted by County

Projects Scheduled

County	Route	Job No	Job Name	Year	Cost (\$ in Millions)
White	Hwy. 36	050280	Joy - Searcy (Safety Impvts.) (S)	2019	10-15

Disclaimer: Cost ranges are planning level estimates based on historical data for similar type projects. Amounts shown may change as design progresses.


MAP OF PROJECTS

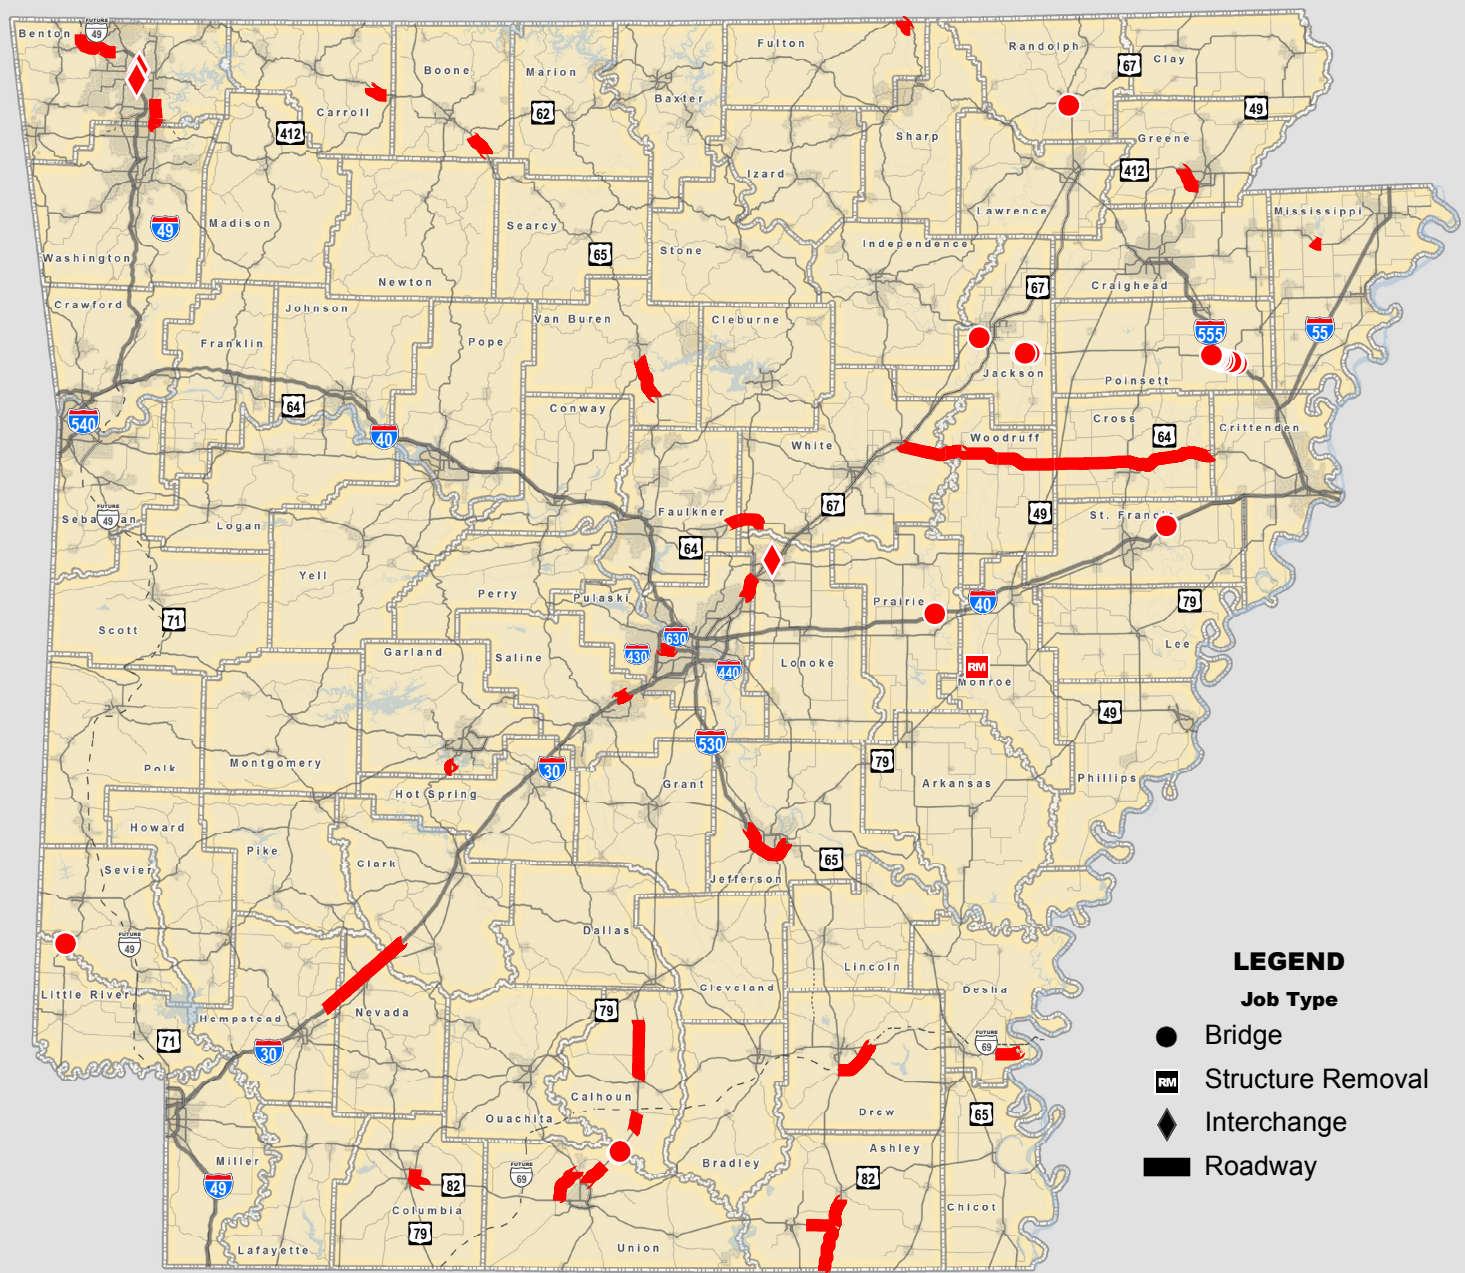

LEGEND

Job Type


- Bridge
- RM Structure Removal
- ◆ Interchange
- █ Roadway



PM: PS: CLD: 10/18/2018


Projects Awarded at \$10 Million or More Under Construction As Of September 30, 2018



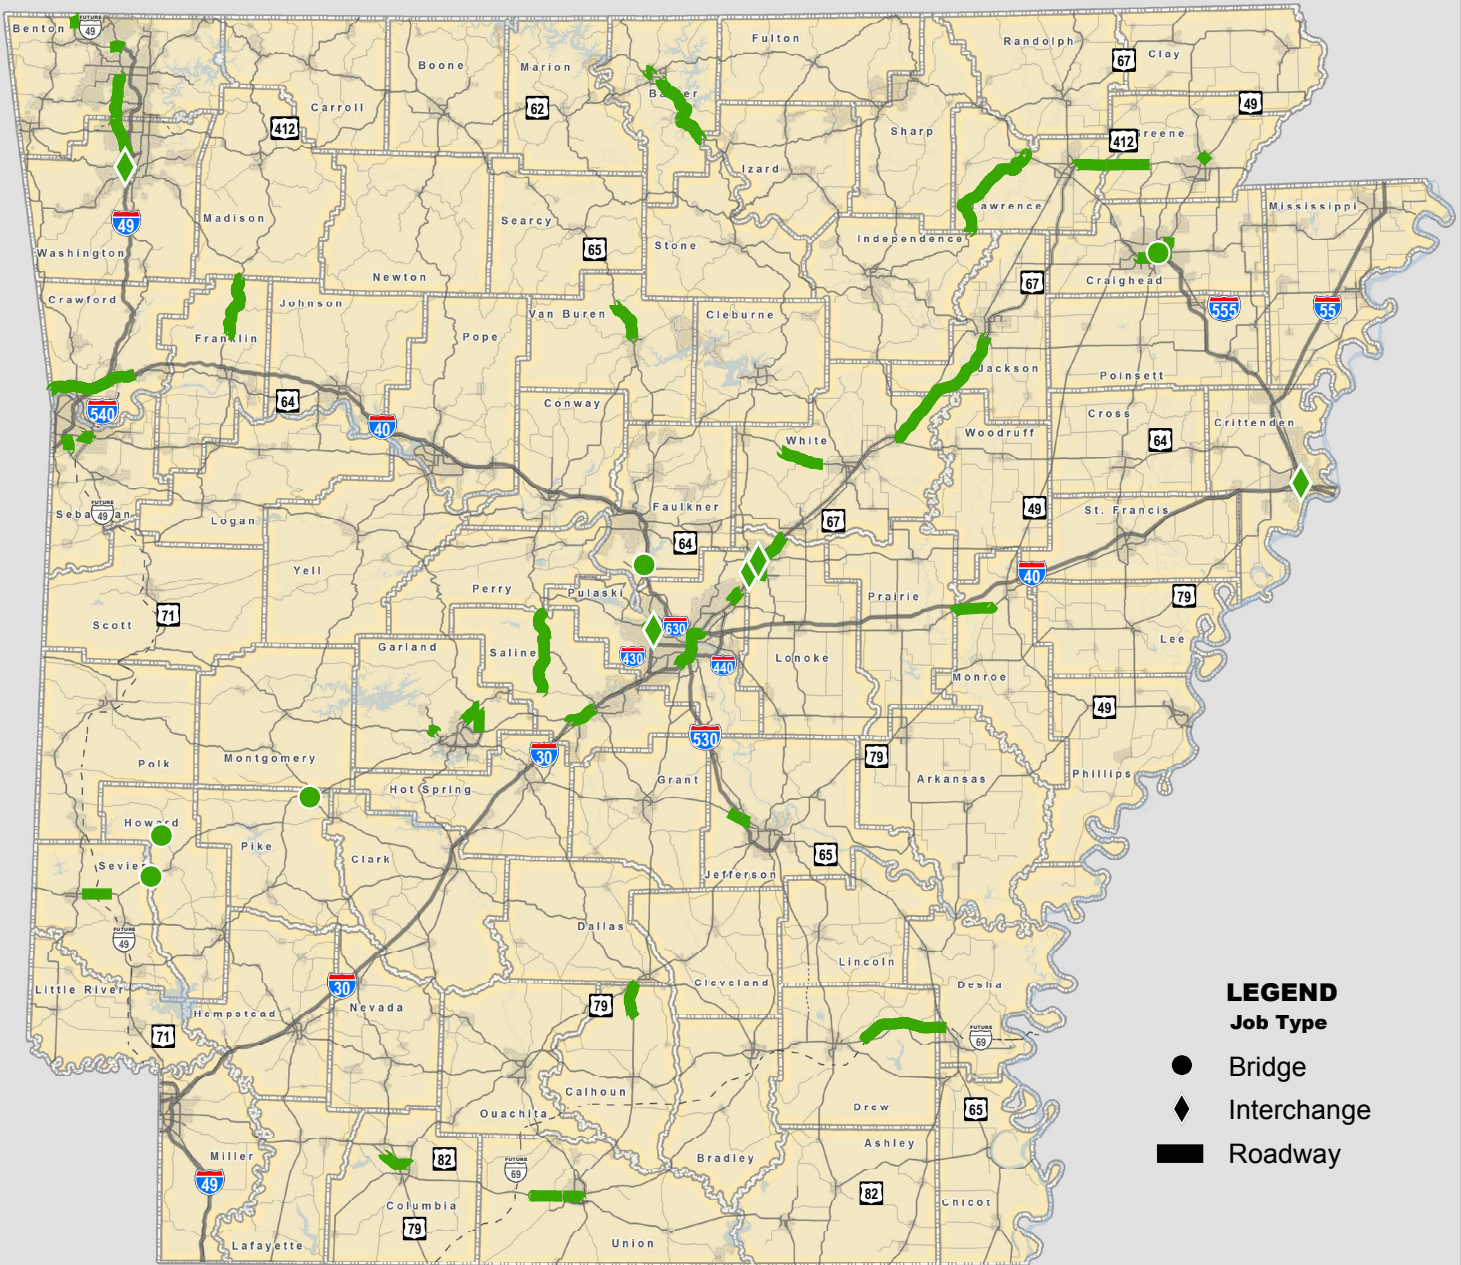

LEGEND
Job Type

- Bridge
- ◆ Interchange
- ▬ Roadway



Scheduled STIP Projects Estimated at \$10 Million or More
As Of September 30, 2018



Document Path: \\santitas\GIS\Programs\Connecticut\Projects\10_Million_Dollar Jobs\10_17_2018\STIP_Job_10_17_2018.mxd

APPENDIX


ARKANSAS HIGHWAY COMMISSION

NAME	PHONE	EMAIL
Dick Trammel - Chairman	(501) 569-2244	Dick.Trammel@ardot.gov
Thomas B. Schueck - Vice Chairman	(501) 569-2244	Tom.Schueck@ardot.gov
Robert S. Moore, Jr. - Member	(501) 569-2244	RobertSMooreJr@ardot.gov
Dalton A. Farmer, Jr. - Member	(501) 569-2244	Alec.Farmer@ardot.gov
Philip Taldo - Member	(501) 569-2244	Philip.Taldo@ardot.gov

ARDOT ADMINISTRATIVE CONTACTS

NAME	TITLE	PHONE	EMAIL
Scott E. Bennett, P.E.	Director	(501) 569-2211	Scott.Bennett@ardot.gov
Lorie Tudor	Deputy Director and Chief Operating Officer	(501) 569-2612	Lorie.Tudor@ardot.gov
Emanuel Banks	Deputy Director and Chief Engineer	(501) 569-2214	Emanuel.Banks@ardot.gov
Randy Ort	Assistant Chief Administration	(501) 569-4987	Randall.Ort@ardot.gov
Mike Fugett	Assistant Chief Engineer Design	(501) 569-2301	Michael.Fugett@ardot.gov
Tony Sullivan	Assistant Chief Engineer Operations	(501) 569-2221	Tony.Sullivan@ardot.gov
Kevin Thornton	Assistant Chief Engineer Planning	(501) 569-2241	Kevin.Thornton@ardot.gov
Ben Browning	Alternative Project Delivery Director	(501) 569-4984	Benjamin.Browning@ardot.gov
Keli Wylie	Connecting Arkansas Program Administrator	(501) 569-2247	Keli.Wylie@ardot.gov
Gill Rogers	Governmental Relations Officer	(501) 569-2108	Gill.Rogers@ardot.gov

ARDOT DISTRICT MAP & CONTACTS

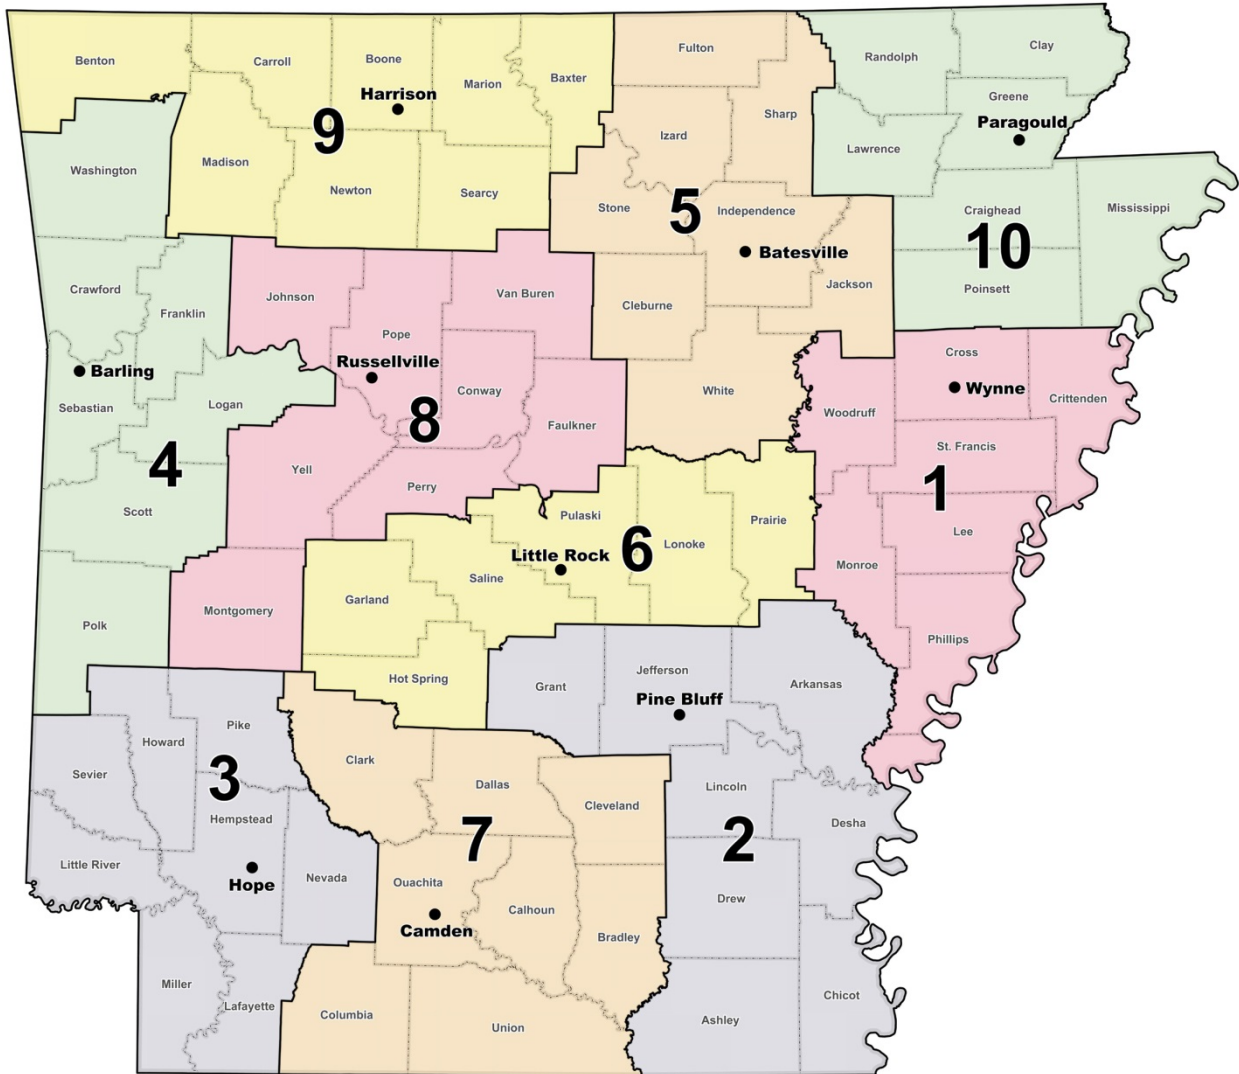

District	District Engineer	City	Email	Phone
District 1	Rex Vines	Wynne	Rex.Vines@ardot.gov	870-238-8144
District 2	Deric Wyatt	Pine Bluff	Deric.Wyatt@ardot.gov	870-534-1612
District 3	Stephen Frisbee	Hope	Steve.Frisbee@ardot.gov	870-777-3457
District 4	Chad Adams	Fort Smith	Chad.Adams@ardot.gov	479-484-5306
District 5	Bruce Street	Batesville	Bruce.Street@ardot.gov	870-251-2374
District 6	Mark Headley	Little Rock	Mark.Headley@ardot.gov	501-569-2266
District 7	David Archer	Camden	David.Archer@ardot.gov	870-836-6401
District 8	Scott Mullis	Russellville	John.Mullis@ardot.gov	479-968-2286
District 9	Steve Lawrence	Harrison	Steve.Lawrence@ardot.gov	870-743-2100
District 10	Brad Smithee	Paragould	Mark.Smithee@ardot.gov	870-239-9511

ACT 1

1 State of Arkansas
2 90th General Assembly
3 Third Extraordinary Session, 2016
4

Call Item 2

A Bill

HOUSE BILL 1009

5 By: Representatives Davis, Eaves, Brown, Della Rosa, J. Mayberry, Ballinger, Bell, Cozart, Dotson,
6 Eads, Eubanks, Henderson, House, Lemons, Speaks, Sullivan
7 By: Senator Hester
8

For An Act To Be Entitled

9
10 AN ACT TO CREATE THE ARKANSAS HIGHWAY IMPROVEMENT
11 PLAN OF 2016; TO DECLARE AN EMERGENCY; AND FOR OTHER
12 PURPOSES.
13

Subtitle

14
15
16 TO CREATE THE ARKANSAS HIGHWAY
17 IMPROVEMENT PLAN OF 2016; AND TO DECLARE
18 AN EMERGENCY.
19

20
21 BE IT ENACTED BY THE GENERAL ASSEMBLY OF THE STATE OF ARKANSAS:
22

23 SECTION 1. DO NOT CODIFY. This act shall be known and may be cited as
24 the "Arkansas Highway Improvement Plan of 2016".
25

26 SECTION 2. Arkansas Code § 10-3-309(b)(2)(B), concerning the
27 definition of "state agency", is amended to read as follows:

28 (B) "State agency" does not include the following unless
29 the Legislative Council adopts rules under subsection (h) of this section
30 ~~including~~ that include one (1) or more of the following in the definition of
31 "state agency":

32 (i) The Arkansas State Game and Fish Commission, if
33 the rule is not promulgated under authority of a statute enacted by the
34 General Assembly;

35 (ii) ~~The~~ Except as provided in §§ 10-3-3102 and 27-
36 65-107(a)(18)(A), the State Highway Commission and the Arkansas State Highway



1 and Transportation Department, if the rule is not promulgated under authority
2 of a statute enacted by the General Assembly; and

3 (iii) An institution of higher education.
4

5 SECTION 3. Arkansas Code Title 10, Chapter 3, is amended to add an
6 additional subchapter to read as follows:

7 Subchapter 31 – Highway Commission Review and Advisory Subcommittee of
8 the Legislative Council

9 10-3-3101. Creation.

10 (a) The Highway Commission Review and Advisory Subcommittee of the
11 Legislative Council is created.

12 (b)(1) The Highway Commission Review and Advisory Subcommittee of the
13 Legislative Council shall consist of twenty (20) members with at least four
14 (4) or more members of the General Assembly from each congressional district
15 of the state.

16 (2) The Legislative Council may through a suspension of its
17 rules, alter the membership of the Highway Commission Review and Advisory
18 Subcommittee of the Legislative Council.

19
20 10-3-3102. Duties.

21 (a) The Highway Commission Review and Advisory Subcommittee of the
22 Legislative Council shall review:

23 (1)(A) Proposed rules of the State Highway Commission required
24 under § 27-65-107(a)(18)(A).

25 (B)(i) Subdivision (a)(1)(A) of this section is limited to
26 rule review only.

27 (ii) Rules promulgated by the State Highway
28 Commission are not subject to approval by the Highway Commission Review and
29 Advisory Subcommittee of the Legislative Council, the Legislative Council, or
30 the Administrative Rules and Regulations Subcommittee of the Legislative
31 Council under this section or § 10-3-309; and

32 (2) Other State Highway Commission matters the Highway
33 Commission Review and Advisory Subcommittee of the Legislative Council
34 considers necessary to perform its duties under this section.

35 (b) The Highway Commission Review and Advisory Subcommittee of the
36 Legislative Council shall perform such other duties as may be assigned to it

1 by the Legislative Council.

2
3 (c) As a subcommittee of the Legislative Council, actions of the
4 Highway Commission Review and Advisory Subcommittee shall be reported to the
5 Legislative Council for final consideration and adoption.

6
7 SECTION 4. Arkansas Code § 19-3-521(a)(2)(B), concerning the
8 Securities Reserve Fund, is amended to read as follows:

9 (B) However, moneys in the Securities Reserve Fund in
10 excess of one hundred thousand dollars (\$100,000) shall be available at all
11 times to the Chief Fiscal Officer of the State ~~for transfer to the Budget~~
12 ~~Stabilization Trust Fund~~ as authorized by § 19-5-905, there to be used as
13 provided by law.

14
15 SECTION 5. Arkansas Code Title 19, Chapter 5, Subchapter 2 is amended
16 to add a new section to read as follows:

17 19-5-207. Certain sales and use taxes not subject to deduction,
18 transfer, or distribution.

19 The sales and use taxes levied under Arkansas Constitution, Amendment
20 91, § 3, are not subject to deduction, transfer, or distribution to the
21 Constitutional Officers Fund or the State Central Services Fund under §§ 19-
22 5-202, 19-5-203, and 19-5-205.

23
24 SECTION 6. Arkansas Code § 19-5-406 is amended to read as follows:
25 19-5-406. Transfer of remaining revenue.

26 After making the maximum annual allocation, as provided for in § 19-5-
27 402: ~~, all remaining general revenues available for distribution during each~~
28 ~~fiscal year shall be transferred on the last day of business in each calendar~~
29 ~~month to the General Revenue Allotment Reserve Fund, there to be used for the~~
30 ~~respective purposes as provided by law.~~

31 (1) Seventy-five percent (75%) of the remaining general revenues
32 available for distribution during each fiscal year shall be transferred on
33 the last day of business in each calendar month to the General Revenue
34 Allotment Reserve Fund, there to be used for the respective purposes as
35 provided by law; and

36 (2) Twenty-five percent (25%) of the remaining general revenues

1 available for distribution during each fiscal year shall be transferred on
 2 the last day of business in each calendar month to the Arkansas Highway
 3 Transfer Fund.

4
 5 SECTION 7. Arkansas Code § 19-5-501(a)(2), concerning the Budget
 6 Stabilization Trust Fund, is amended to read as follows:

7 (2) The Budget Stabilization Trust Fund shall consist of funds
 8 made available and transferred to it from the Securities Reserve Fund as set
 9 out in § 19-5-905 ~~and this section~~, the fund balance and other assets
 10 remaining in the State Budget Revolving Fund on June 30, 1987, and any other
 11 funds made available by law. ~~The Treasurer of State, after complying with §~~
 12 ~~27-70-204 for distributing interest income earned from investment of average~~
 13 ~~daily balances of the State Highway and Transportation Department Fund; § 15-~~
 14 ~~41-110 for distributing interest earned from investment of average daily~~
 15 ~~balances of the Game Protection Fund; and any other laws enacted by the~~
 16 ~~General Assembly for disposition of interest income earned from investment of~~
 17 ~~average daily State Treasury balances, shall credit to the Budget~~
 18 ~~Stabilization Trust Fund fifty percent (50%) of the interest income received~~
 19 ~~and credited to the Securities Reserve Fund and credit to the General~~
 20 ~~Improvement Fund fifty percent (50%) of the interest income received and~~
 21 ~~credited to the Securities Reserve Fund as certified by the Chief Fiscal~~
 22 ~~Officer of the State.~~

23
 24 SECTION 8. Arkansas Code § 19-5-905 is amended to read as follows:
 25 19-5-905. Securities Reserve Fund.

26 (a) There is established on the books of the Treasurer of State, the
 27 Auditor of State, and the Chief Fiscal Officer of the State a trust fund to
 28 be known as the "Securities Reserve Fund". ~~This fund~~ The Securities Reserve
 29 Fund shall consist of moneys derived from savings effected in the retirement
 30 in advance of maturity of nonhighway direct general obligation bonds of the
 31 state, of discounts received in the purchase of securities, and of premiums
 32 and interest derived from the sale of securities held in the Securities
 33 Account by the Treasurer of State as custodian. ~~It shall be used for~~ The
 34 Securities Reserve Fund shall be used as follows:

35 (1) ~~Paying~~ To pay premiums and the purchase and absorbing of
 36 discounts in the sale of securities held in the Securities Account, not to

1 exceed five hundred thousand dollars (\$500,000) in any one (1) fiscal year;

2 (2) ~~Guaranteeing~~ To guarantee bonds in an aggregate principal
3 amount not to exceed five million dollars (\$5,000,000) outstanding at any
4 time, with no bond bearing interest at a rate exceeding eight percent (8%)
5 per annum, of the Museum and Cultural Commission Fund authorized, and in the
6 manner prescribed in the Arkansas Museum and Cultural Center Act, ~~by~~ § 13-5-
7 301 et seq., not to exceed five hundred thousand dollars (\$500,000) in any
8 one (1) fiscal year;

9 (3) ~~Guaranteeing~~ To guarantee bonds of any other park or
10 recreation facility approved by the Governor and the Department of Parks and
11 Tourism, not to exceed five hundred thousand dollars (\$500,000) in the
12 aggregate, after seeking advice of the Legislative Council and the
13 Legislative Joint Auditing Committee;

14 (4) ~~Guaranteeing~~ To guarantee industrial development bonds as
15 authorized by §§ 15-4-702 – 15-4-710;

16 (5) ~~Absorbing~~ To absorb losses incurred in the investing of
17 securities held in the Securities Account in the State Treasury and in bank
18 depositories. The balance of ~~this fund~~ the Securities Reserve Fund shall
19 always be available for this purpose; ~~and~~

20 (6) ~~Guaranteeing~~ To guarantee to students to attend truck
21 driving school at the Arkansas Commercial Driver Training Institute at
22 Arkansas State University-Newport, in an aggregate principal amount not to
23 exceed four hundred thousand dollars (\$400,000) outstanding at any one (1)
24 time;

25 (7) To distribute:

26 (A) Interest income earned on investment of average daily
27 balances of the following:

28 (i) The State Highway and Transportation Department
29 Fund, as authorized by § 27-70-204;

30 (ii) The Game Protection Fund, as authorized by §
31 15-41-110;

32 (iii) The funds deposited into the State Treasury by
33 state agencies, boards, and commissions that were previously held as cash
34 funds in a bank depository or investment depository, as authorized by § 19-3-
35 518(d); and

36 (iv) State and Local Fiscal Assistance Act of 1972,

1 31 U.S.C. § 6701 et seq., as authorized by § 19-3-521(c);

2 (B) Interest income earned from investment of average
 3 daily State Treasury balances by any other laws enacted by the General
 4 Assembly;

5 (8) After the distributions enumerated in subdivision (a)(7) of
 6 this section, for a one-time transfer by the Chief Fiscal Officer of the
 7 State, one million five hundred thousand dollars (\$1,500,000) to the Arkansas
 8 Highway Transfer Fund, to be transferred only in Fiscal Year 2017;

9 (9) After the distributions enumerated in subdivisions (a)(7)
 10 and (8) of this section, for a transfer by the Chief Fiscal Officer of the
 11 State of five million dollars (\$5,000,000) each fiscal year to the Budget
 12 Stabilization Trust Fund;

13 (10) After the transfer to the Budget Stabilization Trust Fund
 14 enumerated in subdivision (a)(9) of this section, for a transfer by the Chief
 15 Fiscal Officer of the State of twenty million dollars (\$20,000,000) beginning
 16 in Fiscal Year 2018 and each fiscal year thereafter to the Arkansas Highway
 17 Transfer Fund;

18 (11) For a transfer by the Chief Fiscal Officer on the last
 19 business day of the fiscal year to the Budget Stabilization Trust Fund to
 20 reimburse the Budget Stabilization Trust Fund for any current fiscal year
 21 transfers that have been made to the following:

22 (A) The Department of Correction Farm Fund under § 19-5-
 23 501(b)(1);

24 (B) The State Military Department Fund under § 19-5-
 25 501(b)(3);

26 (C) The Disaster Assistance Fund under § 19-5-1006;

27 (D) The Miscellaneous Revolving Fund under § 19-5-1009;

28 (E) The State Central Services Fund under § 19-5-501(d);

29 and

30 (F) The State Board of Election Commissioners, as
 31 authorized by law; and

32 (12) After all distributions and transfers under this section,
 33 less one hundred thousand dollars (\$100,000) under § 19-3-521(a)(2), for a
 34 transfer by the Chief Fiscal Officer of the State on the last business day of
 35 the fiscal year of the fund balance to the Long Term Reserve Fund.

36 ~~(b) Moneys in this fund in excess of one hundred thousand dollars~~

1 ~~(\$100,000) shall, at all times, be available to the Chief Fiscal Officer of~~
 2 ~~the State for transfer to the Budget Stabilization Trust Fund, there to be~~
 3 ~~used as provided by law.~~

4 ~~(c)(b) In the event any loss~~ If any loss is shall be sustained in
 5 relation to securities at any time held in the Securities Account or in any
 6 bank depository and ~~in the event~~ if the credit balance in the Securities
 7 Reserve Fund ~~shall be~~ is insufficient to absorb ~~such~~ the loss, the Chief
 8 Fiscal Officer of the State shall cause a transfer of moneys to be made from
 9 the Budget Stabilization Trust Fund to the Securities Reserve Fund in such
 10 amount as shall, when added to the credit balance in the Securities Reserve
 11 Fund, equal the amount of ~~such~~ the loss. It is the intent of the General
 12 Assembly that no loss shall be sustained by any account the funds of which
 13 were used in making such investments and deposits.

14
 15 SECTION 9. Arkansas Code § 19-5-1103(b), concerning the Property Tax
 16 Relief Trust Fund, is amended to read as follows:

17 (b) The fund shall consist of such revenues as generated by §§ 26-52-
 18 302(c), 26-52-317(c)(1)(B), 26-52-319(a)(2)(B), 26-53-107(c), 26-53-
 19 145(c)(1)(B), 26-53-148(a)(2)(B), ~~26-56-201(g)(1)(C)~~, and 26-56-224(c)(2) and
 20 shall be used for such purposes as set out in § 26-26-310.

21
 22 SECTION 10. Arkansas Code § 19-5-1227(b)(3), concerning the
 23 Educational Adequacy Fund, is amended to read as follows:

24 (3) The revenues generated by §§ 26-52-302(d), 26-52-316, 26-52-
 25 317(c)(1)(C), 26-52-319(a)(2)(C), 26-53-107(d), 26-53-145(c)(1)(C), 26-53-
 26 148(a)(2)(C), ~~26-56-201(g)(1)(B)~~, 26-56-224(c)(3), and 26-57-
 27 1002(d)(1)(A)(ii); and

28
 29 SECTION 11. Arkansas Code § 19-6-201(68), concerning the enumeration
 30 of general revenues, is repealed.

31 ~~(68) The first four million dollars (\$4,000,000) of the eight and~~
 32 ~~one half cent (8½¢) tax on distillate special fuels levied each fiscal year~~
 33 ~~under § 26-56-201(a)(1)(A)(i);~~

34
 35 SECTION 12. Arkansas Code § 19-6-301(3)(A), concerning the enumeration
 36 of special revenues, is amended to read as follows:

1 (A) Eight and one-half cent (8.5¢) tax on distillate
2 special motor fuels levied by § 26-56-201(a)(1)(A)(i), ~~after the deduction of~~
3 ~~the first four million dollars (\$4,000,000) each fiscal year under § 26-56-~~
4 ~~201(g)(1)~~ and the one cent (1¢) tax on distillate special motor fuels levied
5 by § 26-56-201(a)(1)(A)(ii);
6

7 SECTION 13. Arkansas Code Title 19, Chapter 6, Subchapter 8, is
8 amended to add an additional section to read as follows:

9 19-6-832. Arkansas Highway Transfer Fund.

10 (a) There is created on the books of the Treasurer of the State, the
11 Auditor of State, and the Chief Fiscal Officer of the State a special revenue
12 fund to be known as the “Arkansas Highway Transfer Fund”.

13 (b) The Arkansas Highway Transfer Fund shall be used to provide
14 additional funding to the Arkansas State Highway and Transportation
15 Department for use in constructing and maintaining the highways of this
16 state.

17 (c) In the event revenues to the department are insufficient to fully
18 address the highway construction and maintenance needs of the state, the
19 department may provide a written document to the Governor outlining the
20 reasons that additional funding is needed and requesting that the Governor
21 provide a recommendation to the Legislative Council or the Joint Budget
22 Committee for review and approval of the transfer of funds in the Arkansas
23 Highway Transfer Fund to the State Highway and Transportation Department
24 Fund.

25 (d) Upon review and approval of the Legislative Council or the Joint
26 Budget Committee, the Chief Fiscal Officer of the State may transfer funds
27 from the Arkansas Highway Transfer Fund to the State Highway and
28 Transportation Department Fund as deemed necessary to provide additional
29 funding to address the highway construction and maintenance needs of the
30 state.

31 (e) The requirement of approval by the Legislative Council or Joint
32 Budget Committee is not a severable part of this section. If the requirement
33 of approval by the Legislative Council or Joint Budget Committee is ruled
34 unconstitutional by a court of competent jurisdiction, this entire section is
35 void.
36

1 SECTION 14. The introductory language of Arkansas Code § 19-6-484,
 2 concerning the Conservation Tax Fund, is amended to read as follows:

3 The Conservation Tax Fund shall consist of those ~~general revenues as~~
 4 ~~specified in § 26-56-201(g)(1)(D) and those~~ special revenues as specified in
 5 § 19-6-301(193) there to be distributed to the fund accounts as set out
 6 below, which are created by this section unless specifically created in other
 7 provisions of the Arkansas Code, and under the following procedures:

8
 9 SECTION 15. Arkansas Code § 19-6-486 is amended to read as follows:

10 19-6-486. ~~Arkansas Rainy Day Fund.~~ Long Term Reserve Fund.

11 (a) There is created on the books of the Treasurer of State, the
 12 Auditor of State, and the Chief Fiscal Officer of the State a special revenue
 13 fund to be known as the ~~“Arkansas Rainy Day Fund”~~ “Long Term Reserve Fund”.

14 (b) The fund shall consist of such funds as may be provided by the
 15 General Assembly.

16 (c) The fund shall be used to distribute moneys to one (1) or more
 17 funds or fund accounts in the Revenue Stabilization Law of Arkansas, § 19-5-
 18 101 et seq.

19 (d)(1) After determining the estimated amount of general revenue that
 20 will be available for allocation to the state agencies under the Revenue
 21 Stabilization Law, § 19-5-101 et seq., and after making the determination
 22 required by § 19-5-1227(c) and prior to making any transfers deemed necessary
 23 by the Chief Fiscal Officer of the State in § 19-5-1227(d), the Chief Fiscal
 24 Officer of the State may transfer funds from the ~~Arkansas Rainy Day Fund~~ Long
 25 Term Reserve Fund in the event a “revenue shortfall” exists to meet the
 26 state’s financial obligation to provide an adequate educational system for
 27 the state and to provide for the effective operation of state government. In
 28 the event the Chief Fiscal Officer of the State determines that a “revenue
 29 shortfall” exists as defined as a circumstance when the official forecast of
 30 gross general revenue certified by the Chief Fiscal Officer of the State is
 31 projected to increase less than three percent (3%) over and above the gross
 32 general revenue collections of the previous fiscal year due to changes in
 33 economic conditions, he or she may then transfer funds from the ~~Arkansas~~
 34 ~~Rainy Day Fund~~ Long Term Reserve Fund, as approved by the Legislative Council
 35 or Joint Budget Committee, to various funds and fund accounts, as deemed
 36 necessary, in the Revenue Stabilization Law for the purpose of meeting

1 unanticipated shortfalls in state general revenue.

2 (2) Or the Chief Fiscal Officer of the State may transfer funds
3 from the ~~Arkansas Rainy Day Fund~~ Long Term Reserve Fund to the Economic
4 Development Superprojects Project Fund for projects authorized under Arkansas
5 Constitution, Amendment 82, as approved by the Governor and the Legislative
6 Council or Joint Budget Committee.

7 (3) Determining the maximum amount of appropriation and general
8 revenue funding for a state agency each fiscal year is the prerogative of the
9 General Assembly. This is usually accomplished by delineating such maximums
10 in the appropriation acts for a state agency and the general revenue
11 allocations authorized for each fund and fund account by amendment to the
12 Revenue Stabilization Law. Further, the General Assembly has determined that
13 creating the ~~Arkansas Rainy Day Fund~~ Long Term Reserve Fund and establishing
14 the procedures for the transfer of funds to various fund and fund accounts in
15 the Revenue Stabilization Law or to the Economic Development Superprojects
16 Project Fund, or both, provides for the efficient and effective operation of
17 state government if a revenue shortfall is determined to exist. Therefore, it
18 is both necessary and appropriate that the General Assembly maintain
19 oversight by requiring prior approval of the Legislative Council or Joint
20 Budget Committee as provided by this section. The requirement of approval by
21 the Legislative Council or Joint Budget Committee is not a severable part of
22 this section. If the requirement of approval by the Legislative Council or
23 Joint Budget Committee is ruled unconstitutional by a court of competent
24 jurisdiction, this entire section is void.

25 (e)(1) Upon recommendation by the Chief Fiscal Officer of the State,
26 the Governor may determine that circumstances exist that meet the
27 requirements for the utilization of the ~~Arkansas Rainy Day Fund~~ Long Term
28 Reserve Fund as set out in this section and the procedures set out herein
29 shall apply.

30 (2) When the Governor determines there is a need requiring
31 transfer from the ~~Arkansas Rainy Day Fund~~ Long Term Reserve Fund, he or she
32 shall instruct the Chief Fiscal Officer of the State to prepare and submit
33 written documentation to the Legislative Council or the Joint Budget
34 Committee. Such documentation shall include:

35 (A) Sufficient financial data that will enable the
36 verification of the existence of an emergency and the amount necessary to

1 address the need for ~~rainy day funds~~ long term reserve funds;

2 (B) A proposed distribution of moneys from the ~~Arkansas~~
3 ~~Rainy Day Fund~~ Long Term Reserve Fund to one or more funds or fund accounts
4 in the Revenue Stabilization Law, or to the Economic Development
5 Superprojects Project Fund, or both; and

6 (C) A statement certifying that no other funds are
7 available that could be transferred in lieu of the funds in the ~~Arkansas~~
8 ~~Rainy Day Fund~~ Long Term Reserve Fund.

9 (3) Such documentation shall be submitted to the Legislative
10 Council or Joint Budget Committee for approval prior to the implementation of
11 the proposed distribution. The Chief Fiscal Officer of the State, after
12 having sought and received prior approval of the Legislative Council or Joint
13 Budget Committee, shall cause the required transfers to be made on his or her
14 books and on the books of the Treasurer of State and the Auditor of State
15 from the ~~Arkansas Rainy Day Fund~~ Long Term Reserve Fund to the appropriate
16 funds and fund accounts in the Revenue Stabilization Law or to the Economic
17 Development Superprojects Project Fund, or both. In no event shall the
18 amounts transferred in any fiscal year to the funds and fund accounts in the
19 Revenue Stabilization Law by this section cause the general revenues to
20 exceed the maximum allocations authorized in the Revenue Stabilization Law.

21 (4) Determining the maximum amount of appropriation and general
22 revenue funding for a state agency each fiscal year is the prerogative of the
23 General Assembly. This is usually accomplished by delineating such maximums
24 in the appropriation acts for a state agency and the general revenue
25 allocations authorized for each fund and fund account by amendment to the
26 Revenue Stabilization Law. Further, the General Assembly has determined that
27 creating the ~~Arkansas Rainy Day Fund~~ Long Term Reserve Fund and establishing
28 the procedures for the transfer of funds to various funds and fund accounts
29 in the Revenue Stabilization Law or to the Economic Development Superprojects
30 Project Fund, or both, provides for the efficient and effective operation of
31 state government if a revenue shortfall is determined to exist. Therefore, it
32 is both necessary and appropriate that the General Assembly maintain
33 oversight by requiring prior approval of the Legislative Council or Joint
34 Budget Committee as provided by this section. The requirement of approval by
35 the Legislative Council or Joint Budget Committee is not a severable part of
36 this section. If the requirement of approval by the Legislative Council or

1 Joint Budget Committee is ruled unconstitutional by a court of competent
2 jurisdiction, this entire section is void.

3 (f) During each fiscal year, after the provisions of § 19-5-1004(b)(2)
4 are complied with, the Chief Fiscal Officer of the State may replenish the
5 ~~Arkansas Rainy Day Fund~~ Long Term Reserve Fund by transferring no more than
6 fifty percent (50%) of the balance in the General Revenue Allotment Reserve
7 Fund or an amount equal to all transfers made under this section during the
8 fiscal year immediately preceding the fiscal year in which such replenishment
9 is made under this section, whichever is less, to the ~~Arkansas Rainy Day Fund~~
10 Long Term Reserve Fund. In no event shall the balance of the ~~Arkansas Rainy~~
11 ~~Day Fund~~ Long Term Reserve Fund exceed one hundred twenty five million
12 dollars (\$125,000,000) at any time.

13
14 SECTION 16. Arkansas Code § 26-56-201(f), concerning the imposition
15 and distribution of distillate special fuels tax, is amended to read as
16 follows:

17 (f) ~~Except as provided in subsection (g) of this section, the~~ The
18 additional taxes collected under this section are special revenues and shall
19 be distributed as set forth in the Arkansas Highway Revenue Distribution Law,
20 § 27-70-201 et seq., subject to any requirements for the repayment of bonds
21 issued under the Arkansas Highway Financing Act of 1999, § 27-64-201 et seq.,
22 the Arkansas Interstate Highway Financing Act of 2007, § 27-64-401 et seq.,
23 and the Arkansas Highway Financing Act of 2011, § 27-64-501 et seq.

24
25 SECTION 17. Arkansas Code § 26-56-201(g), concerning the imposition
26 and distribution of distillate special fuels tax, is amended to read as
27 follows:

28 (g)(1) ~~In order to offset the general revenues lost by the tax~~
29 ~~exemption contained in § 26-52-436(c) and (d) and § 26-53-144(c) and (d), the~~
30 ~~Chief Fiscal Officer of the State shall, on or before June 30, 2013, and on~~
31 ~~or before June 30 of each fiscal year thereafter, deposit the first four~~
32 ~~million dollars (\$4,000,000) of the taxes collected under subdivision~~
33 ~~(a)(1)(A)(i) of this section as general revenues, to be distributed as~~
34 ~~follows:~~

35 (A) ~~Seventy five percent (75%) to be deposited into the~~
36 ~~General Revenue Fund Account of the State Apportionment Fund;~~

1 ~~(B) Fourteen and six tenths percent (14.6%) to be~~
 2 ~~deposited into the Educational Adequacy Fund;~~

3 ~~(C) Eight and three tenths percent (8.3%) to be deposited~~
 4 ~~into the Property Tax Relief Trust Fund; and~~

5 ~~(D) Two and one tenth percent (2.1%) to be deposited into~~
 6 ~~the Conservation Tax Fund.~~

7 ~~(2) The balance of the taxes collected under subdivision~~
 8 ~~(a)(1)(A)(i) of this section shall be deposited as special revenues and~~
 9 ~~distributed in the manner required by law.~~

10 ~~(3) The classification and distribution of taxes under~~
 11 ~~subdivision (g)(1) of this section is subject to any requirements for the~~
 12 ~~repayment of bonds issued under the~~
 13 ~~Arkansas Highway Financing Act of 1999, § 27-64-201 et seq., and the Arkansas~~
 14 ~~Interstate Highway Financing Act of 2007, § 27-64-401 et seq.~~

15 ~~(4) The taxes collected under subdivision (a)(1)(A)(ii) of this~~
 16 ~~section shall be distributed as provided in § 26-56-221.~~

17
 18 SECTION 18. Arkansas Code § 27-70-206(1) concerning distribution of
 19 highway revenue to state funds, is amended to read as follows:

20 (1) First, except as provided by § 19-5-207, three percent (3%)
 21 of the amount thereof to the Constitutional Officers Fund and the State
 22 Central Services Fund, there to be used for the purposes specified for ~~the~~
 23 each fund by the Revenue Stabilization Law, § 19-5-101 et seq.;

24
 25 SECTION 19. Arkansas Code § 27-65-107(a), concerning the powers and
 26 duties of the State Highway Commission, is amended to add additional
 27 subdivisions to read as follows:

28 (18)(A) To propose and submit rules regarding the:

29 (i) Criteria for distribution of funds and the
 30 distribution of funds from the:

31 (a) State Highway and Transportation
 32 Department Fund; and

33 (b) Road and Bridge Repair, Maintenance, and
 34 Grants Fund; and

35 (ii) Spending priority designated for highway
 36 construction contracts and public road construction projects by the Arkansas

1 State Highway and Transportation Department and the commission, including the
 2 criteria used to establish the spending priority.

3 (B)(i) The commission shall submit the proposed rules
 4 required under subdivision (a)(18)(A) of this section to the Highway
 5 Commission Review and Advisory Subcommittee of the Legislative Council for
 6 review.

7 (ii) Proposed rules required under subdivision
 8 (a)(18)(A) of this section that are under consideration at the time the act
 9 passes do not require review by the Highway Commission Review and Advisory
 10 Subcommittee of the Legislative Council prior to implementation but shall be
 11 submitted to the Highway Commission Review and Advisory Subcommittee of the
 12 Legislative Council by October 1, 2017 as a report.

13 (iii) The proposed rules required under subdivision
 14 (a)(18)(A) of this section are not required to be promulgated under the
 15 Arkansas Administrative Procedure Act, § 25-15-201 et seq., but shall be
 16 published after review by the Highway Commission Review and Advisory
 17 Subcommittee of the Legislative Council; and

18 (19) To provide the Highway Commission Review and Advisory
 19 Subcommittee of the Legislative Council with a report on the progress of each
 20 public road construction project of ten million dollars (\$10,000,000) or more
 21 at least quarterly or as required by the Highway Commission Review and
 22 Advisory Subcommittee of the Legislative Council.

23
 24 SECTION 20. Arkansas Code § 27-65-107, concerning the powers and
 25 duties of the State Highway Commission, is amended to add an additional
 26 subsection to read as follows:

27 (d) As used in this section:

28 (1) "Highway construction contract" means a contract for the
 29 construction, restoration, reconstruction, renovation, or repair of a road,
 30 highway, bridge, overpass, interchange, right-of-way, or turnpike that is
 31 part of the state highway system; and

32 (2) "Public road construction project" means the construction,
 33 restoration, reconstruction, renovation, or repair of a road, highway,
 34 street, bridge, overpass, interchange, or right-of-way in which the
 35 construction, restoration, reconstruction, renovation, or repair is to be
 36 performed or is initiated by the Arkansas State Highway and Transportation

1 Department or the commission.

2
3 SECTION 21. TEMPORARY LANGUAGE. DO NOT CODIFY.

4 (a) The Chief Fiscal Officer of the State shall make a one-time
5 transfer on his or her books and those of the Treasurer of State and the
6 Auditor of State the sum of forty million dollars (\$40,000,000) from the
7 funds available in the Rainy Day Set-Aside of the 90th Session Projects
8 Account of the General Improvement Fund as authorized by Acts 2015, No. 1147,
9 § 3(a)(11), to the Arkansas Highway Transfer Fund there to be used only for
10 the purposes set forth in § 19-6-832.

11 (b) Disbursement of funds authorized by this act shall be limited to
12 the appropriation for the agency and funds made available by law for the
13 support of the appropriations. The restrictions of the Arkansas Procurement
14 Law, § 19-11-201 et seq., the General Accounting and Budgetary Procedures
15 Law, § 19-4-101 et seq., the Revenue Stabilization Law, § 19-5-101 et seq.,
16 the Regular Salary Procedures and Restrictions Act, § 21-5-101 et seq., and
17 other fiscal control laws of this state, where applicable, and regulations
18 promulgated by the Department of Finance and Administration, as authorized by
19 law, shall be strictly complied with in disbursement of the funds.

20 (c) It is the intent of the General Assembly that any funds disbursed
21 under the authority of this act shall be in compliance with the stated
22 reasons for which this act was adopted, as evidenced by the Agency Requests,
23 Executive Recommendations, and Legislative Recommendations contained in the
24 budget manuals prepared by the Department of Finance and Administration,
25 letters, or summarized oral testimony in the official minutes of the
26 Legislative Council or Joint Budget Committee which relate to its passage and
27 adoption.

28
29 SECTION 22. EFFECTIVE DATE. Sections 9-12, 14, 16 and 17 of this act
30 are effective on and after July 1, 2017.

31
32 SECTION 23. EMERGENCY CLAUSE. It is found and determined by the
33 General Assembly of the State of Arkansas that Arkansas bridges and roads are
34 in need of repair and proper maintenance; that the repair and proper
35 maintenance of Arkansas bridges and roads are necessary for the preservation
36 of the public peace, health, and safety; that increased funding is essential

1 to the repair and proper maintenance of Arkansas bridges and roads; that this
2 act is designed to provide the necessary funding that is essential to the
3 repair and proper maintenance of Arkansas bridges and roads, and this act is
4 necessary because without this increased funding, the repair and proper
5 maintenance of Arkansas bridges and roads may not be performed. Therefore, an
6 emergency is declared to exist, and Sections 1-8, 13, 15, 18-21 of this act
7 being immediately necessary for the preservation of the public peace, health,
8 and safety shall become effective on July 1, 2016.

9
10
11 **APPROVED: 05/23/2016**
12
13
14
15
16
17
18
19
20
21
22
23
24
25
26
27
28
29
30
31
32
33
34
35
36



www.ARDOT.gov
